Pictorial Programme

LSE St Clement's Building Re-Stack

LS006/J4/April 2015

Rev: J

LSE

BISSET ADAMS

Step 1 - Sixth Floor - Refurbishment

15th January - 20th March 2015

Create 5 new offices on the 6th floor. This will involve new partitions, ceilings, floor finishes, power and data, lighting and acoustic treatment to the flank wall

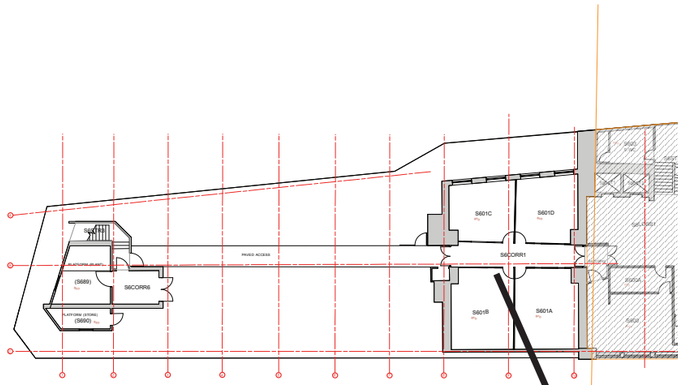

Existing Sixth Floor

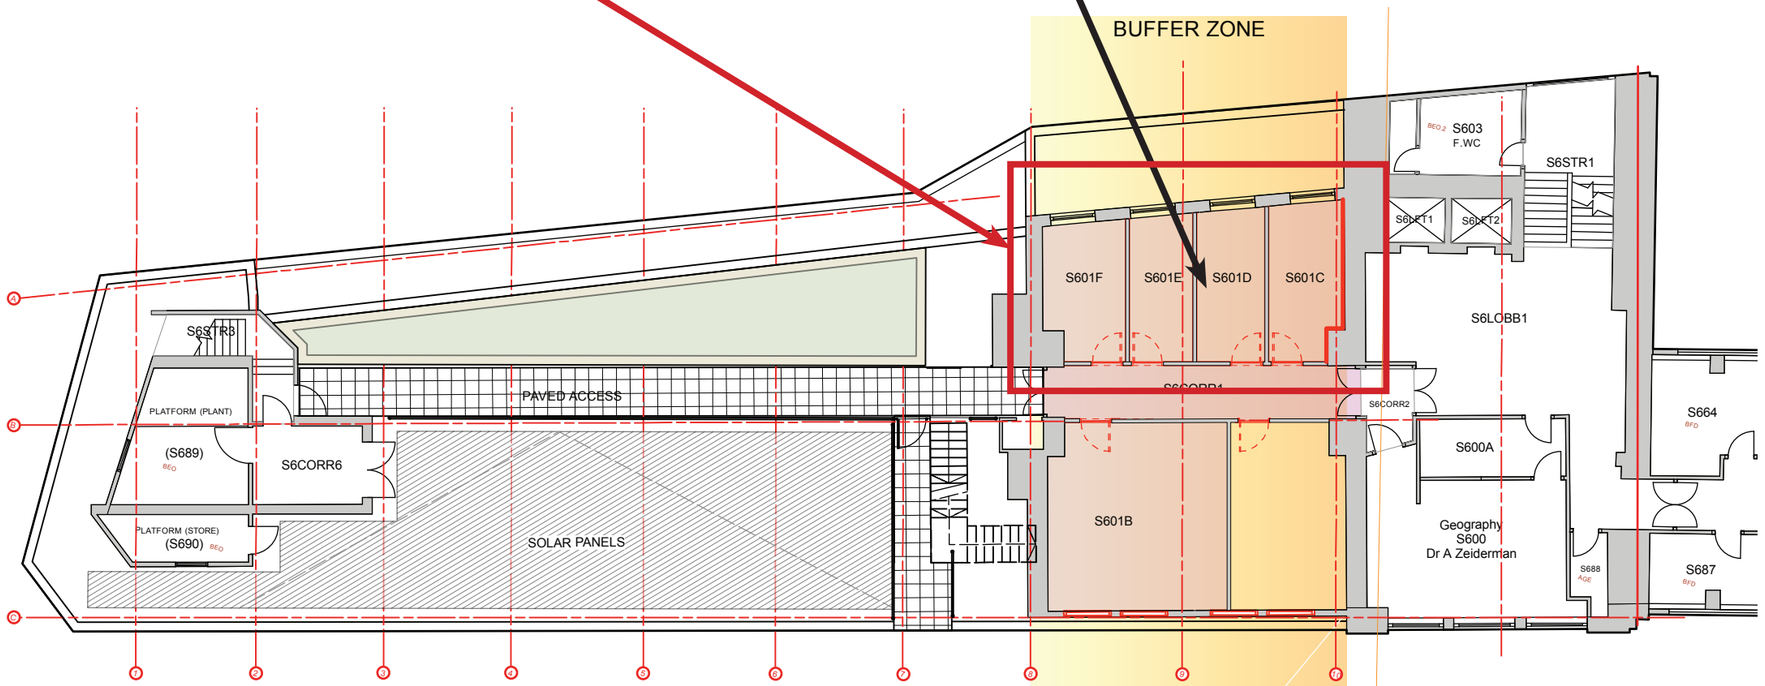

Proposed Sixth Floor

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works



Step 2 - Third Floor - Vacate

27th March - 30th March 2015

Move main area of 3rd floor Social Psychology of the west wing out into new accommodation on Level 3 of Queens House.

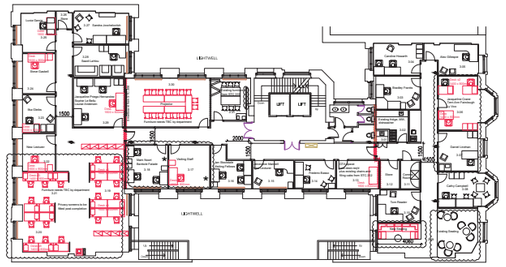

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

BUFFER ZONE

Social Psychology S311
Social Psychology S310
Social Psychology S308
Social Psychology S307
Social Psychology S306
Social Psychology S305a
Social Psychology S305
Social Psychology S304
Social Psychology S303
Social Psychology S302
Social Psychology S317
STORE (S302C)
MSC Research Laboratory
Social Psychology S318
MSC Research Laboratory
Social Psychology S319
Computer Room
M.WC S322
BEO.2
S3STR2
S3LFT2
S3LFT3
S3CORR4
S321 IMT
PRINT ROOM
Workshop Social Psychology S300
Social Psychology S316
Social Psychology S315
Social Psychology S314
Social Psychology S313
Social Psych-ology S312
S3STR1
S3LFT1
S3CORR1
(S311A)
DISABLED REFUGE
S3CORR3
(S302B)
S302A
KITCHEN
Social Psychology
AV Suite
MSC Computer Study Suite S301

Existing Third Floor



Step 3 - Sixth Floor - Move

17th March - 20th April 2015

Move Geography from the 4th and 5th floors into the new created 6th floor offices.
Rm S412 to S601c (Ryan Centner - Geography)
Rm S600 to S601d (Austin Zeiderman - Geography)
Rm S402 to S601e (Neil Lee - Geography)
Rm S416 to S601F (Hyun Shin - Geography)

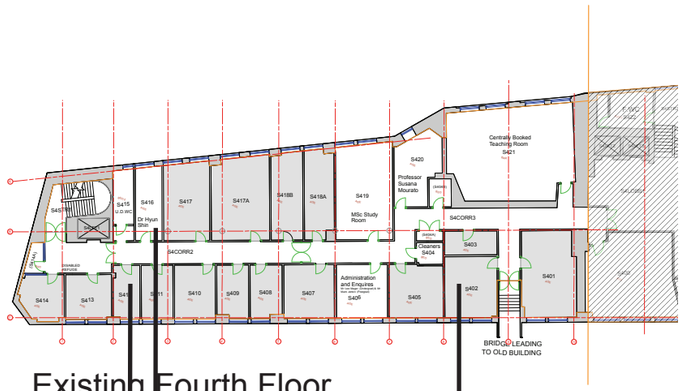

Existing Fourth Floor

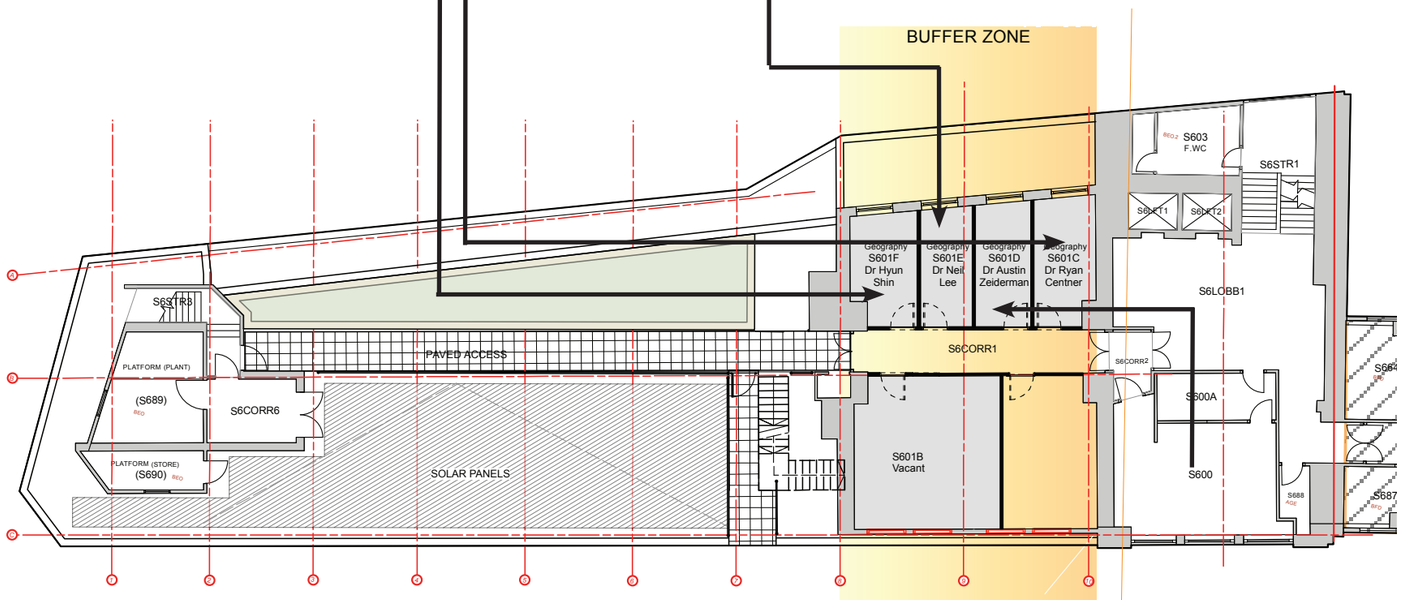

Proposed Sixth Floor

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works



Step 4 - Basement, Ground and First Floor - Vacate

24th April - 27th April 2015

Move IMT located on Basement, Ground and First Floors within west wing and central core into new accommodation on Level 3 of Aldwych House. Also, utilise S53 as a temporary IMT workshop until 25th May 2015.

S05 and S05a is currently an Estates Store and for R&I Contractor. This will be lost from 24th April 2015.

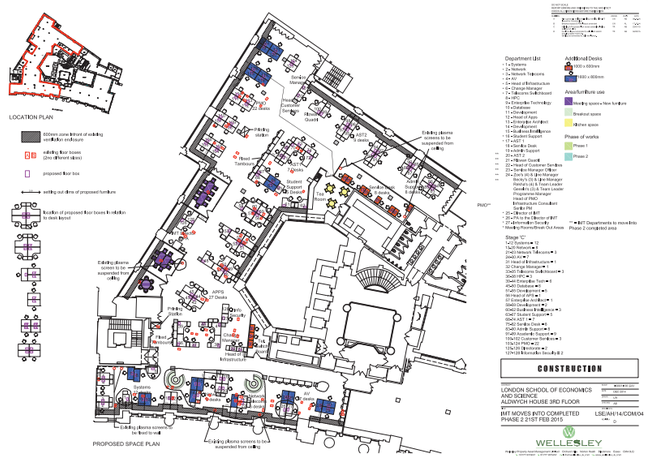

Aldwych House, Level 3.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

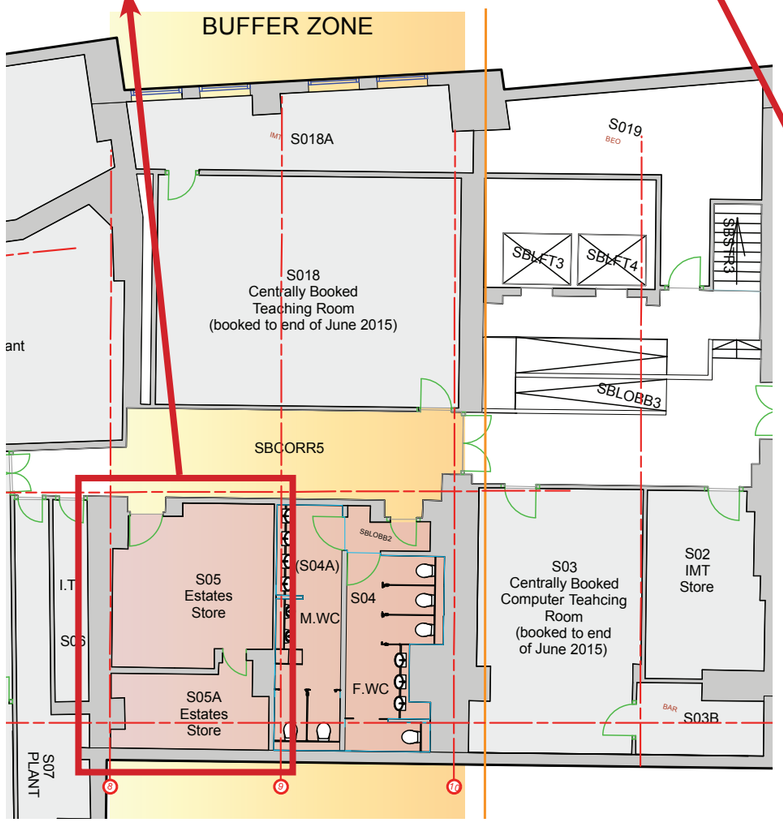

Existing Basement Floor

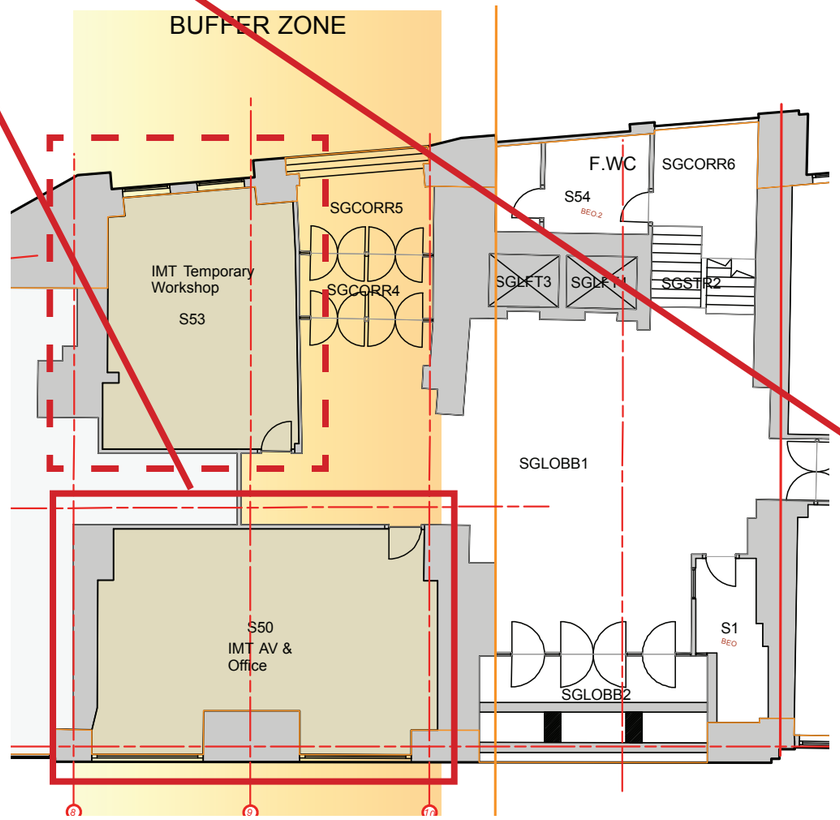

Existing Ground Floor

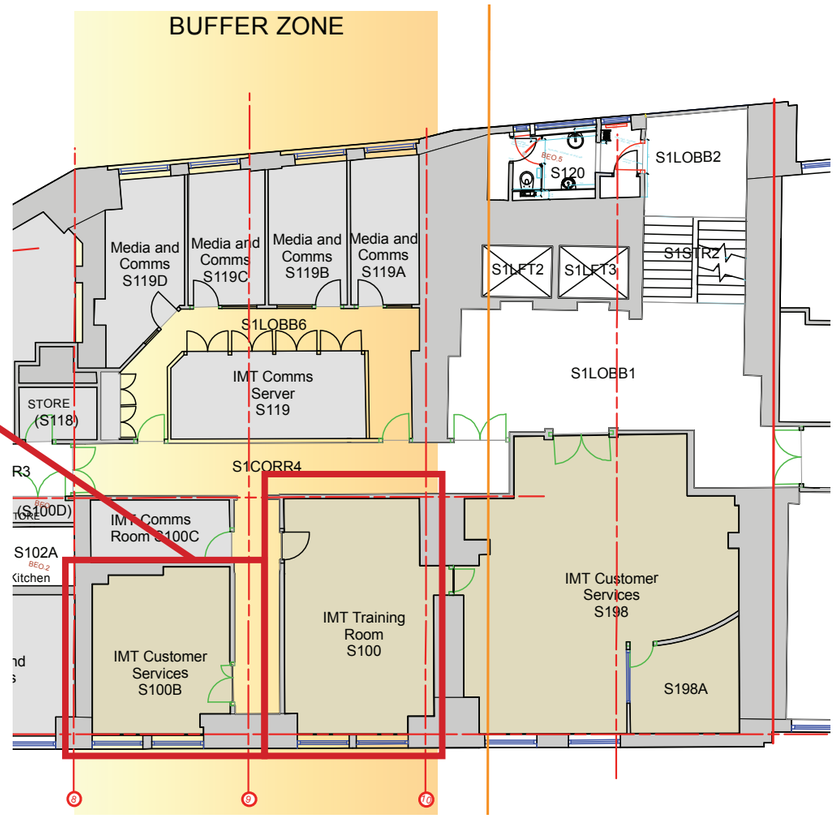

Existing First Floor



Step 5 - Third Floor - Vacate

By 17th May 2015

Move 3rd floor Social Psychology from the proposed 'buffer zone' of west wing out into new accommodation on Fourth Floor of Tower 2.

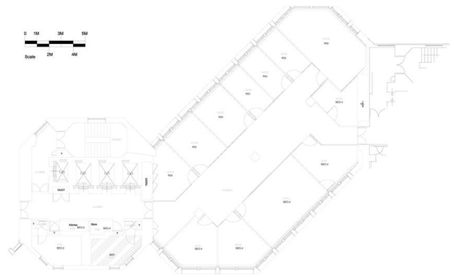

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

BUFFER ZONE

Social Psychology S311
Social Psychology S310
Social Psychology S308
Social Psychology S307
Social Psychology S306
Social Psychology S305a
Social Psychology S305
Social Psychology S304
Social Psychology S303
Social Psychology S302
Social Psychology S317
STORE (S302C)
MSC Research Laboratory
Social Psychology S318
MSC Research Laboratory
Social Psychology S319
Computer Room
Social Psych-ology S312
Social Psychology S313
Social Psychology S314
Social Psychology S315
Social Psychology S316
S3STR1
S3LFT1
S3CORR1
(S311A)
DISABLED REFUGE
(S302)
S302A
KITCHEN
S3CORR3
Social Psychology
MSC Computer Study Suite S301
AV Suite
M.WC S322
BEO.2
S3STR2
S3LFT2
S3LFT3
S3CORR4
S321 IMT
PRINT ROOM
Workshop Social Psychology S300

Existing Third Floor

January 2015	February 2015	March 2015	April 2015	May 2015	June 2015	July 2015	August 2015	September 2015	October 2015	November 2015
12th 19th 26th	2nd 9th 16th 23rd	2nd 9th 16th 23rd 30th	6th 13th 20th 27th	4th 11th 18th 25th	1st 8th 15th 22nd 29th	6th 13th 20th 27th	3rd 10th 17th 24th 31st	7th 14th 21st 28th	5th 12th 19th 26th	2nd 9th 16th 23rd 30th

Step 6 - Basement Floor - Refurbishment

11th May - 30th June 2015

Carry out works to decommission existing basement floor toilets to allow for new stair core to commence and new toilet provisions.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

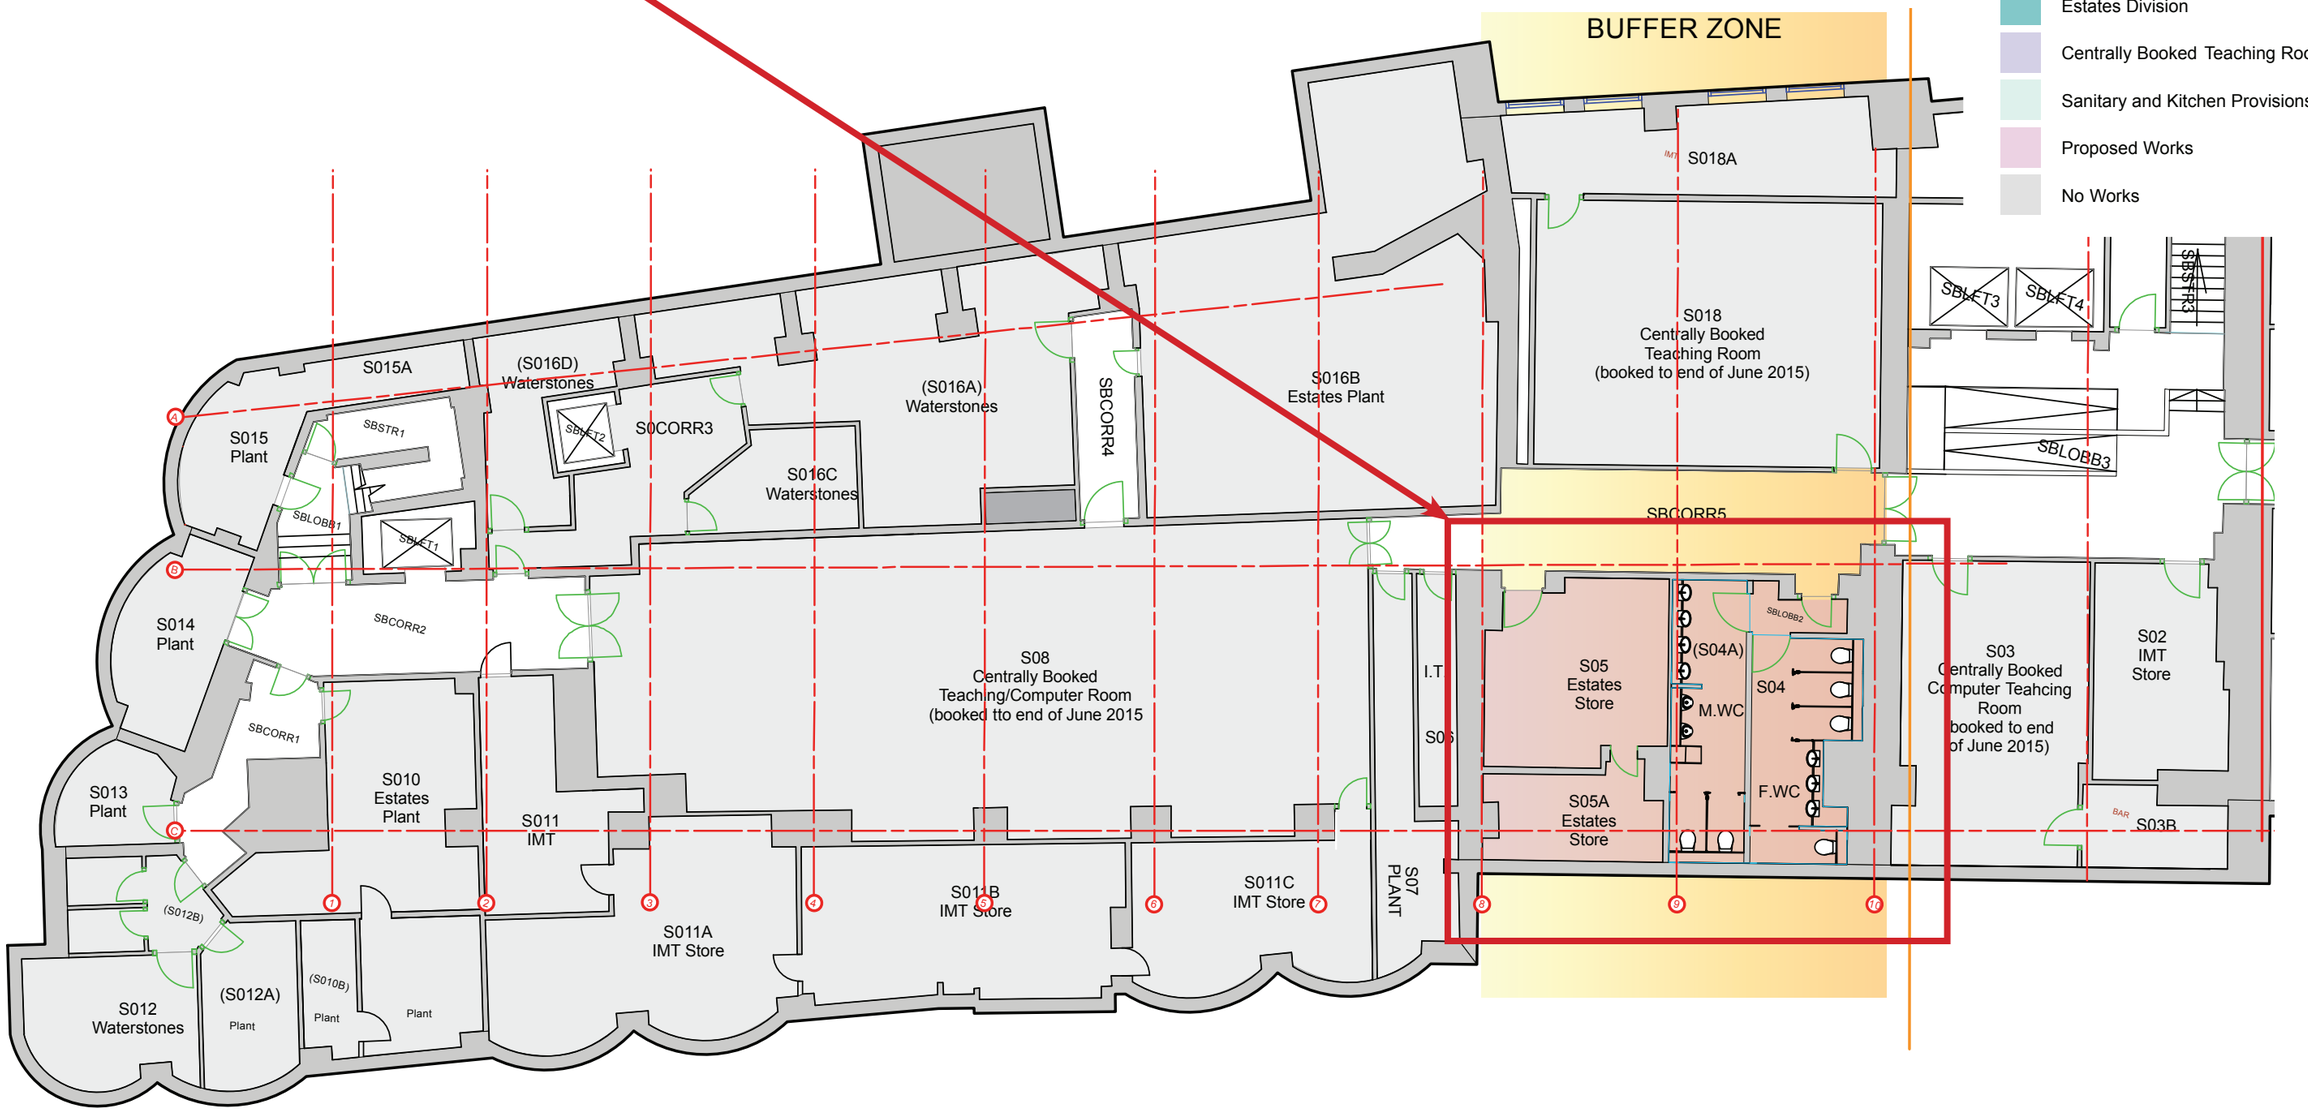

Existing Basement Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 7 - Basement, Ground and First Floor - Vacate

16th May- 22nd May 2015

S198 IMT Customer Services to move out into LRB
Laptop surgery by 22nd May 2015.

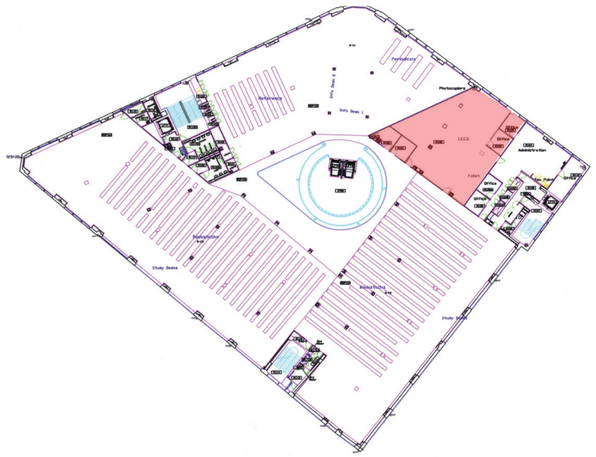

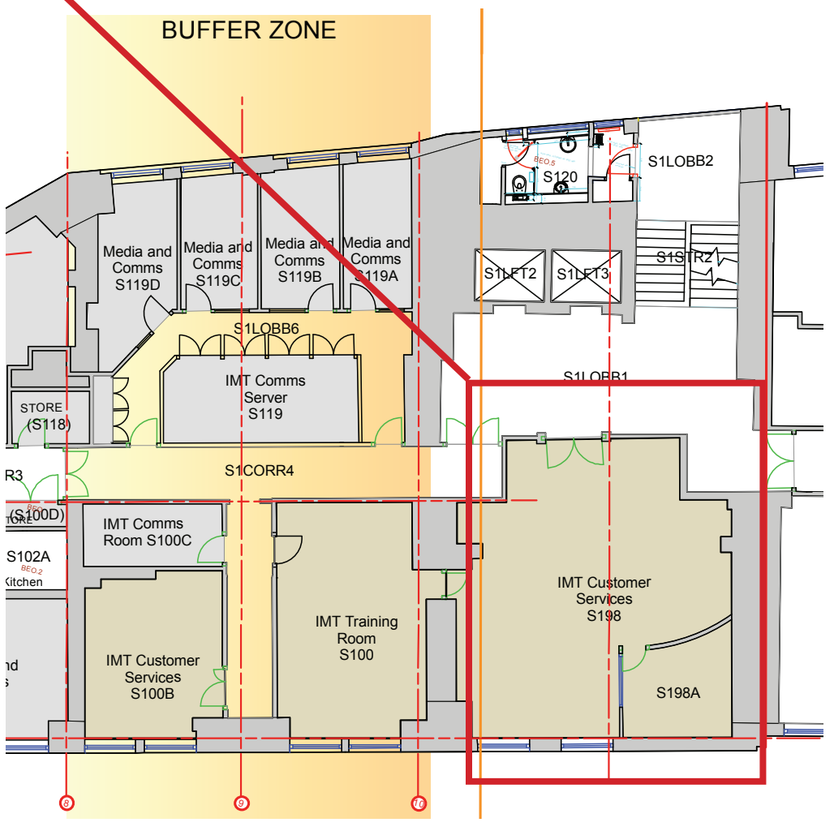

Existing First Floor

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 8 - Fifth Floor - Move

22nd May - 25th May 2015

Move Geography from the 5th floor into existing 4th floor offices.
Rm S507 to S412 (Laura Rozario - Geography)

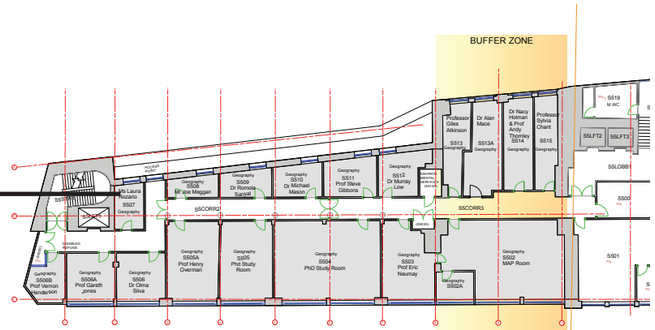

Existing Fifth Floor

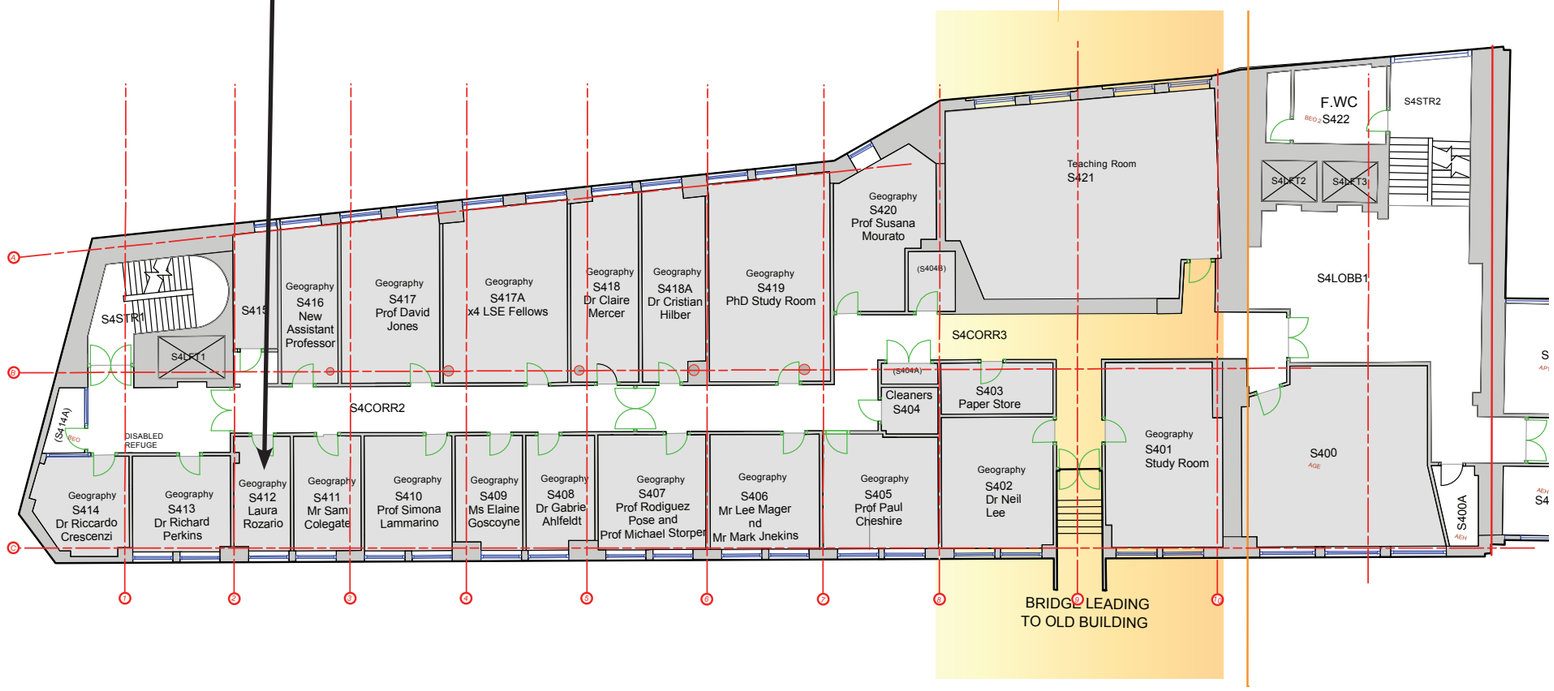

Existing Fourth Floor

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works



Step 9 - New Stair Core - Works

25th May - 19th June 2015

Form cut out for stair core from Basement to 1st floor within buffer zone.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

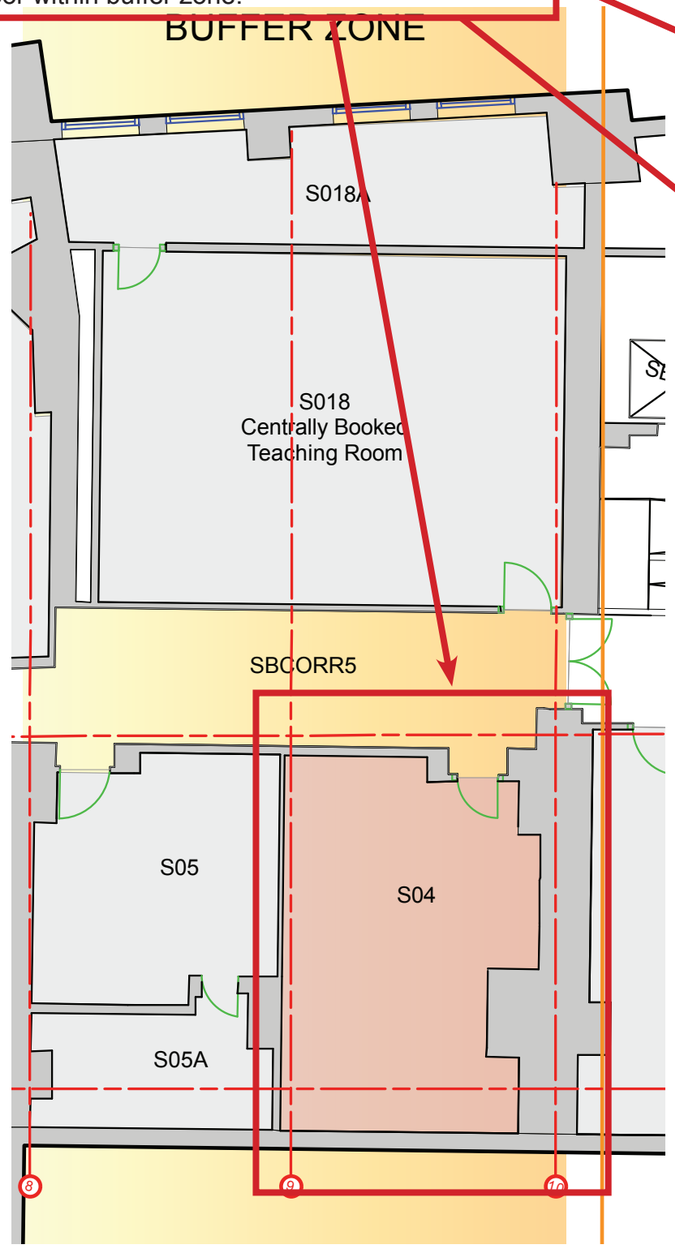

Existing Basement Floor

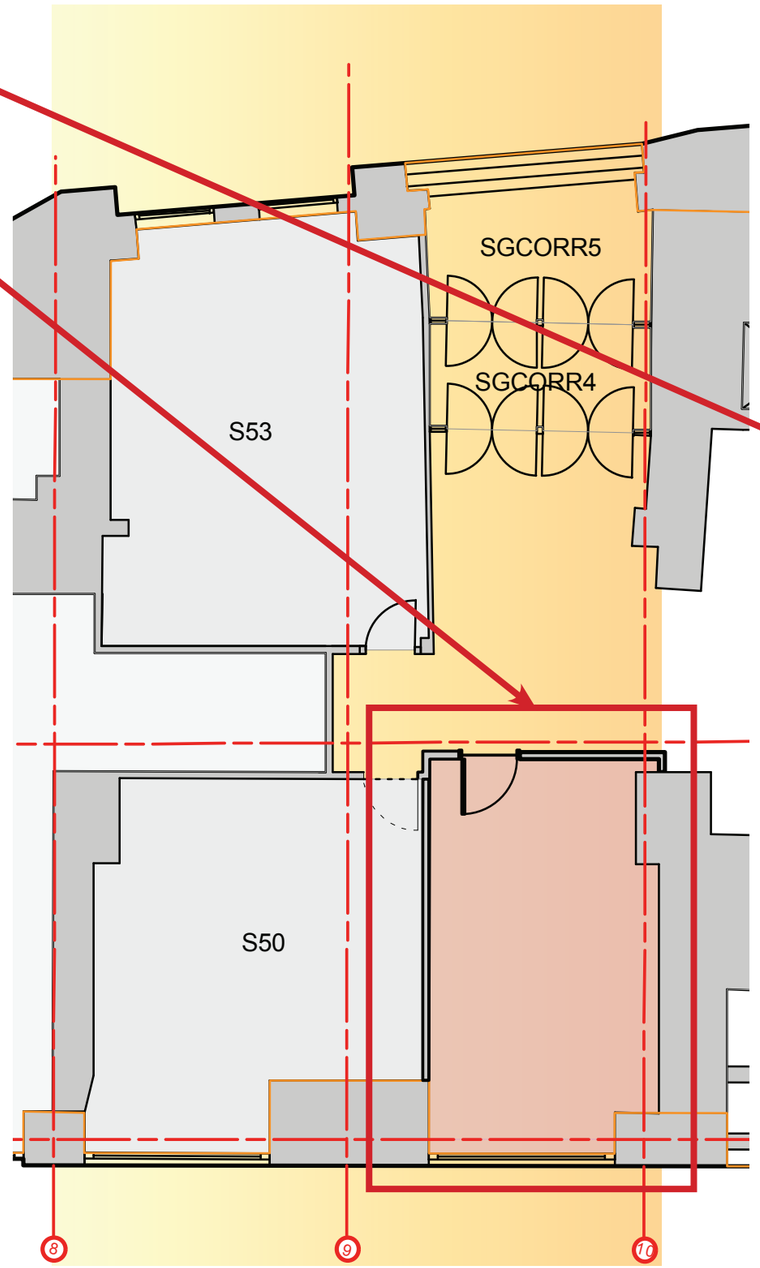

Existing Ground Floor

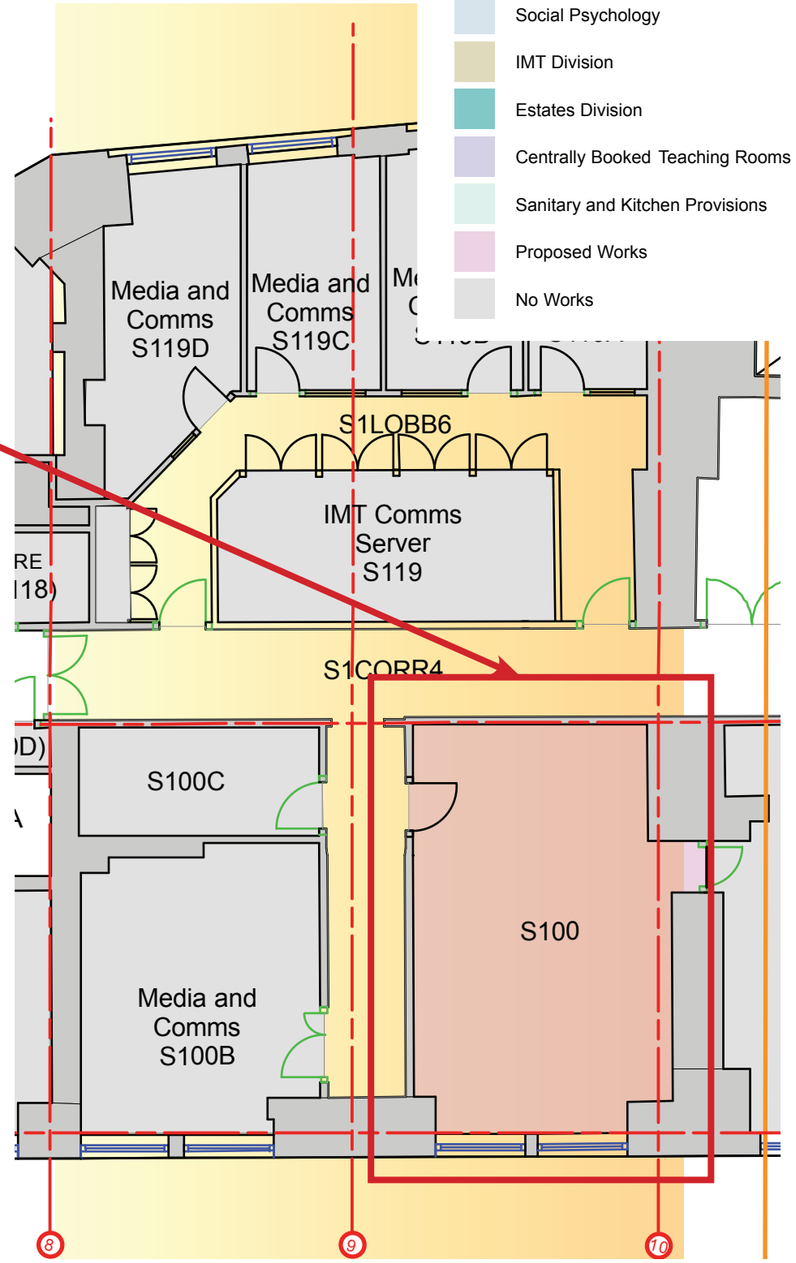

Existing First Floor



Step 10 - Ground Floor - Refurbishment

28th May - 26th June 2015

Carry out works to ground floor where occupants have moved out of the floor by 26th April 2015.
Rm S50 to be split into two - S50a is formed when staircore is opening is formed, leaving S50b.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

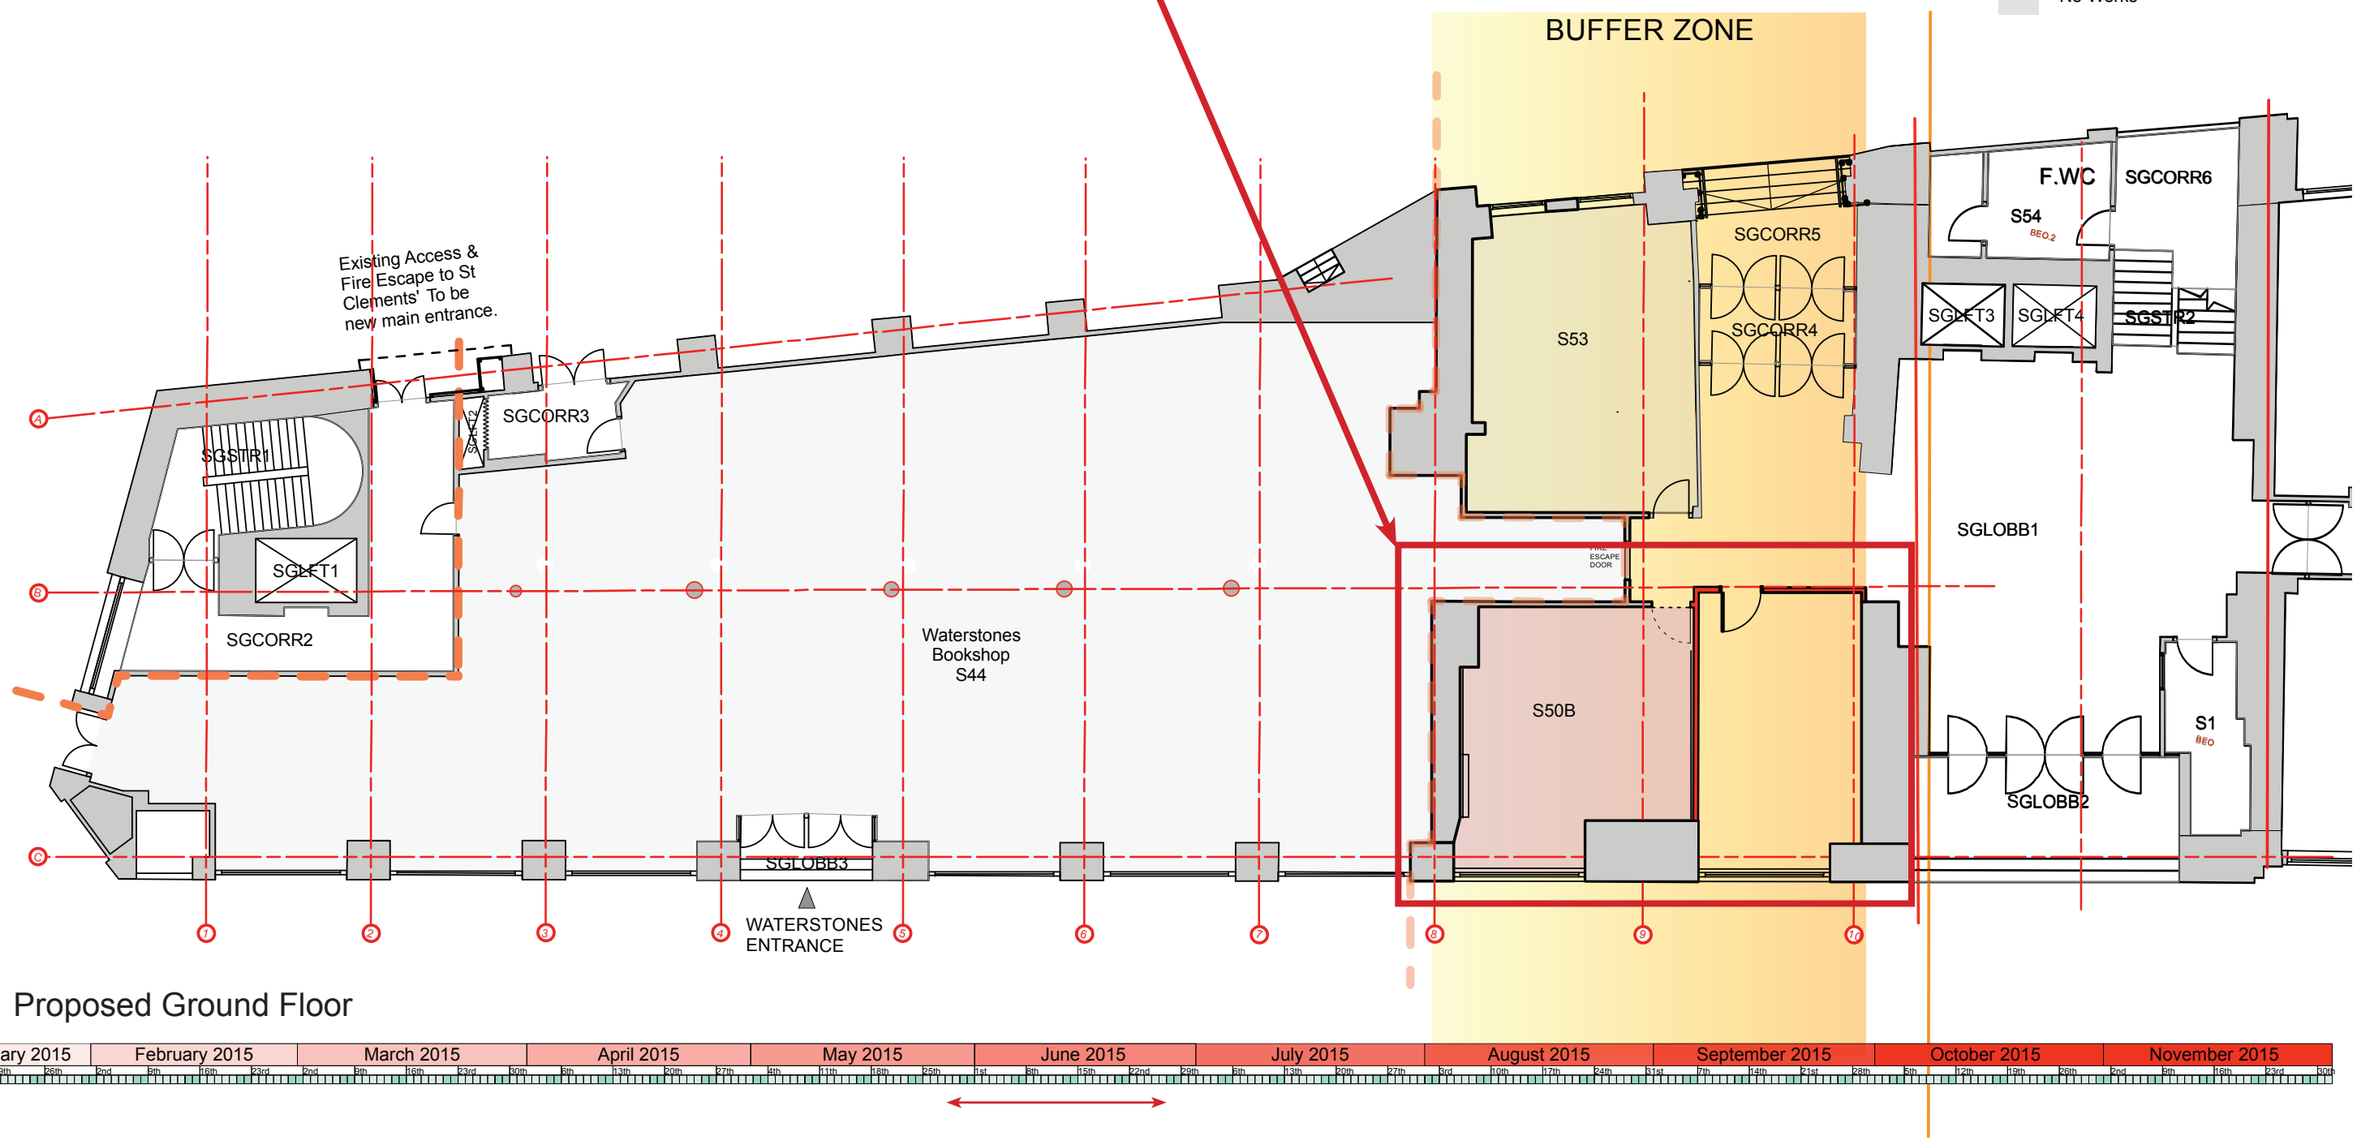

Proposed Ground Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 11 - Third Floor - Refurbishment

25th May - 26th June 2015

Carry out works to third floor where occupants have moved out of the floor by 27th March 2015.
Rm S318 to be split into two - S318a and S318b.
Rm S319 to be split into two - S319a and 319b.
Acoustic quilt lining to be applied to the flank wall of Rm 319b along the flank wall.
Relocate wall between Rm S314 and S315
Rm S315 to be split into two - S315a and S315b.
Rm S312 to be converted into a WC.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

BUFFER ZONE

S312 S313 S314 S315A S315B S316 S317 S318a S318b S319a S319b

S3STR1 S3LFT1 S3CORR1 S3CORR3 S3CORR4 S3STR2 S3LFT2 S3LFT3

M.WC S322 BEO.2

STORE (S302C)

(S302B) S302A BEO.1 KITCHEN

S321 PRINT ROOM

S300

(S311A) DISABLED REFUGE

S311 S310 S308 S307 S306 S305a S305 S304 S303 S302 S301

A B C

1 2 3 4 5 6 7 8 9 10

Proposed Third Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 12 - Fifth Floor - Refurbishment

25th May - 26th June 2015

Carry our works to 5th floor to form new toilets and kitchen-ette and acoustic doors to buffer zone.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

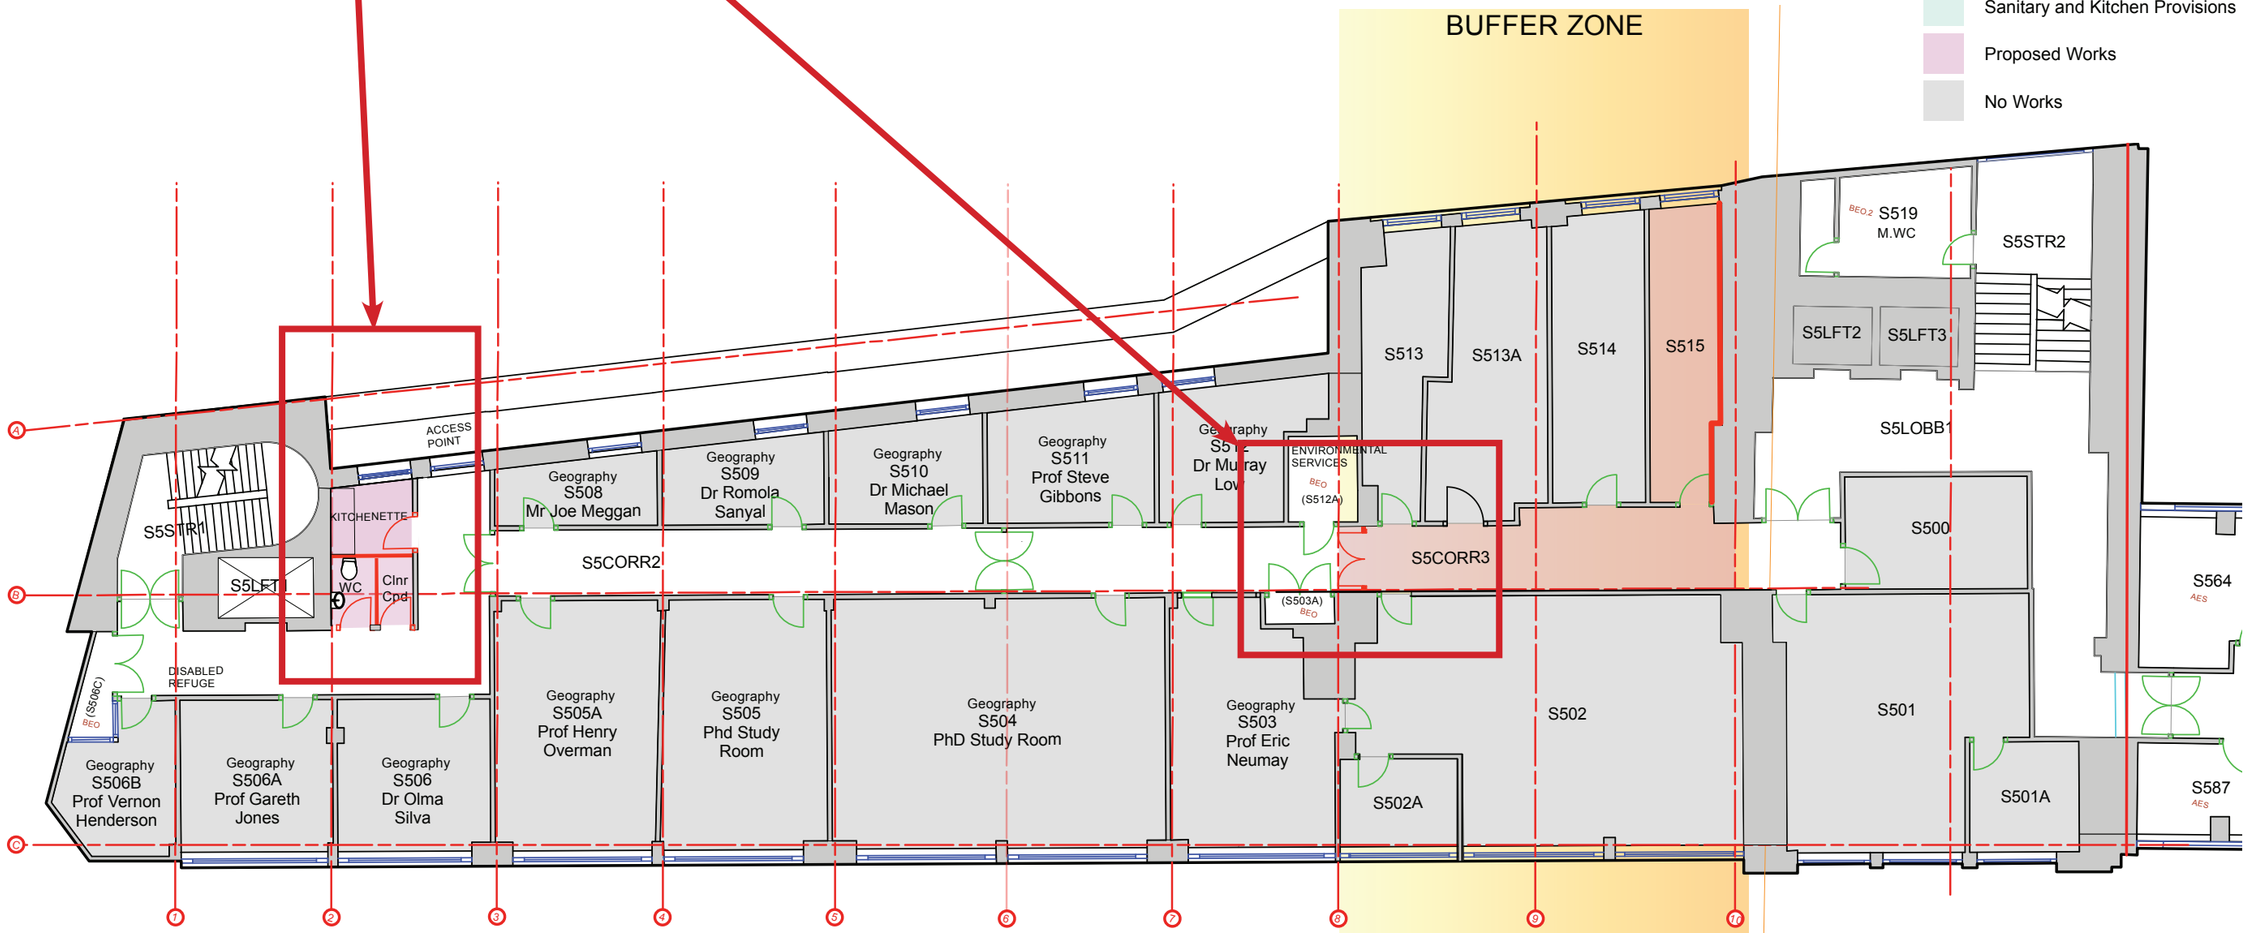

Proposed Fifth Floor



Step 13 - Second Floor - Refurbishment

1st June - 12th June 2015

Provide acoustic baffle to Flank wall of S221.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

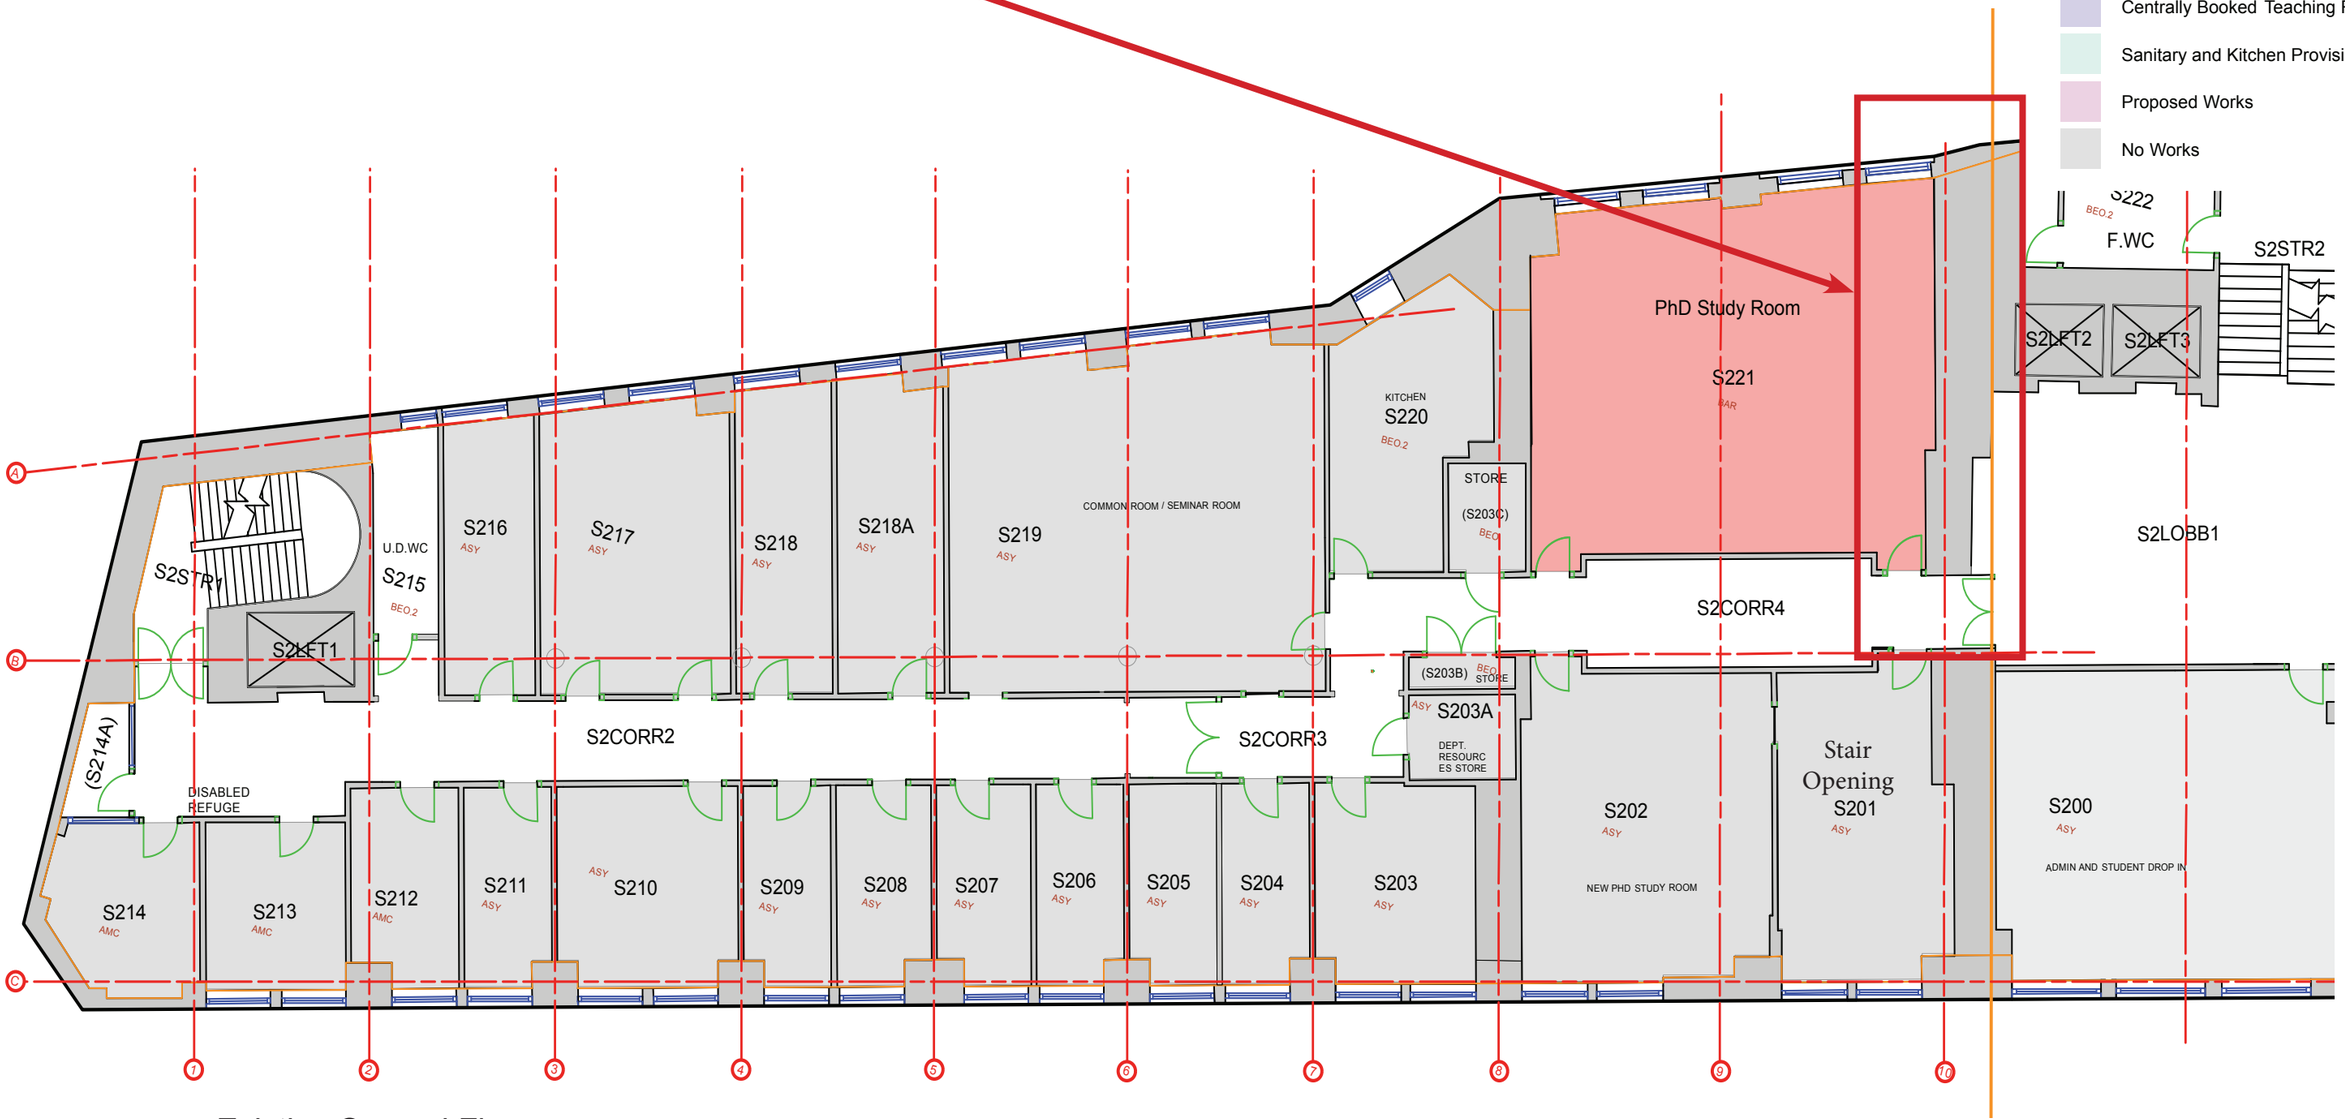

Existing Second Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 14 - Fourth Floor - Refurbishment

1st June - 26th June 2015

Provide acoustic baffle to Flank wall of S421 and create four offices within existing teaching space.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

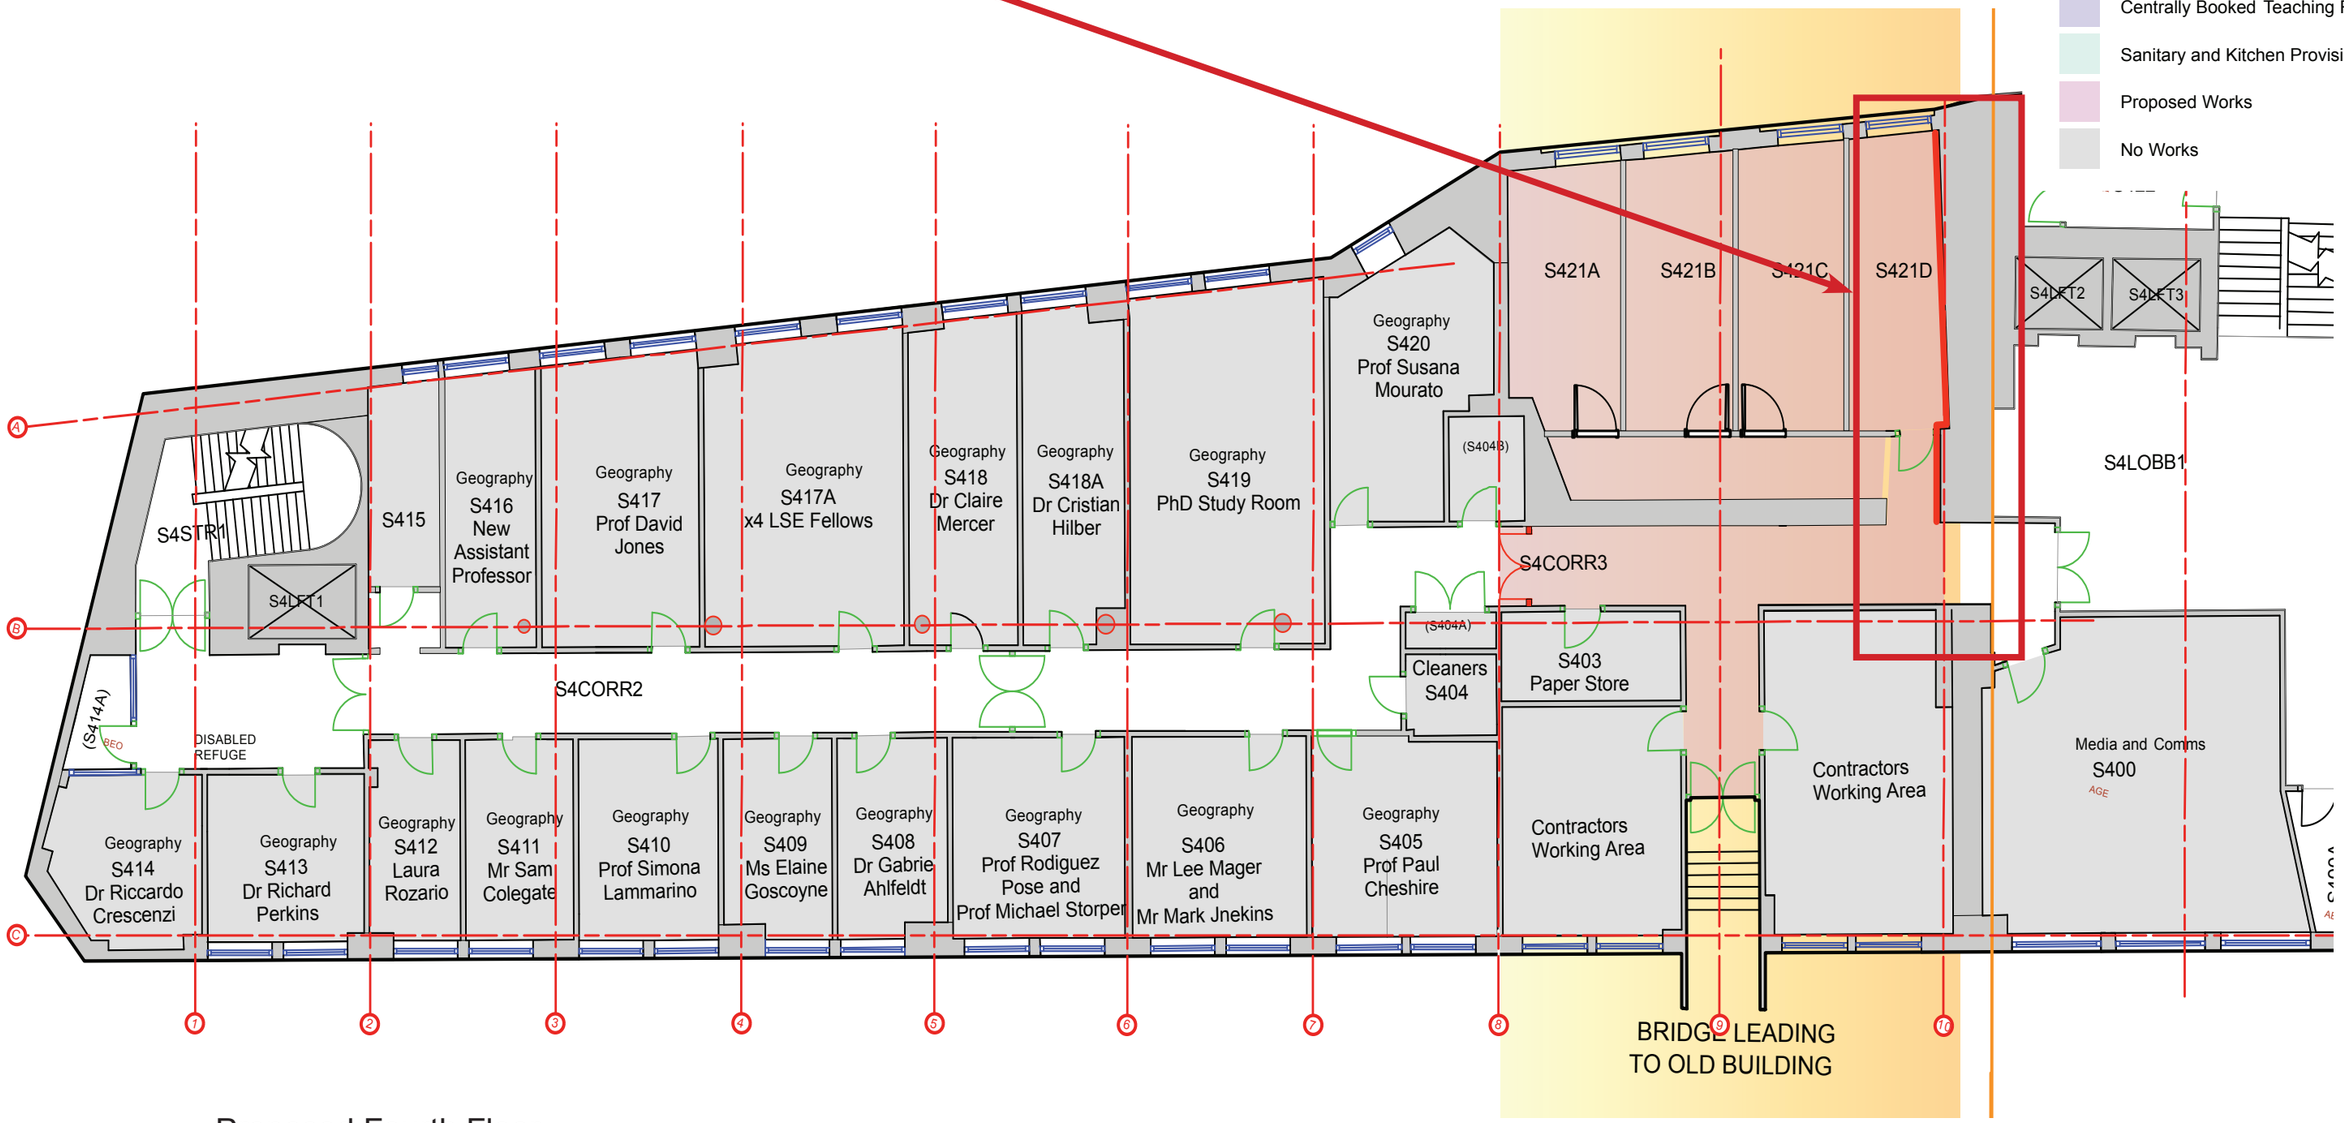

Proposed Fourth Floor



Step 15 - Second Floor - Move

5th June - 8th June 2015

Move Sociology PhD students of Rm S201 and S202 into S221.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

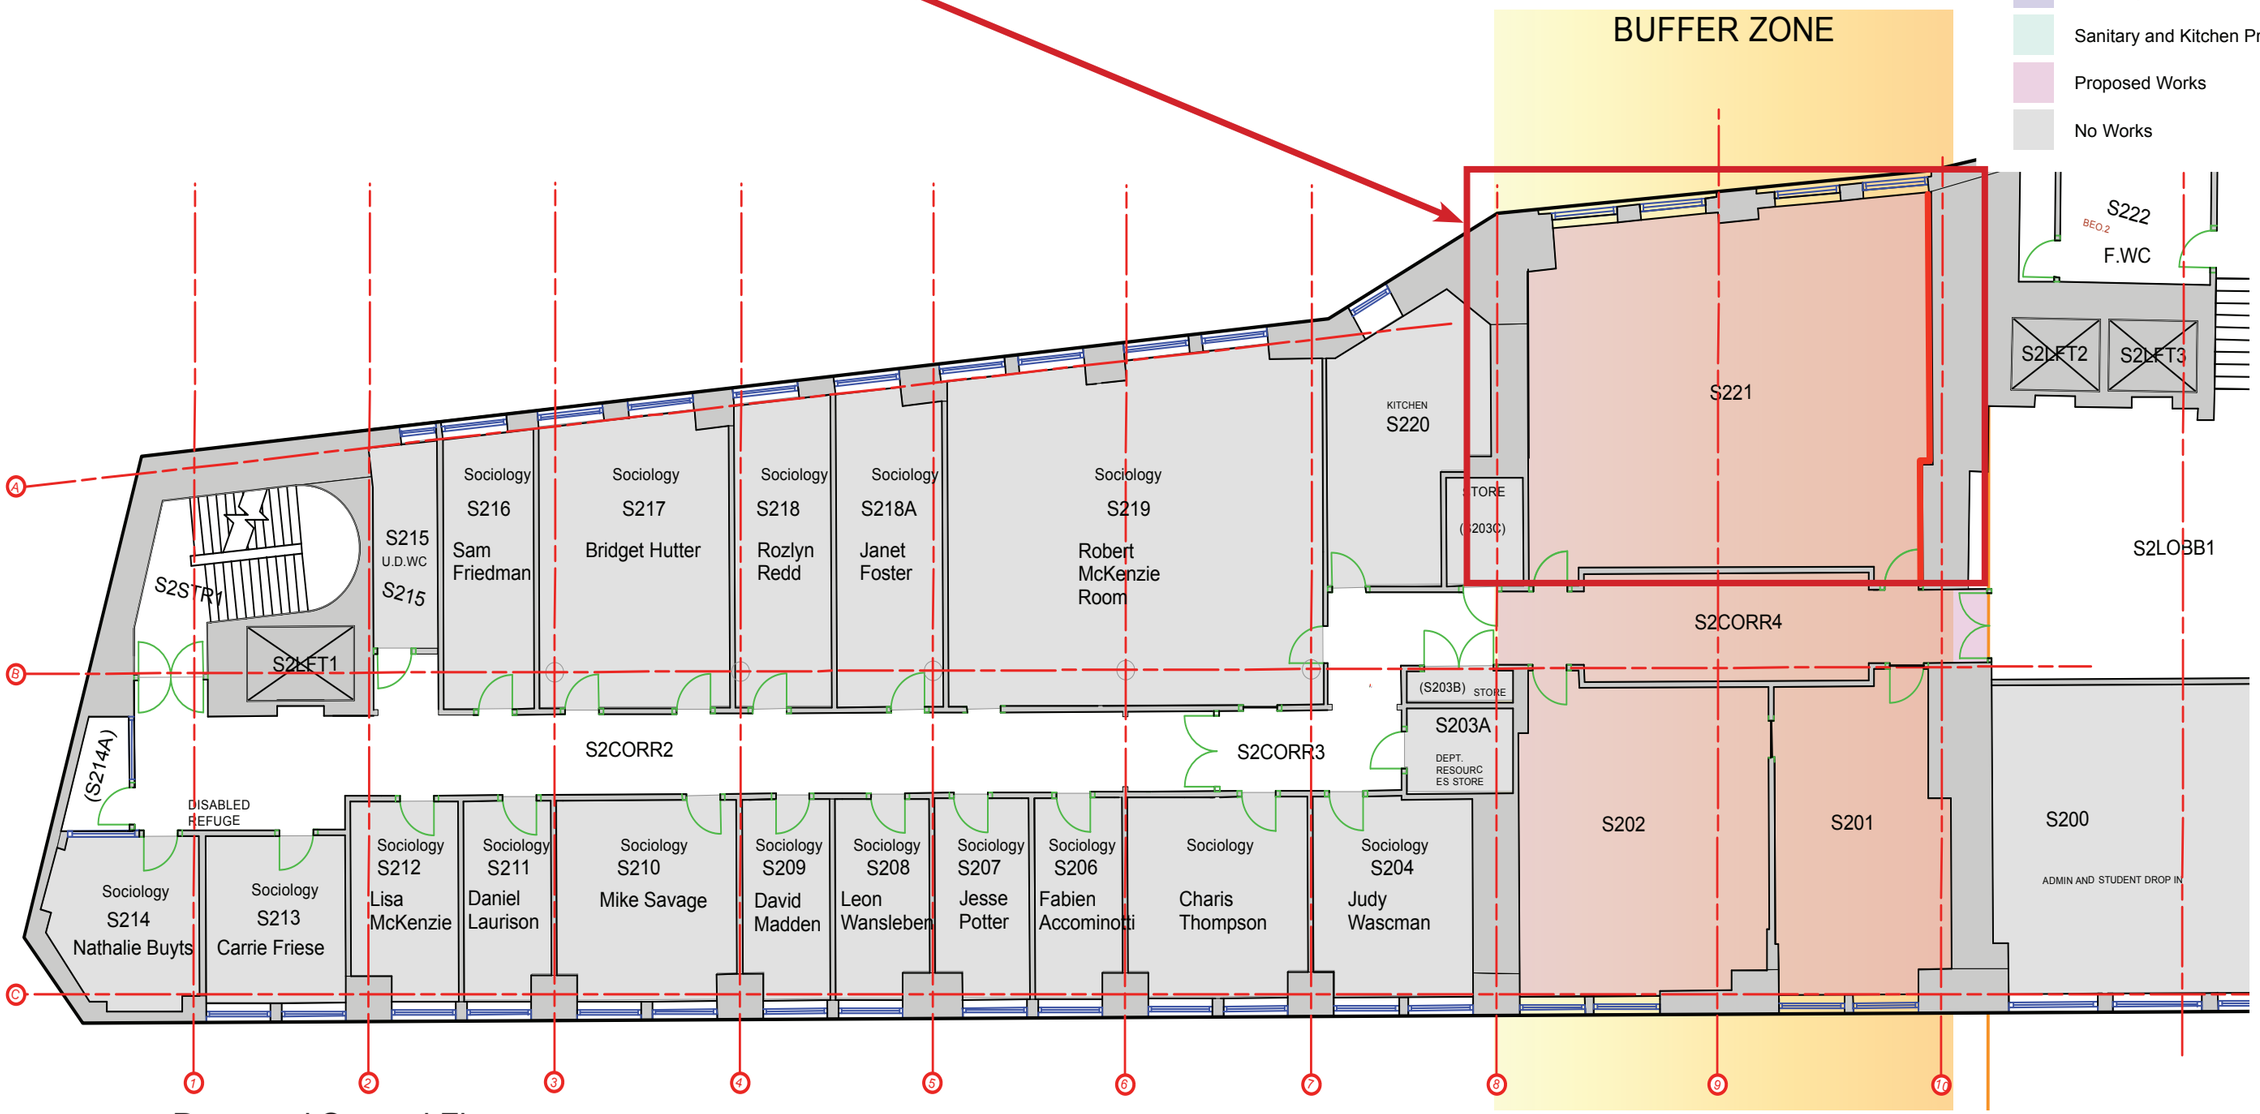

Proposed Second Floor



Step 16 - Third Floor - Vacate

By 15th June 2015

Move 3rd floor Social Psychology workshop into new location to be confirmed.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

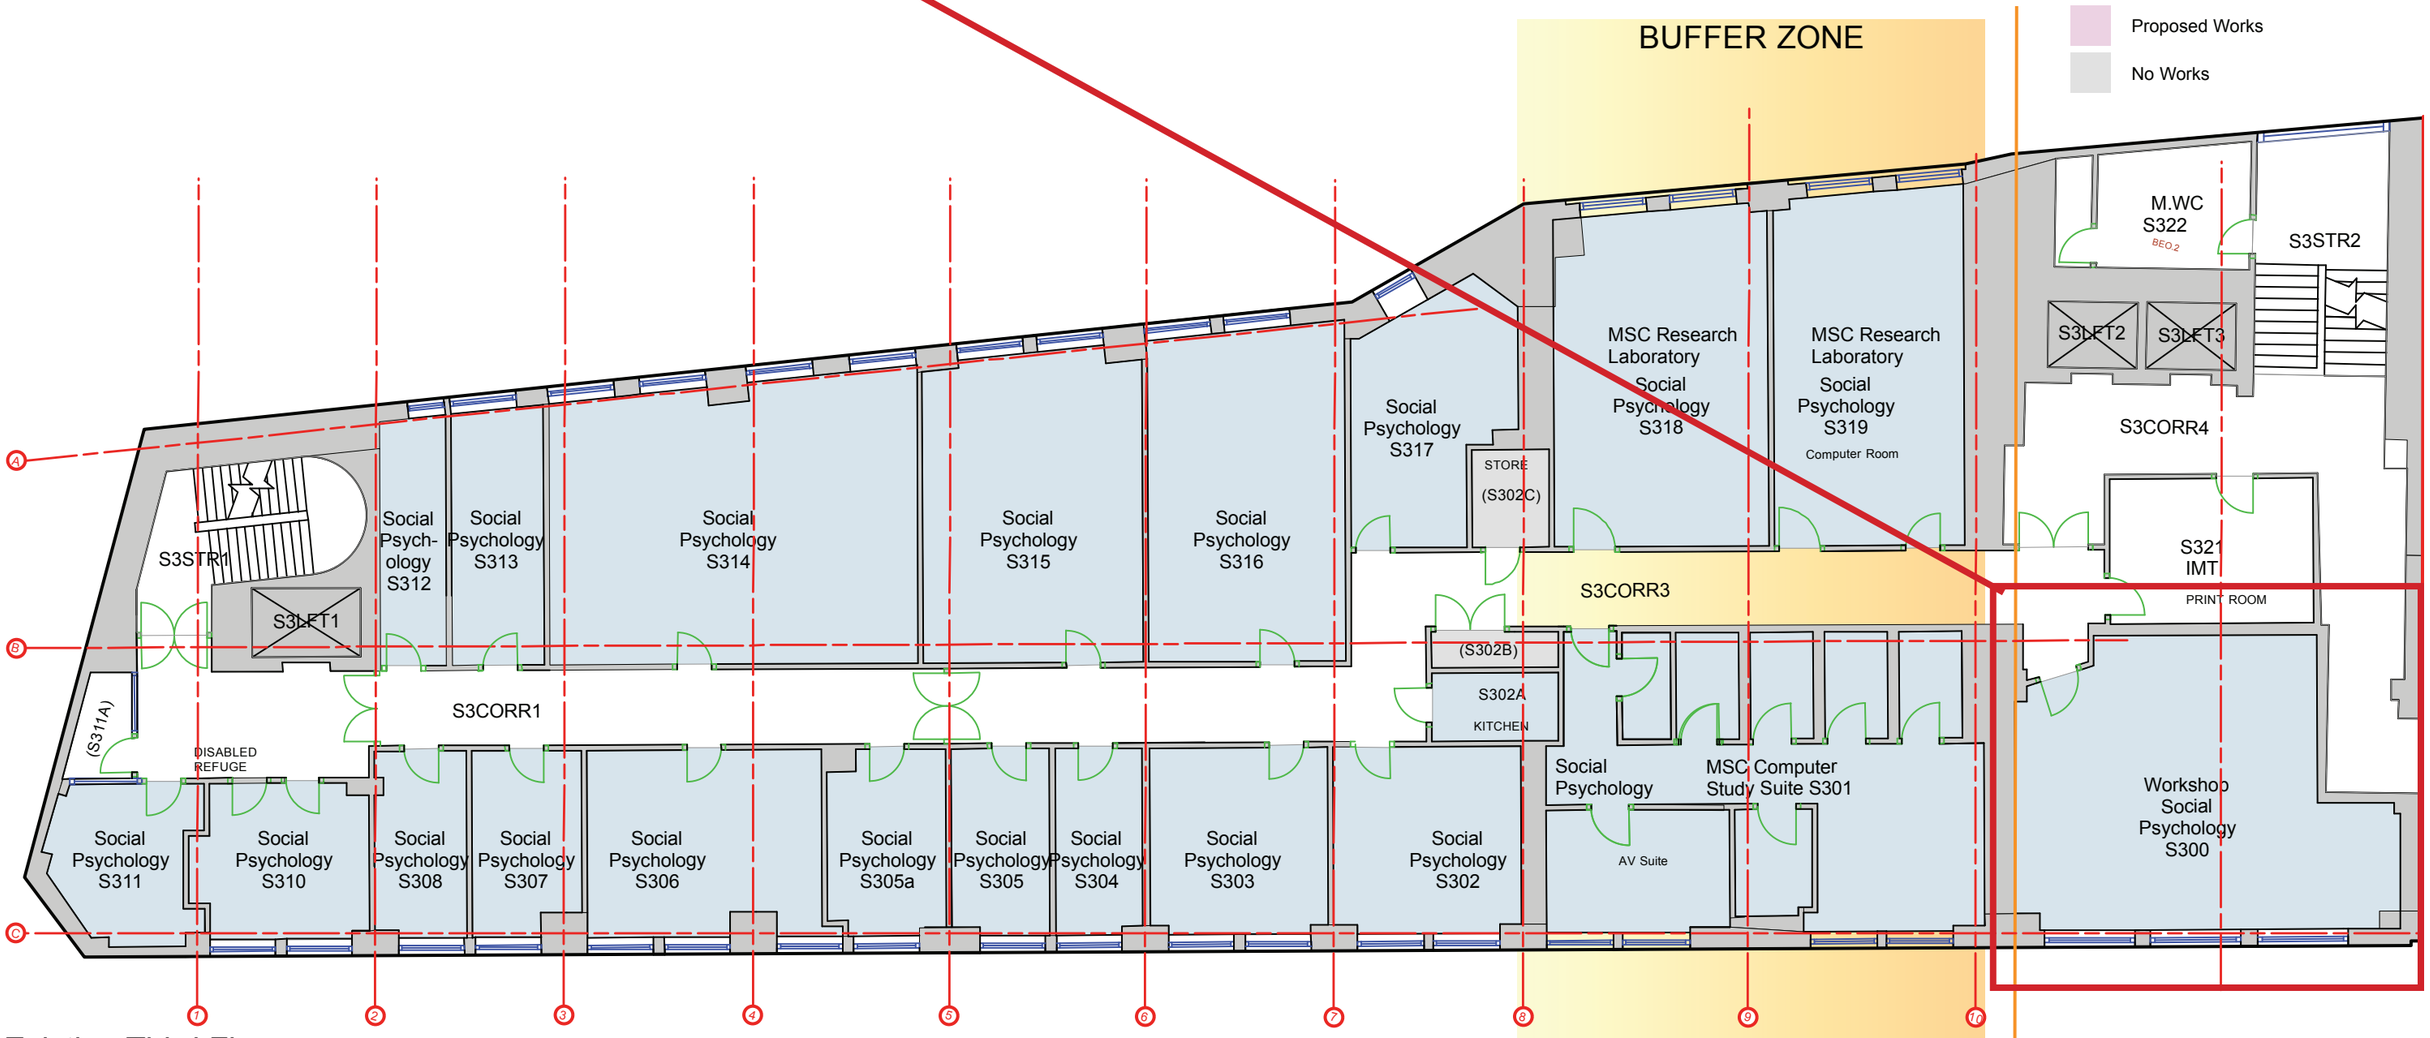

Existing Third Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 17 - New Stair Core - Works

22nd June - 10th July 2015

Form cut out for stair core from Basement to 2nd to 3rd floors within buffer zone.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

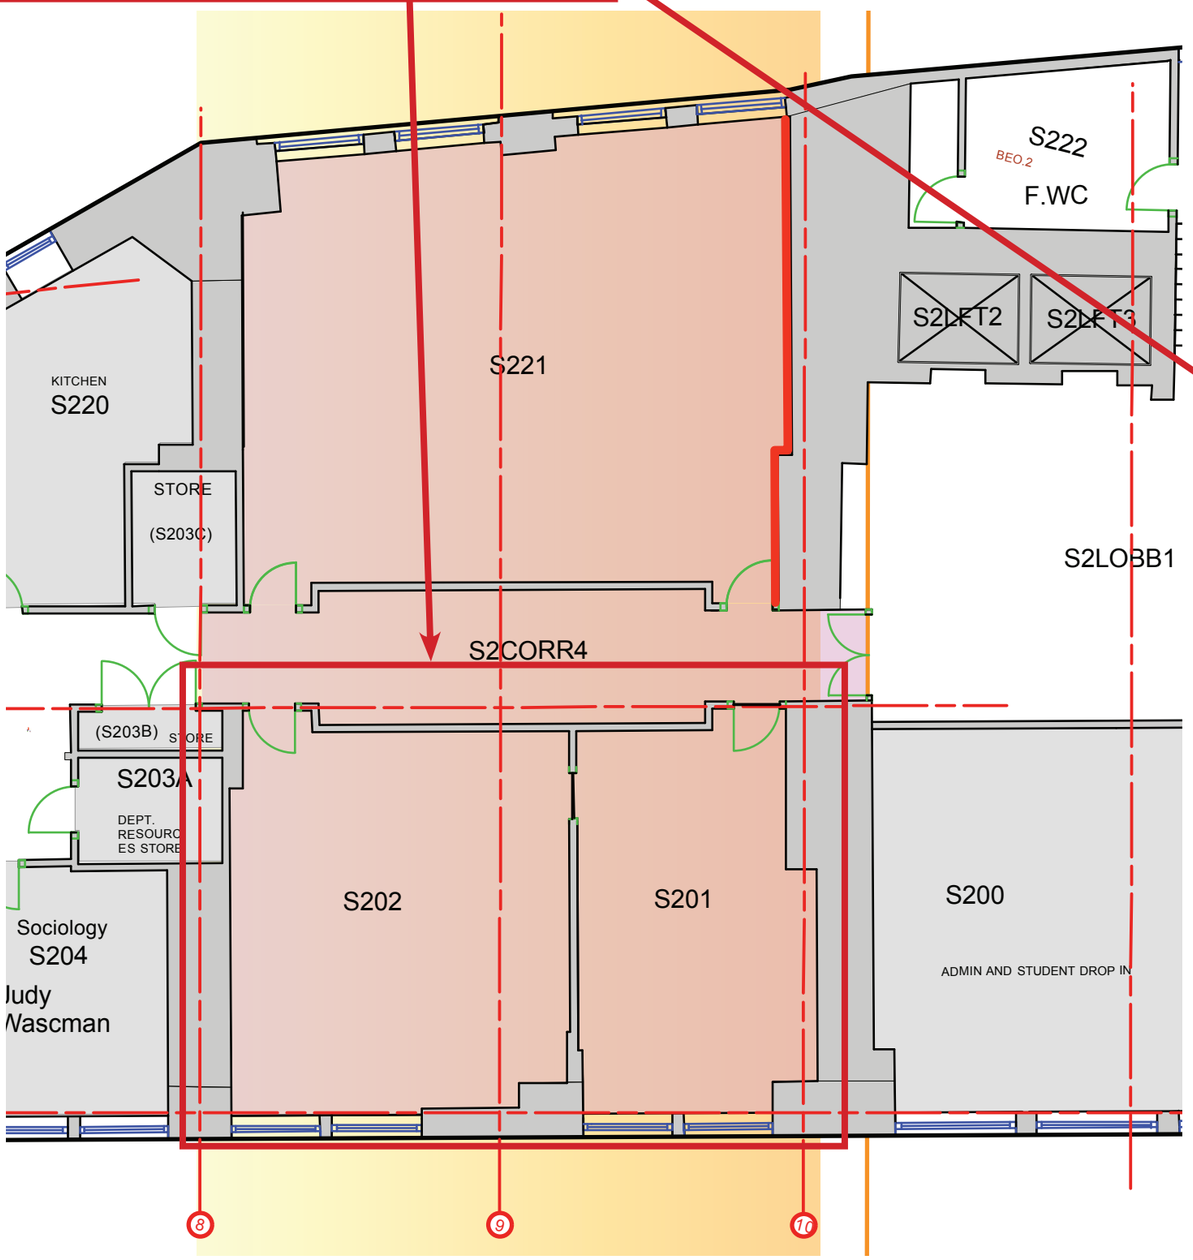

Existing Second Floor

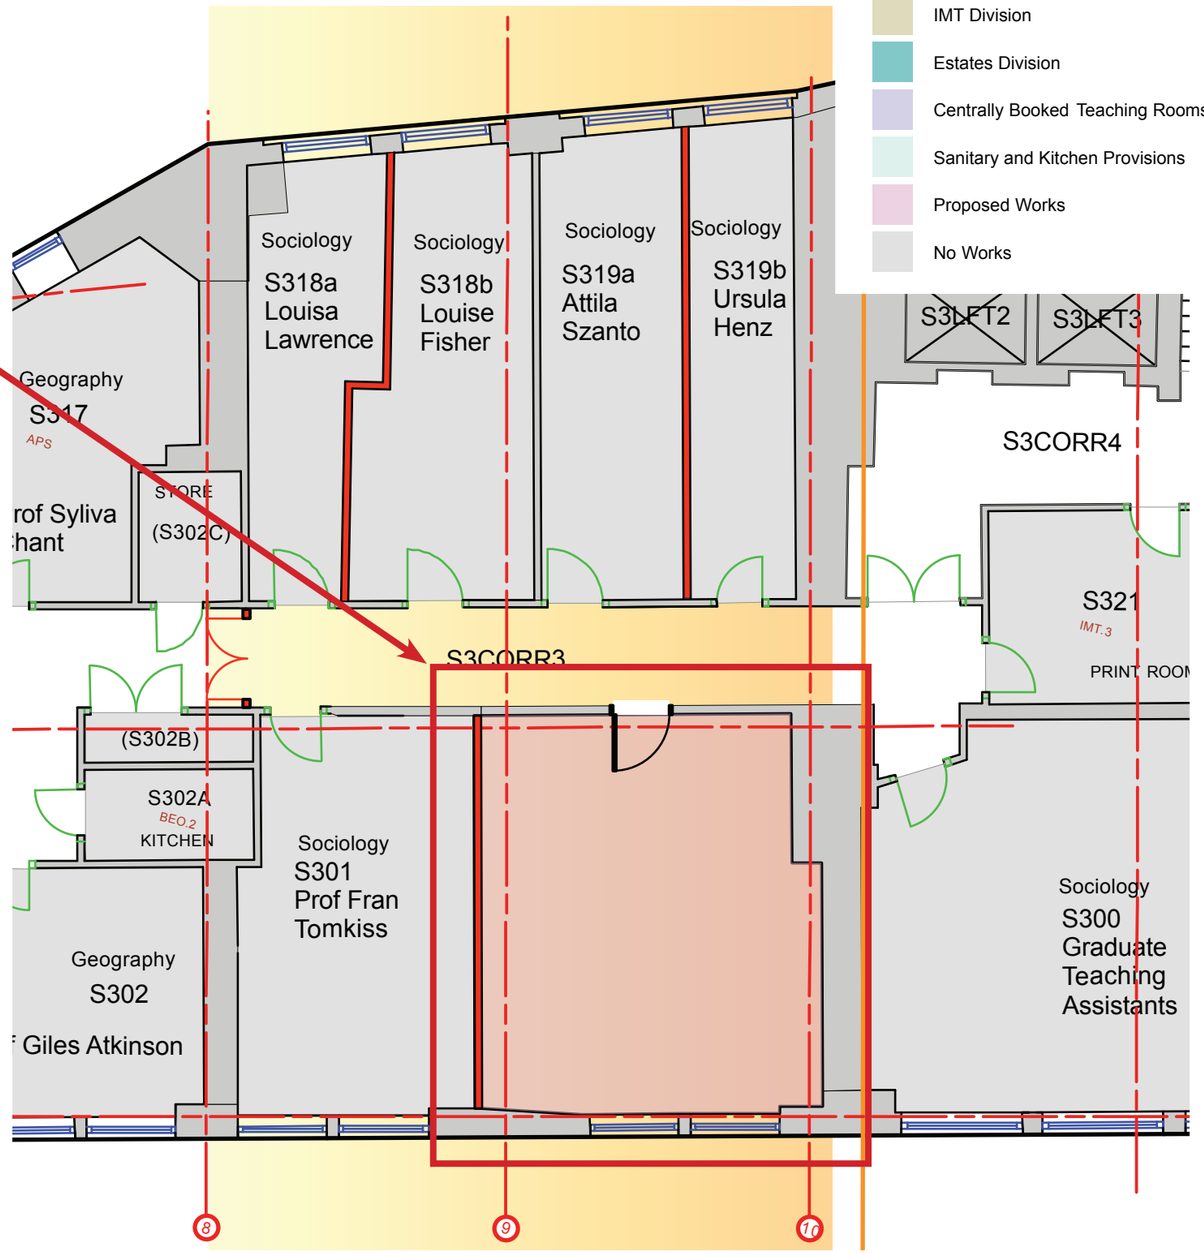

Existing Third Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 18 - Ground Floor - Move

26th June - 29th June 2015

Move occupants of IMT into ground floor accommodation.

Relocate IMT workshop into Rm S50b and S53.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

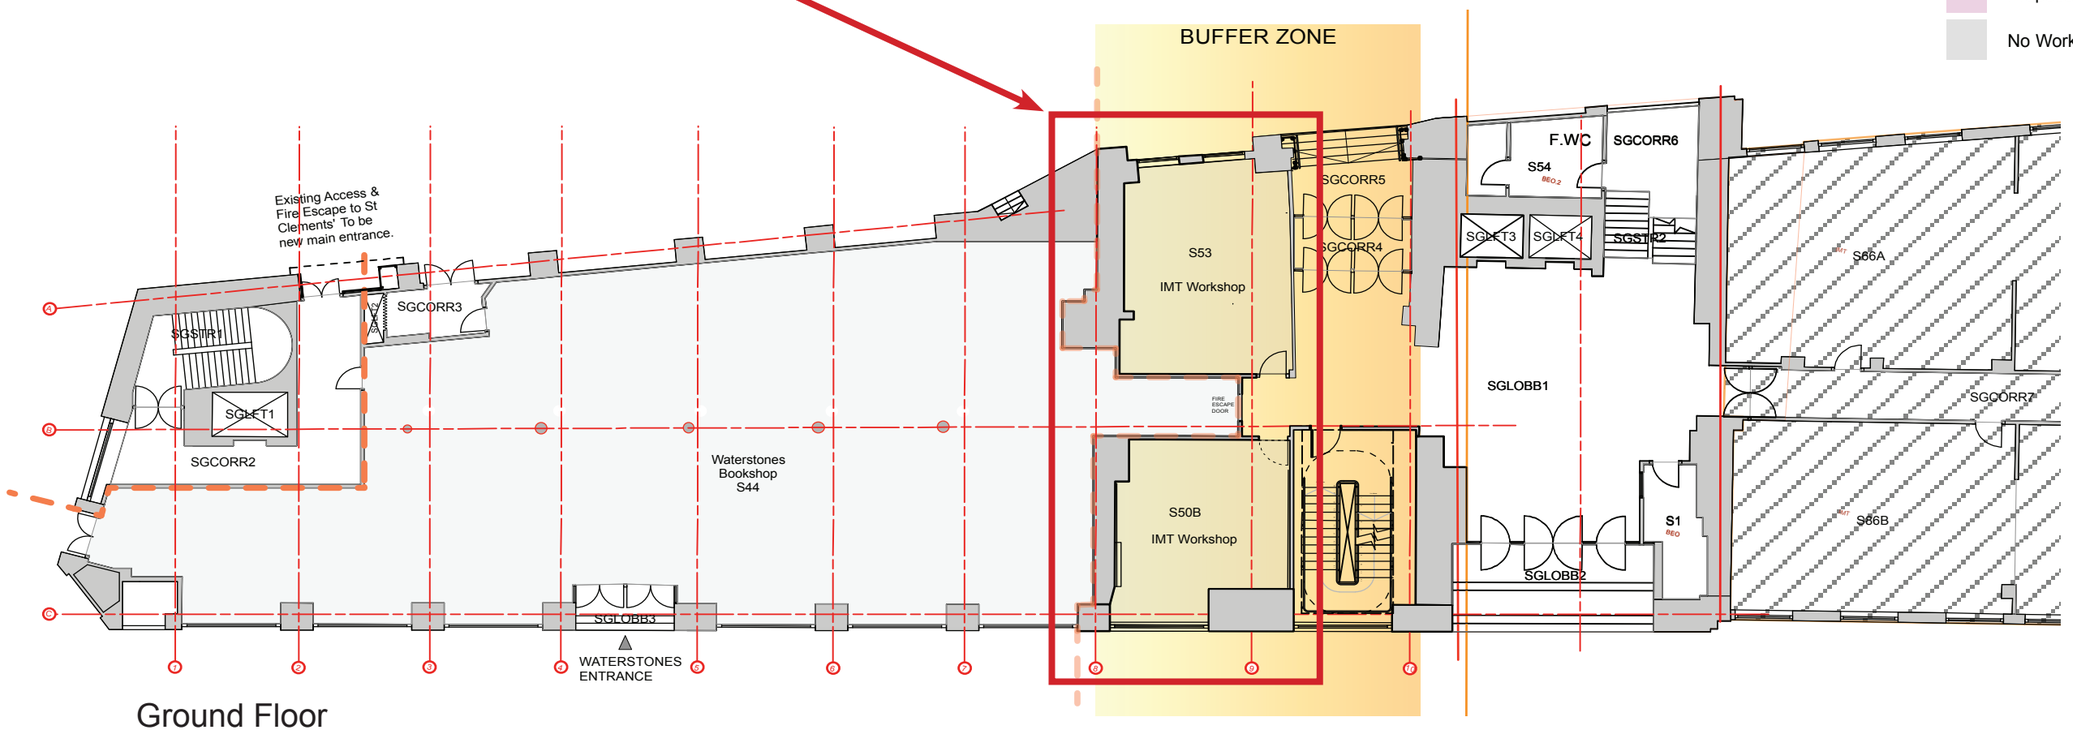

Ground Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 19 - First Floor - Move

26th June - 29th June 2015

Move occupants of Media and Comms into existing space within the Central Core and Buffer Zone
Rm S466 to S100B (???? - Media and Comms)
Rm S877 to S198 (???? - Media and Comms)

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

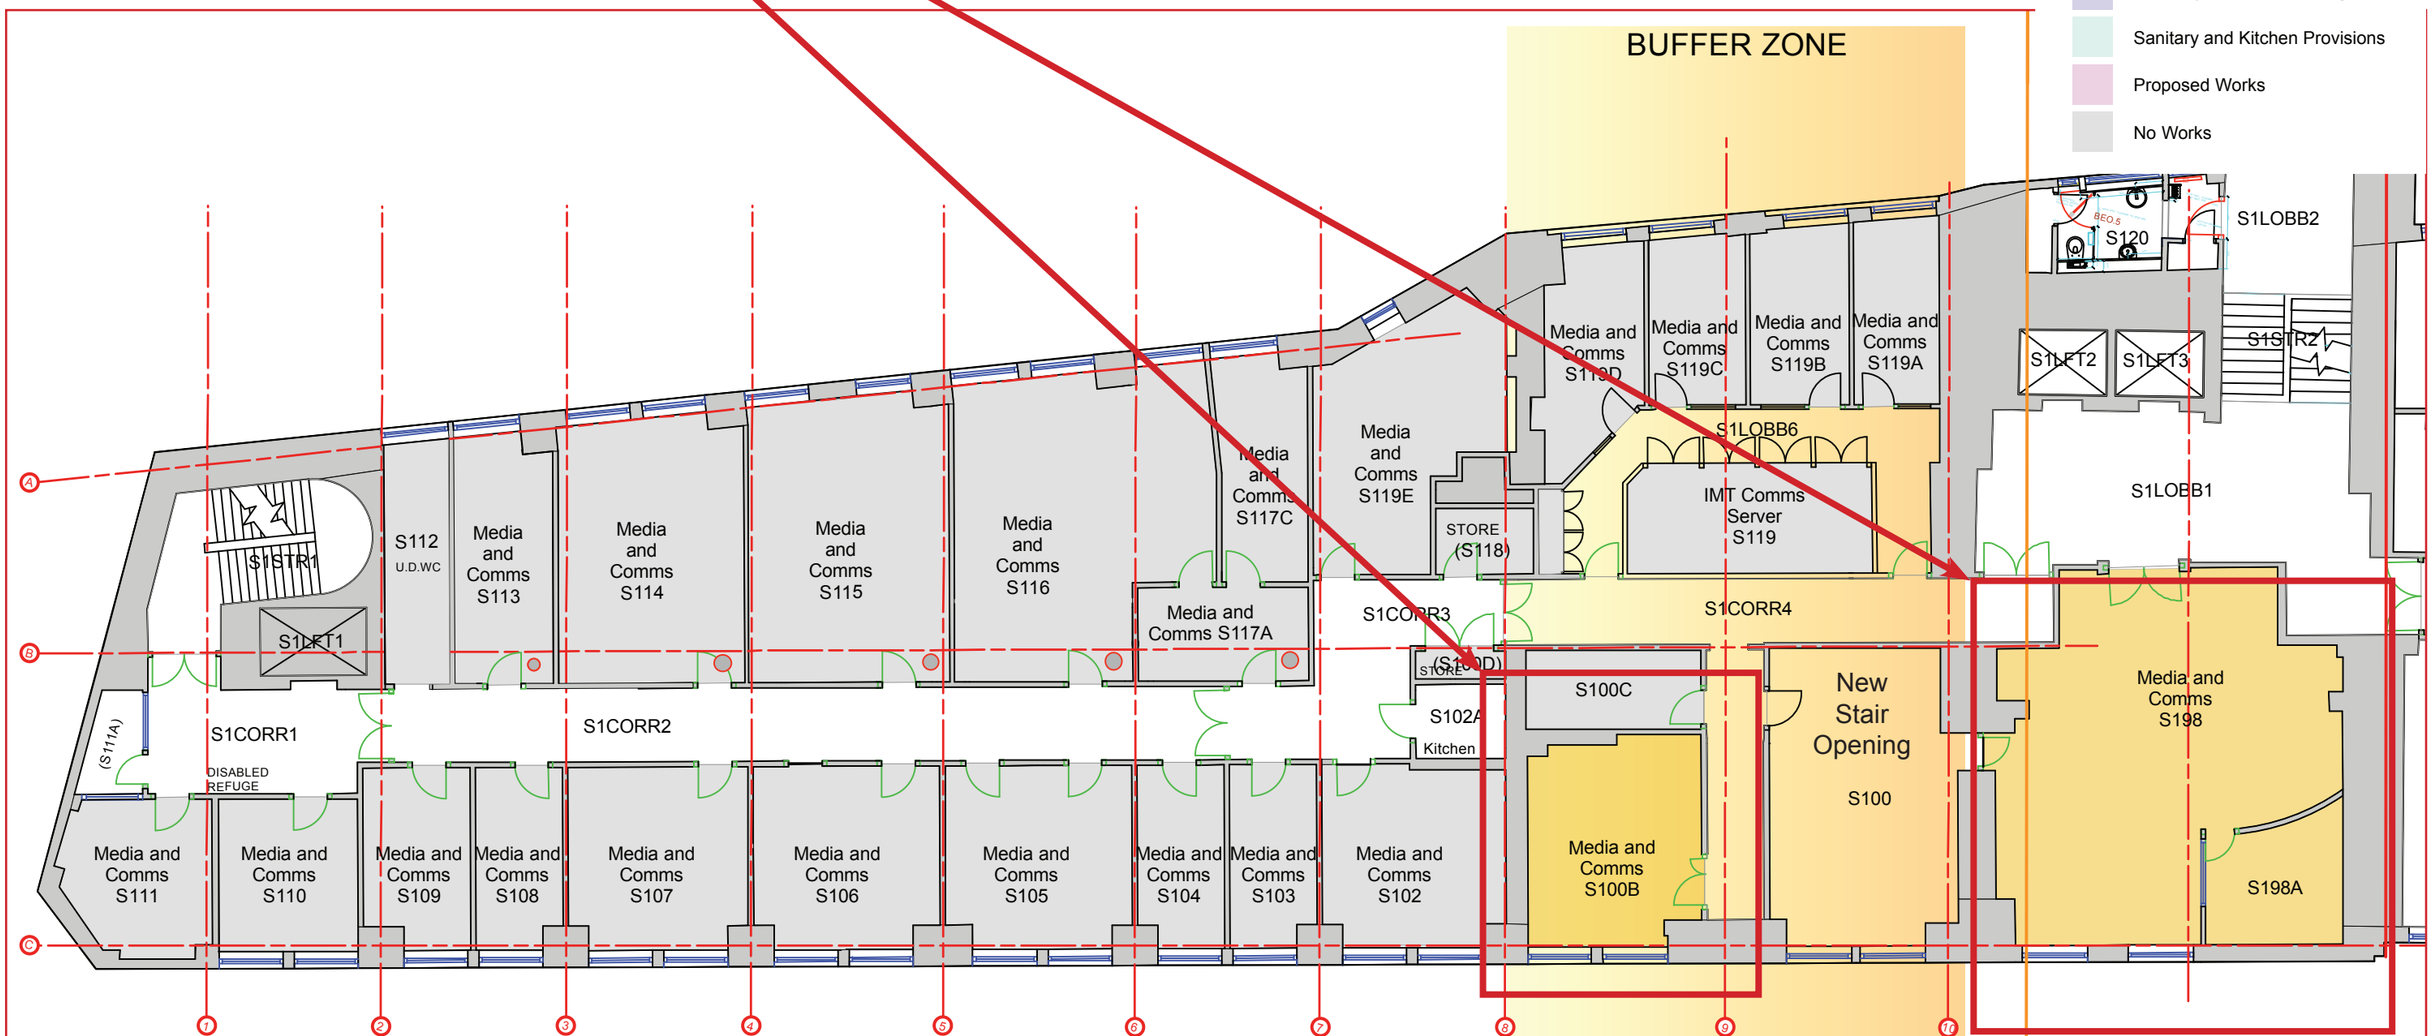

First Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 20 - Second Floor - Move

26th June - 29th June 2015

Move occupants into second floor accommodation.
Rm S264 to S200 (Resource - Sociology)
Rm S380 to S212 (Lisa McKenzie - Sociology)
Rm S376 to S213 (Carrie Friese - Sociology)
Rm S265 to S214 (Nathalie Buyts - Sociology)
All other occupants on the second floor remain in their current location

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

Existing Second Floor

Existing Third Floor

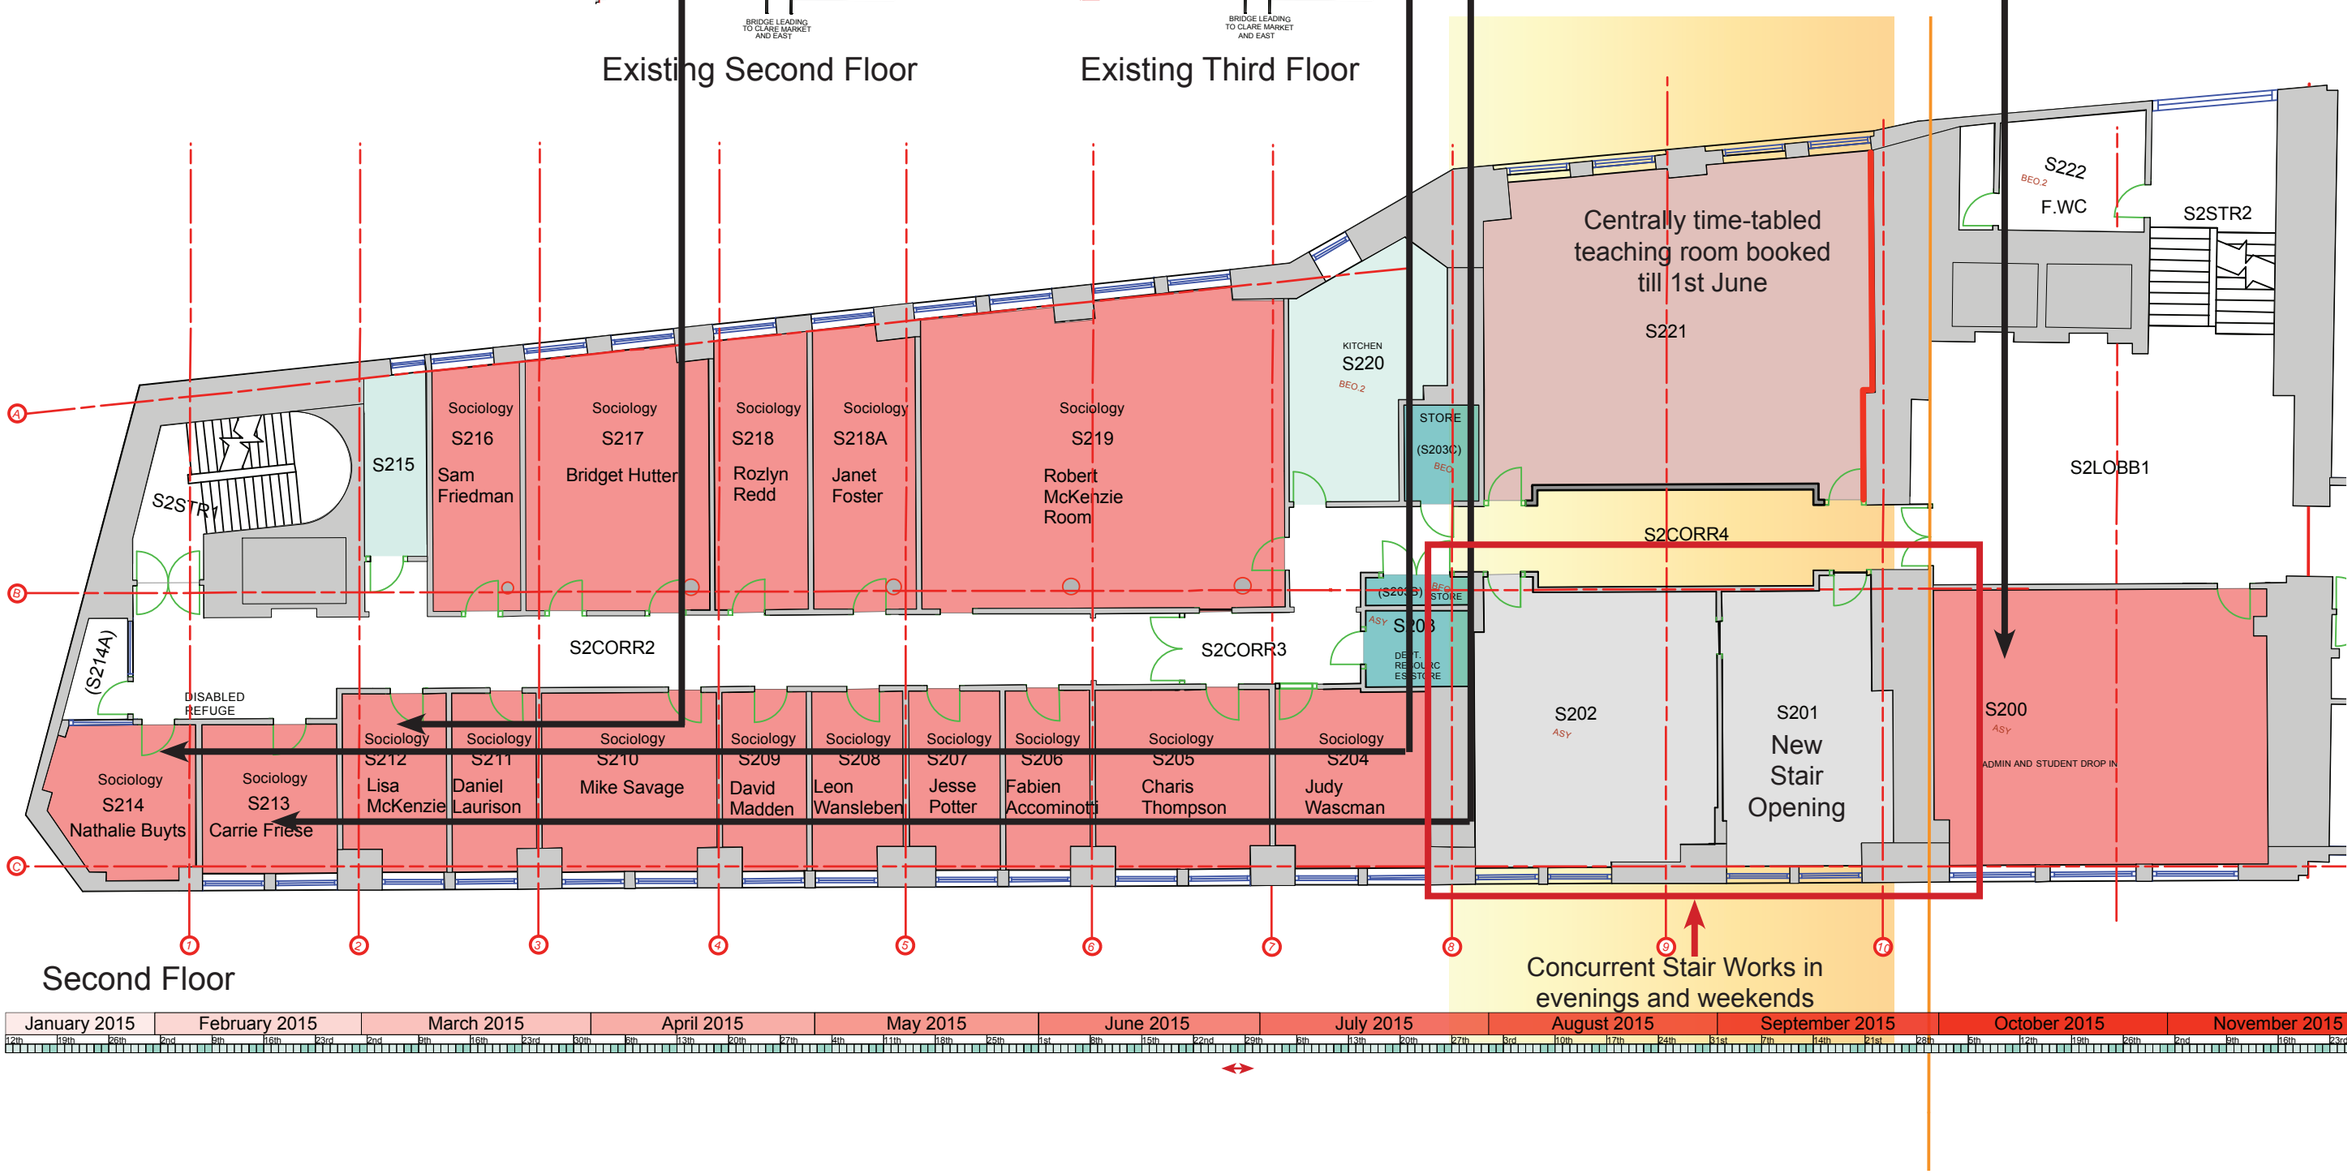

Second Floor

Concurrent Stair Works in evenings and weekends

Step 21 - Third Floor - Move

26th June - 29th June 2015

Move occupants into the 3rd floor space - mainly from the East wing.

Rm S513 to S302 (Giles Atkinson - Geography)
Rm K105 to S305 (Jennifer Baka - Geography)
Rm S417a to S306 (GTA's - Geography)
Rm S401 to S303 (u/g Study Room - Geography)
Rm S502a to S305a (Map Room Office - Geography)
Rm S502 to S314 (Map Room - Geography)
Rm S514 to S315a (Nancy Holman - Geography)
Rm S513a to S315b (Alan Mace - Geography)
Rm S500 to S316 (PhD Study Room - Geography)
Rm S515 to S317 (Sylvia Chant - Geography)

Rm S284 to S318a (Louisa Lawrence - Sociology)
Rm S285 to S318b (Louise Fisher - Sociology)
Rm S287 to S319a (Attila Szanto - Sociology)
Rm S279 to S319b (Ursula Henz - Sociology)
Rm S377 to S301 (Fran Tomkiss - Sociology)
Rm S282 to S300 (Visiting Academics - Sociology)
Rm S278 to S311 (J. Pablo Pardo-Guerra - Sociology)
Rm S382 to S313 (Gunter Gassner - Sociology)
Rm S381 to S308 (C. Olcese & T. Basi - Sociology)
Rm S276 to S307 (Emeriti - Sociology)
Rm S277 to S310 (Nigel Dodd - Sociology)

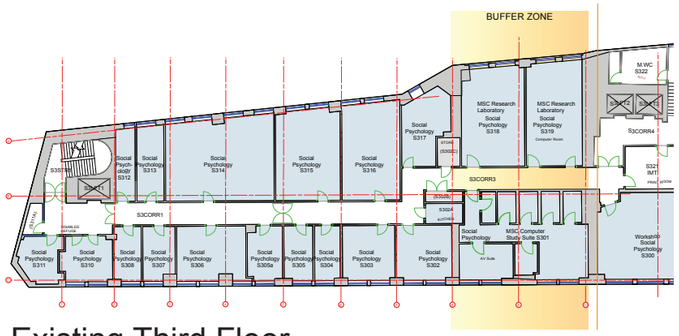

Existing Third Floor

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

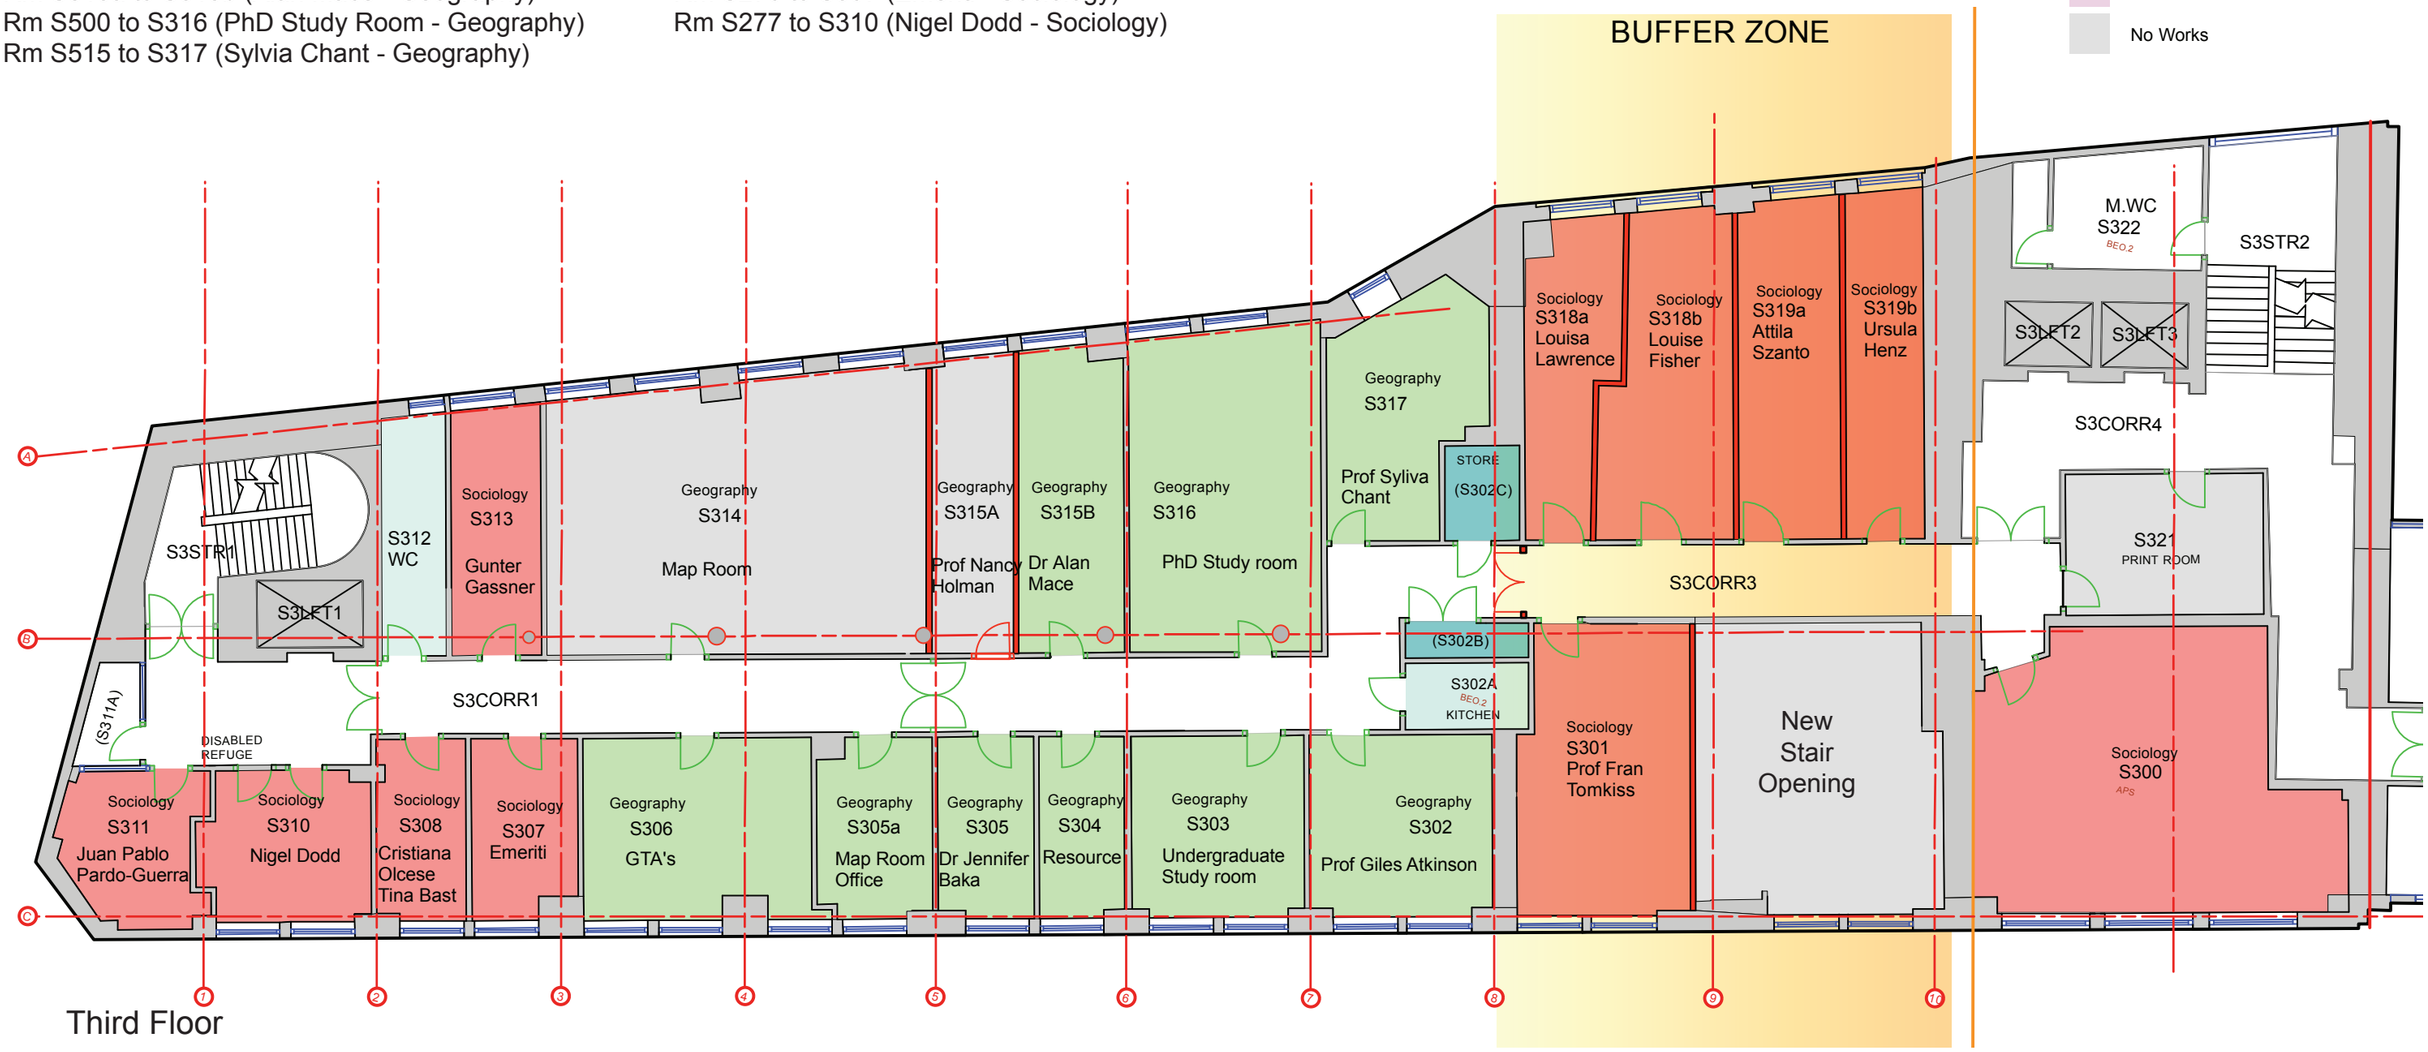

Third Floor



Step 22 - Fourth Floor - Move

26th June - 29th June 2015

Move occupants into newly formed 4th floor offices
Rm S416 - (New Assistant Professor - Geography)
Rm S501 - S417a (LSE Fellows - Geography)
Rm S876 to S400 (???? - Media and Comms)
Rm S477 to S421A (Pat McGrown - Sociology)
Rm S283 to S421B (Robin Archer - Sociology)
Rm S375 to S421C (Suki Ali - Sociology)
Rm S478 to S421D (Claire Moon - Sociology)

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

BUFFER ZONE

Sociology S421A Pat McGovern
Sociology S421B Robin Archer
Sociology S421C Suki Ali
Sociology S421D Rozlyn Redd
Geography S420 Prof Susana Mourato
(S404B)
S4LFT2
S4LFT3
S4LOBB1
S4CORR3
S4STR1
S4LFT1
S415
Geography S416 New Assistant Professor
Geography S417 Prof David Jones
Geography S417A x4 LSE Fellows
Geography S418 Dr Claire Mercer
Geography S418A Dr Cristian Hilber
Study room S419 PhD Study Room
S4CORR2
(S404A)
Cleaners S404
S403 Paper Store
Geography S401 Study Room
Media and Comms S400
S464
S487
(S414A)
DISABLED REFUGE
Geography S414 Dr Riccardo Crescenzi
Geography S413 Dr Richard Perkins
Geography S412 Laura Rozario
Geography S411 Mr Sam Colegate
Geography S410 Prof Simona Lammarino
Geography S409 Ms Elaine Goscoyne
Geography S408 Dr Gabrie Ahlfeldt
Geography S407 Prof Rodiguez Pose and Prof Michael Storper
Geography S406 Mr Lee Mager and Mr Mark Jnekins
Geography S405 Prof Paul Cheshire
Geography S402 Dr Neil Lee
BRIDGE LEADING TO OLD BUILDING

Fourth Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 23 - Fifth Floor - Move

26th June - 29th June 2015

S479 to S513 (Runnymede - Sociology)
S480 to S513a (Runnymede - Sociology)
S475, S476 to S514 (Runnymede - Sociology)
S379 to S515 (Michael McQuarrie - Sociology)
S378 to S501 (Don Slater/Elettra Bordonaro - Sociology)
S280 to S501a (Centennial Professors - Sociology)

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

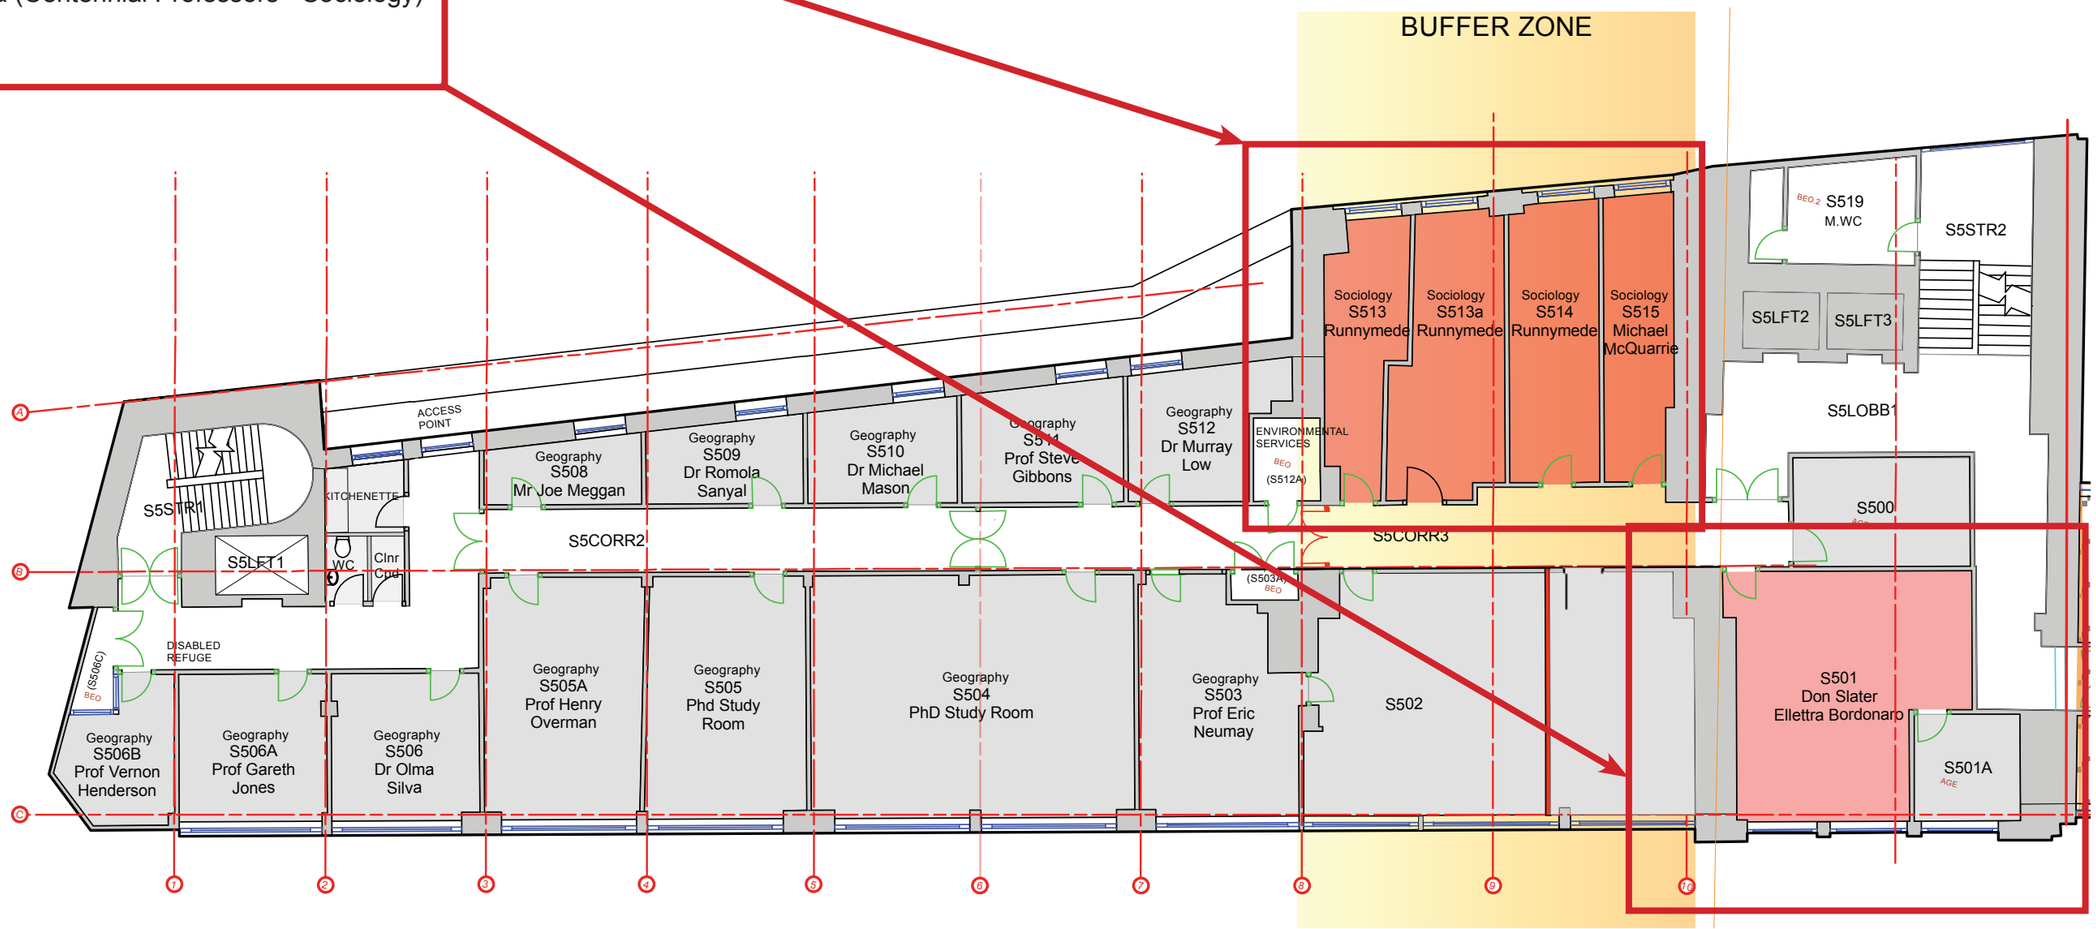

Fifth Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 24 - Sixth Floor - Move

26th June - 29th June 2015

Move occupants into newly existing 6th floor offices
Rm S266 to S600 BJS Jounral Manager - Sociology)
Rm S267 to S600 (BJS Assistant - Sociology)
Rm S268 to S600 (E&S Journal Manager - Sociology)

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

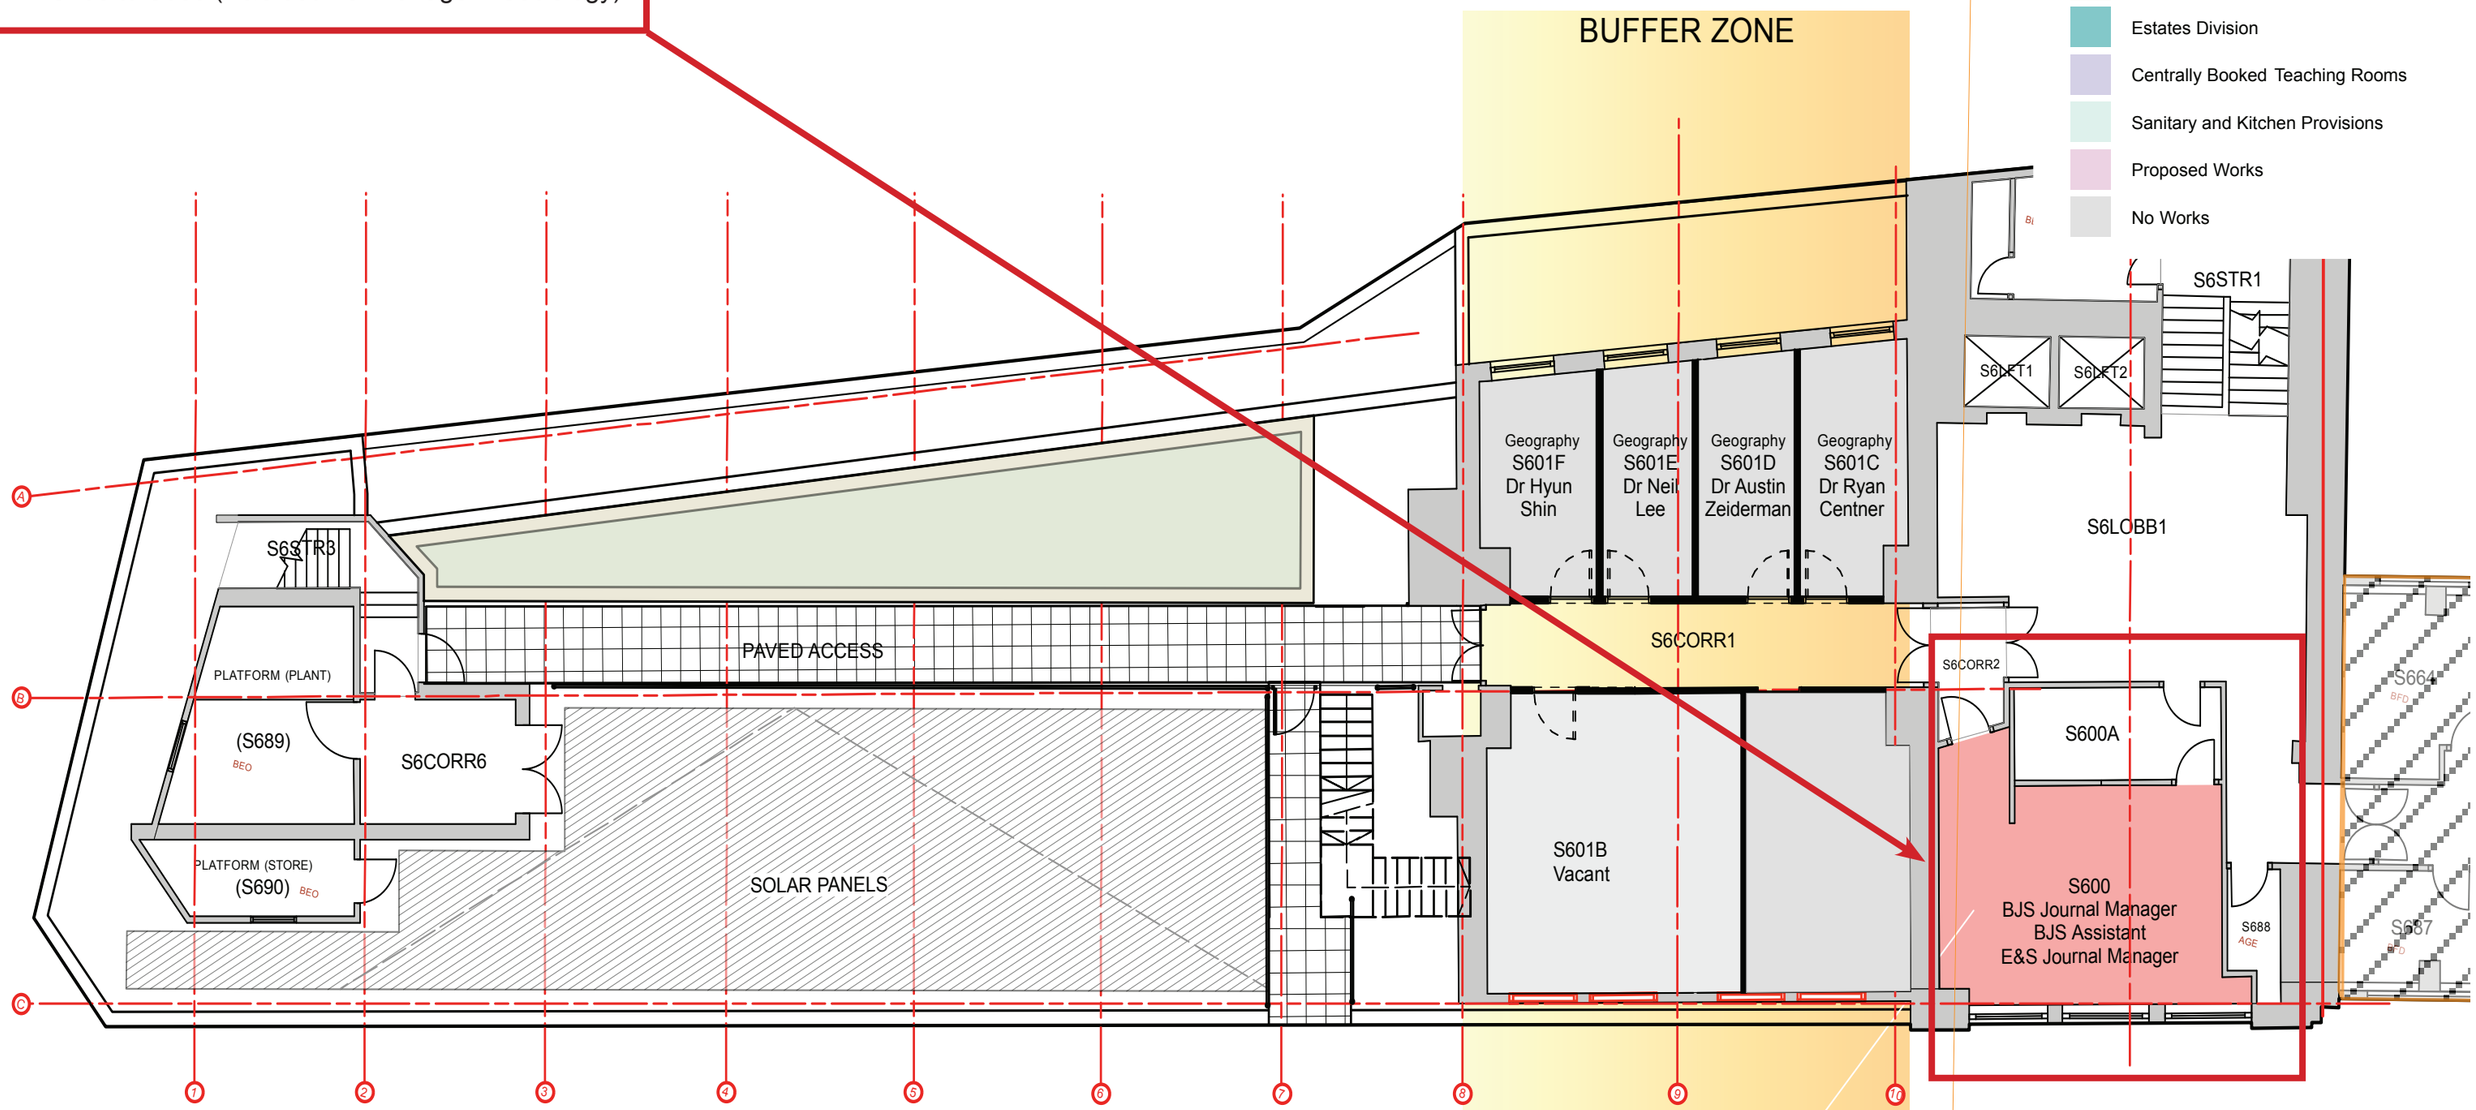

Sixth Floor



Step 25 - Demolitions - 1st cut of East wing

From 1st July 2015

Carry out first cut in demolitions works along the line of the East Wing and Central Core.

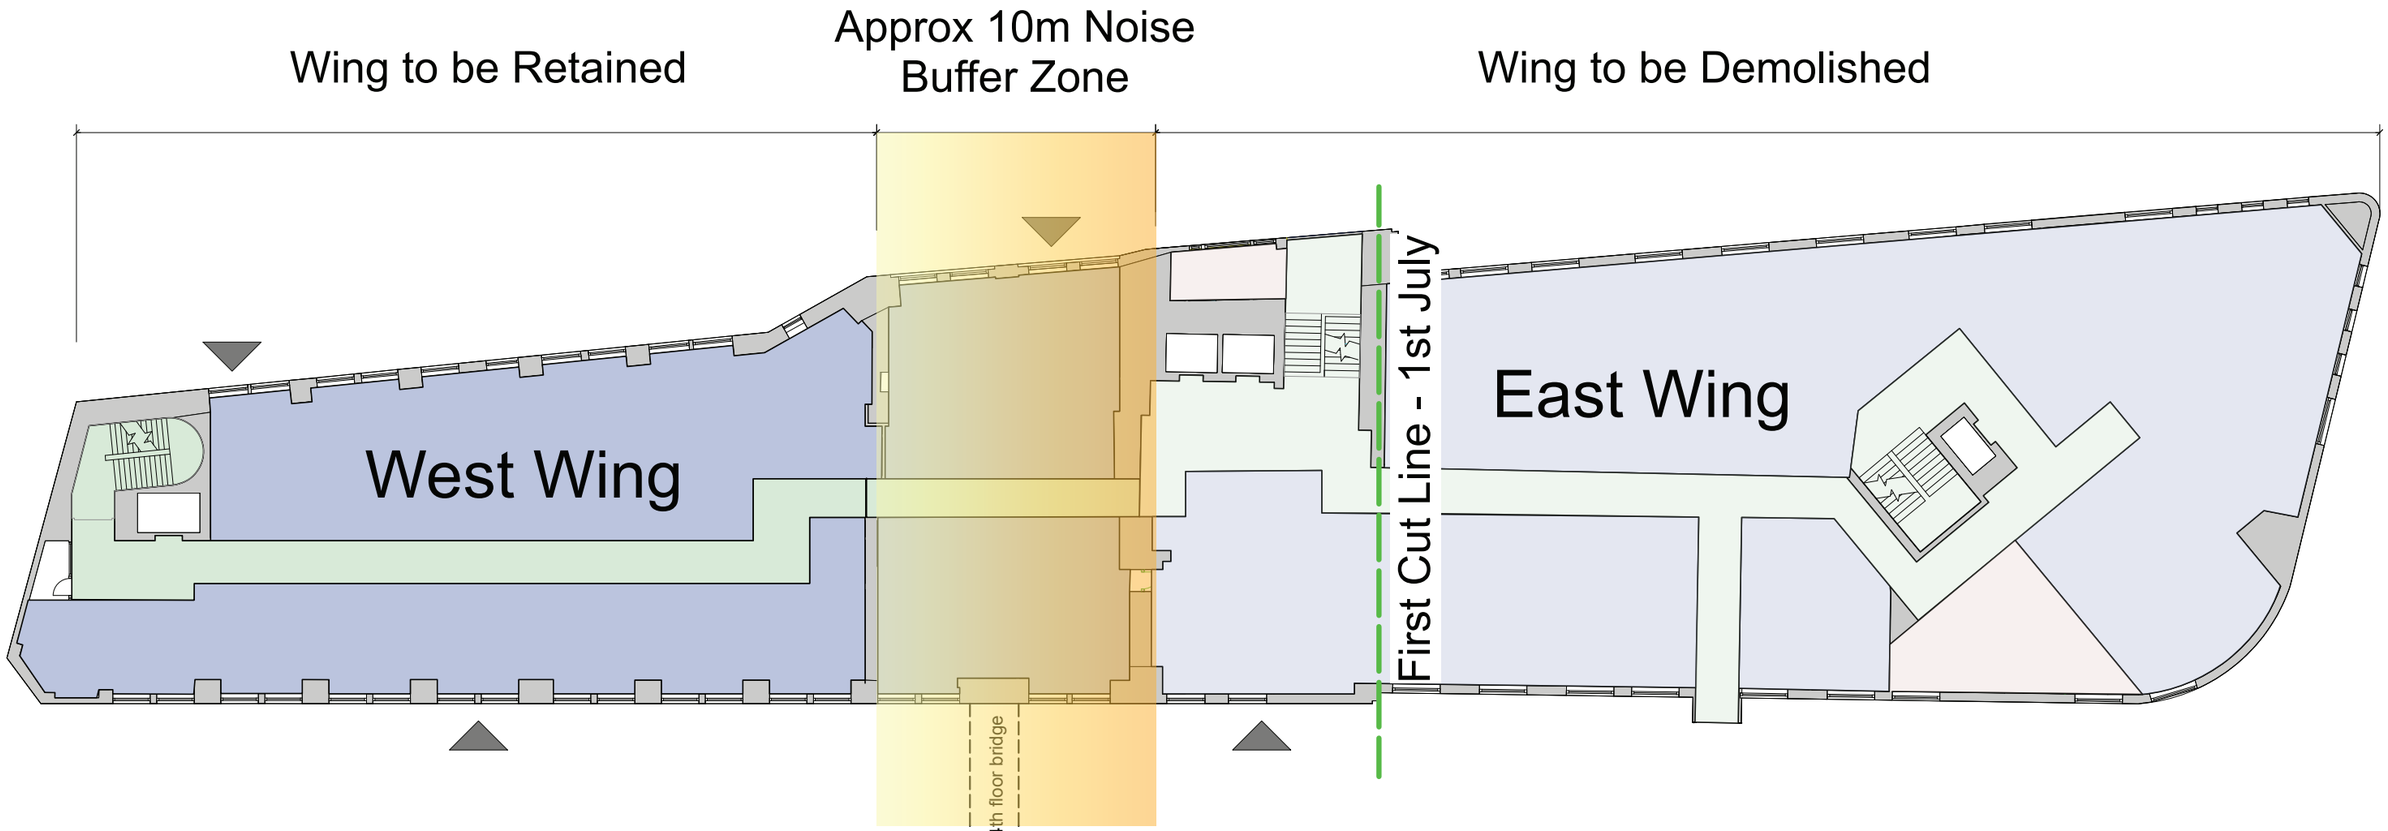

Typical Floor Plan



Step 26 - New Stair Core - Works

13th July - 14th August 2015

Form cut out for stair core from 3rd to 6th floors within buffer zone including new toilet accommodation to 5th Floor and structural steelwork and windows to 6th floor.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

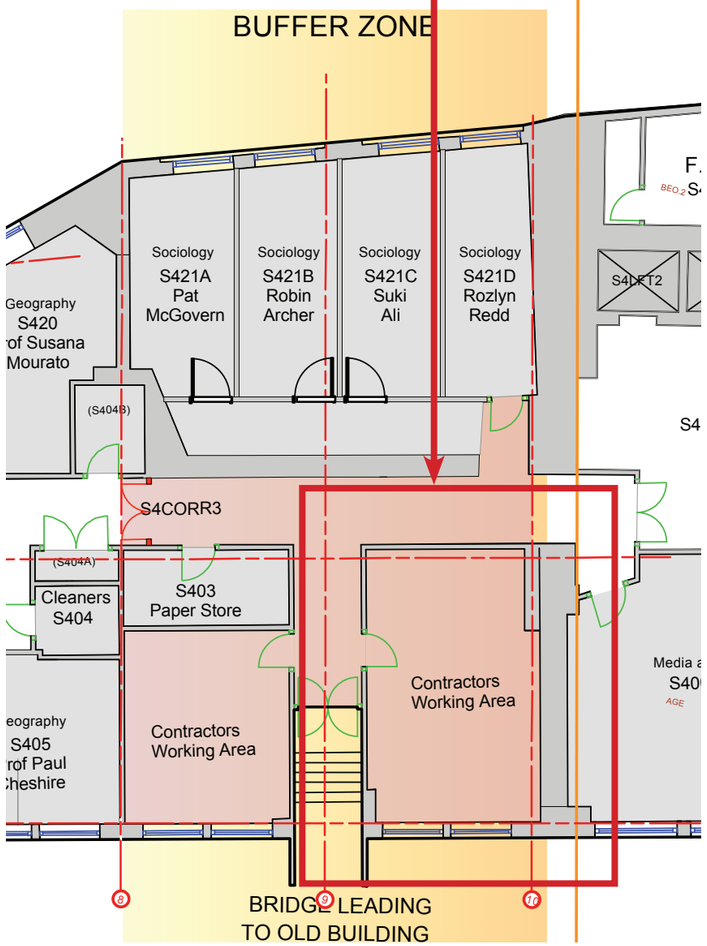

Proposed Fourth Floor

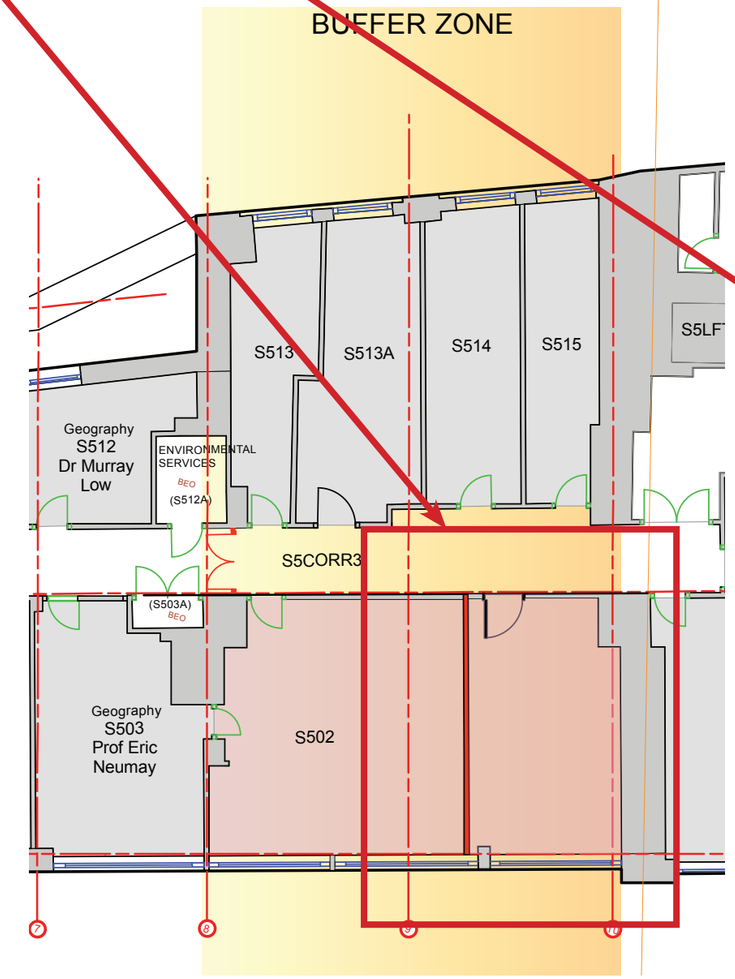

Proposed Fifth Floor

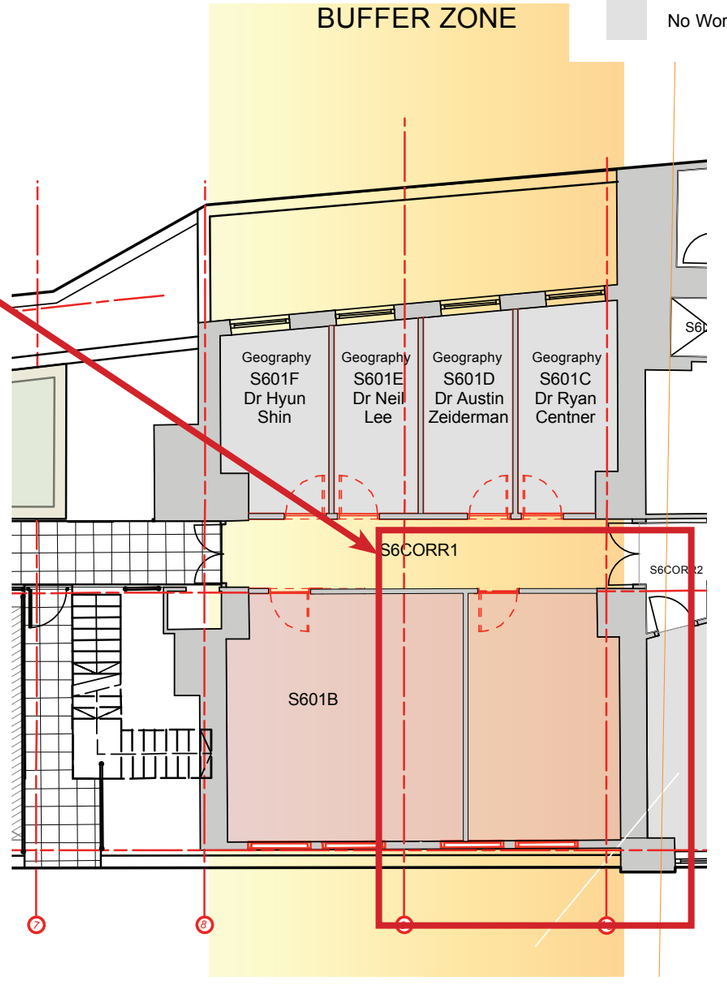

Proposed Sixth Floor



Step 27 - Sixth Floor - Move

21st August 2015

Move RUPS Teaching Studio furniture into Rm S601b. Furniture from existing Rm S400 to be stored from 26th June as Media and Comms take this space from then.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

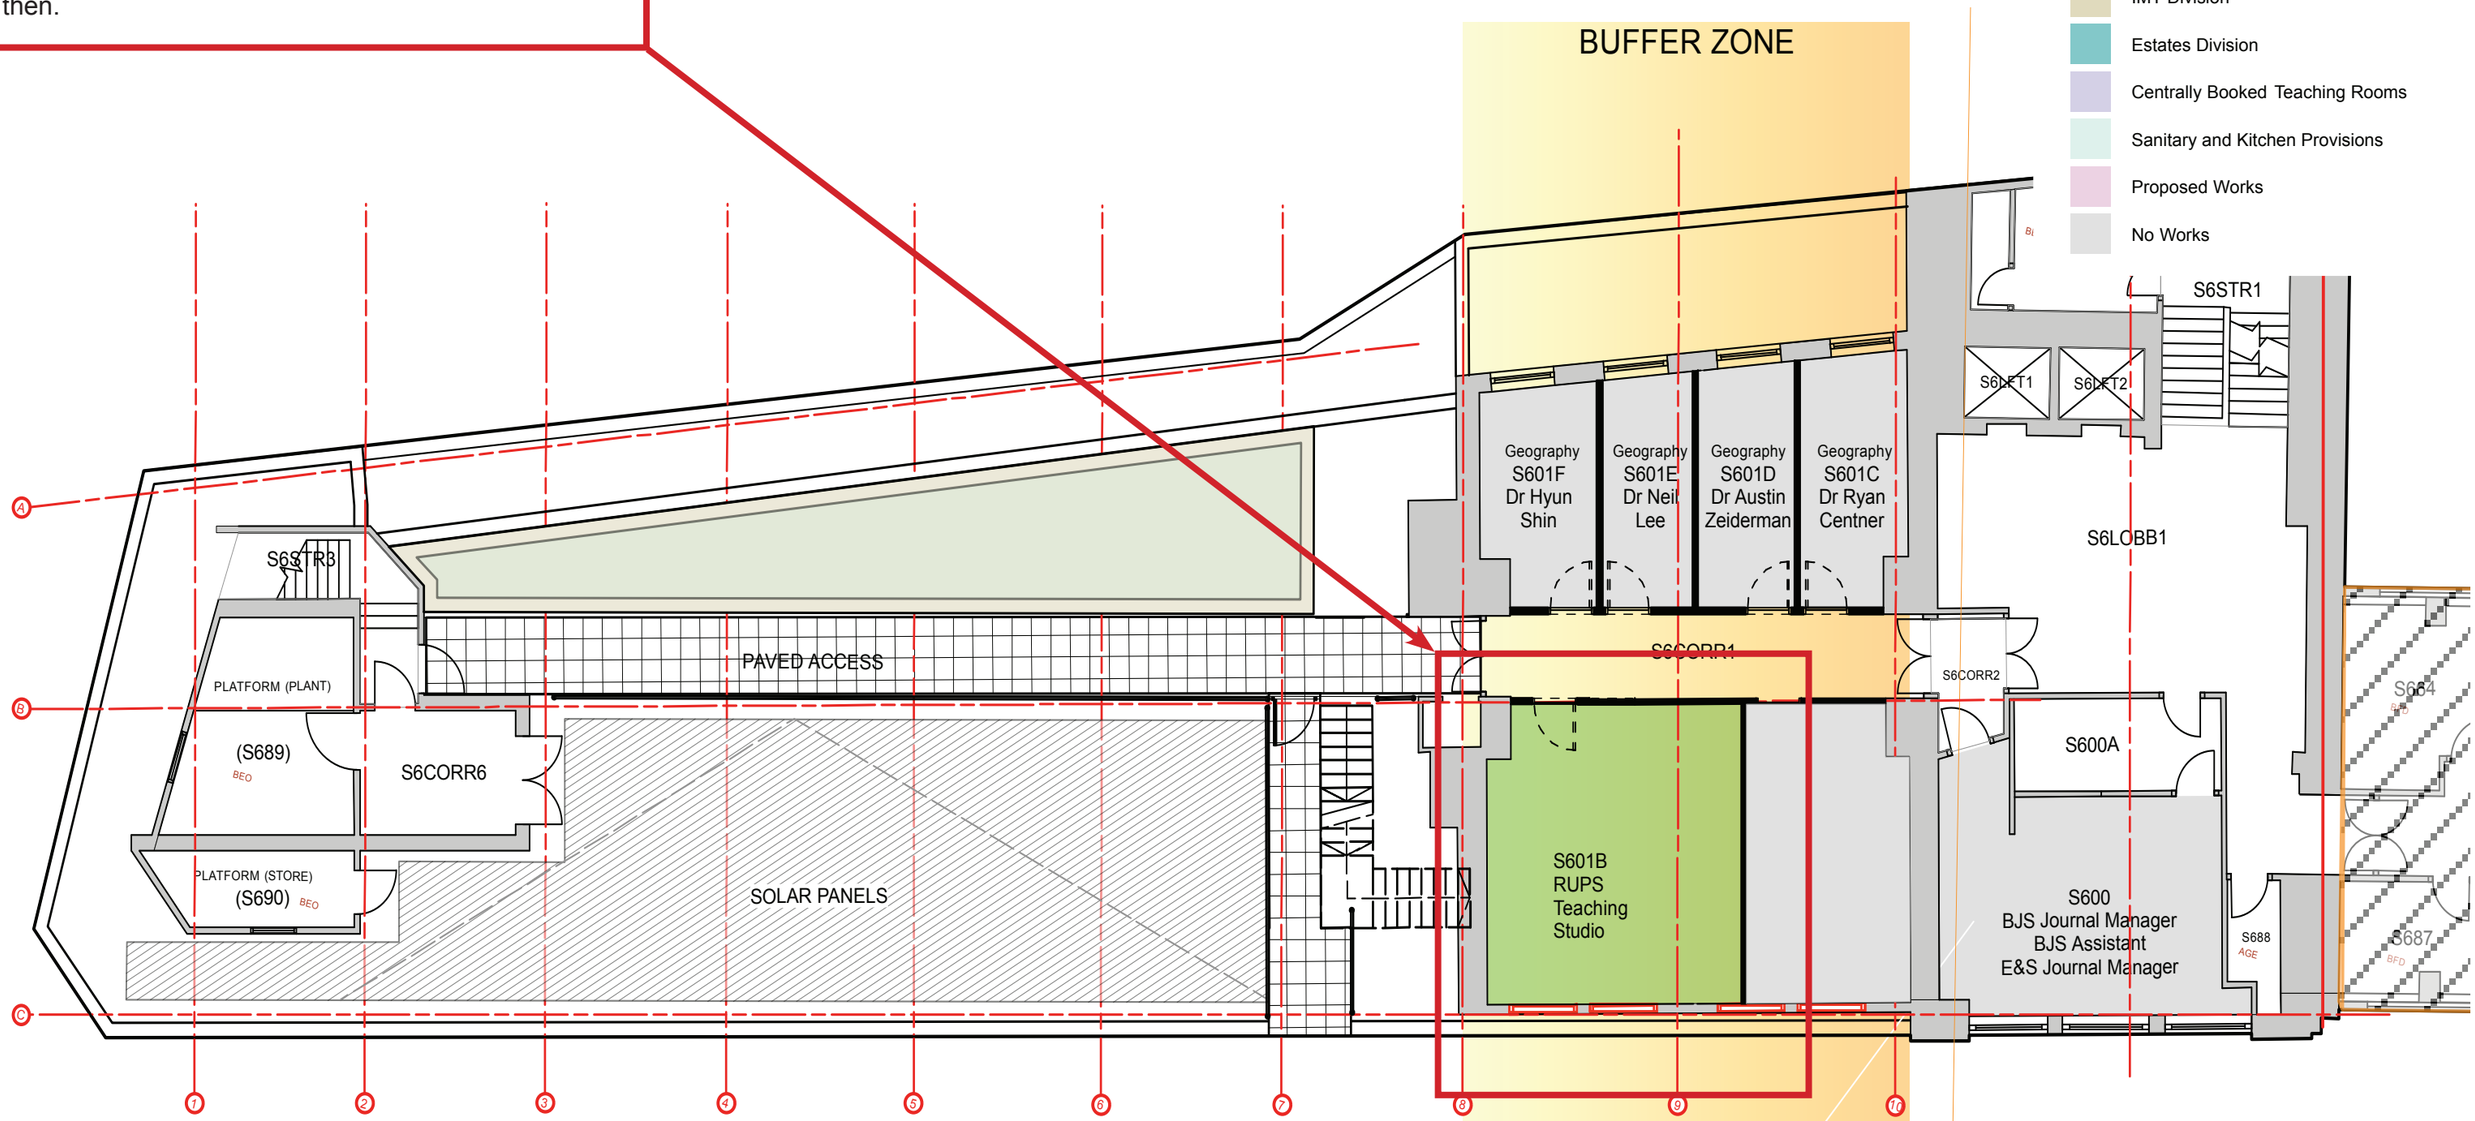

Sixth Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 28 - First Floor - Vacate

18th Sept - 21st Sept 2015 (TBC)

Move Media and Comms out of St Clement's west wing into Tower 2 Level 6 & 7.

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

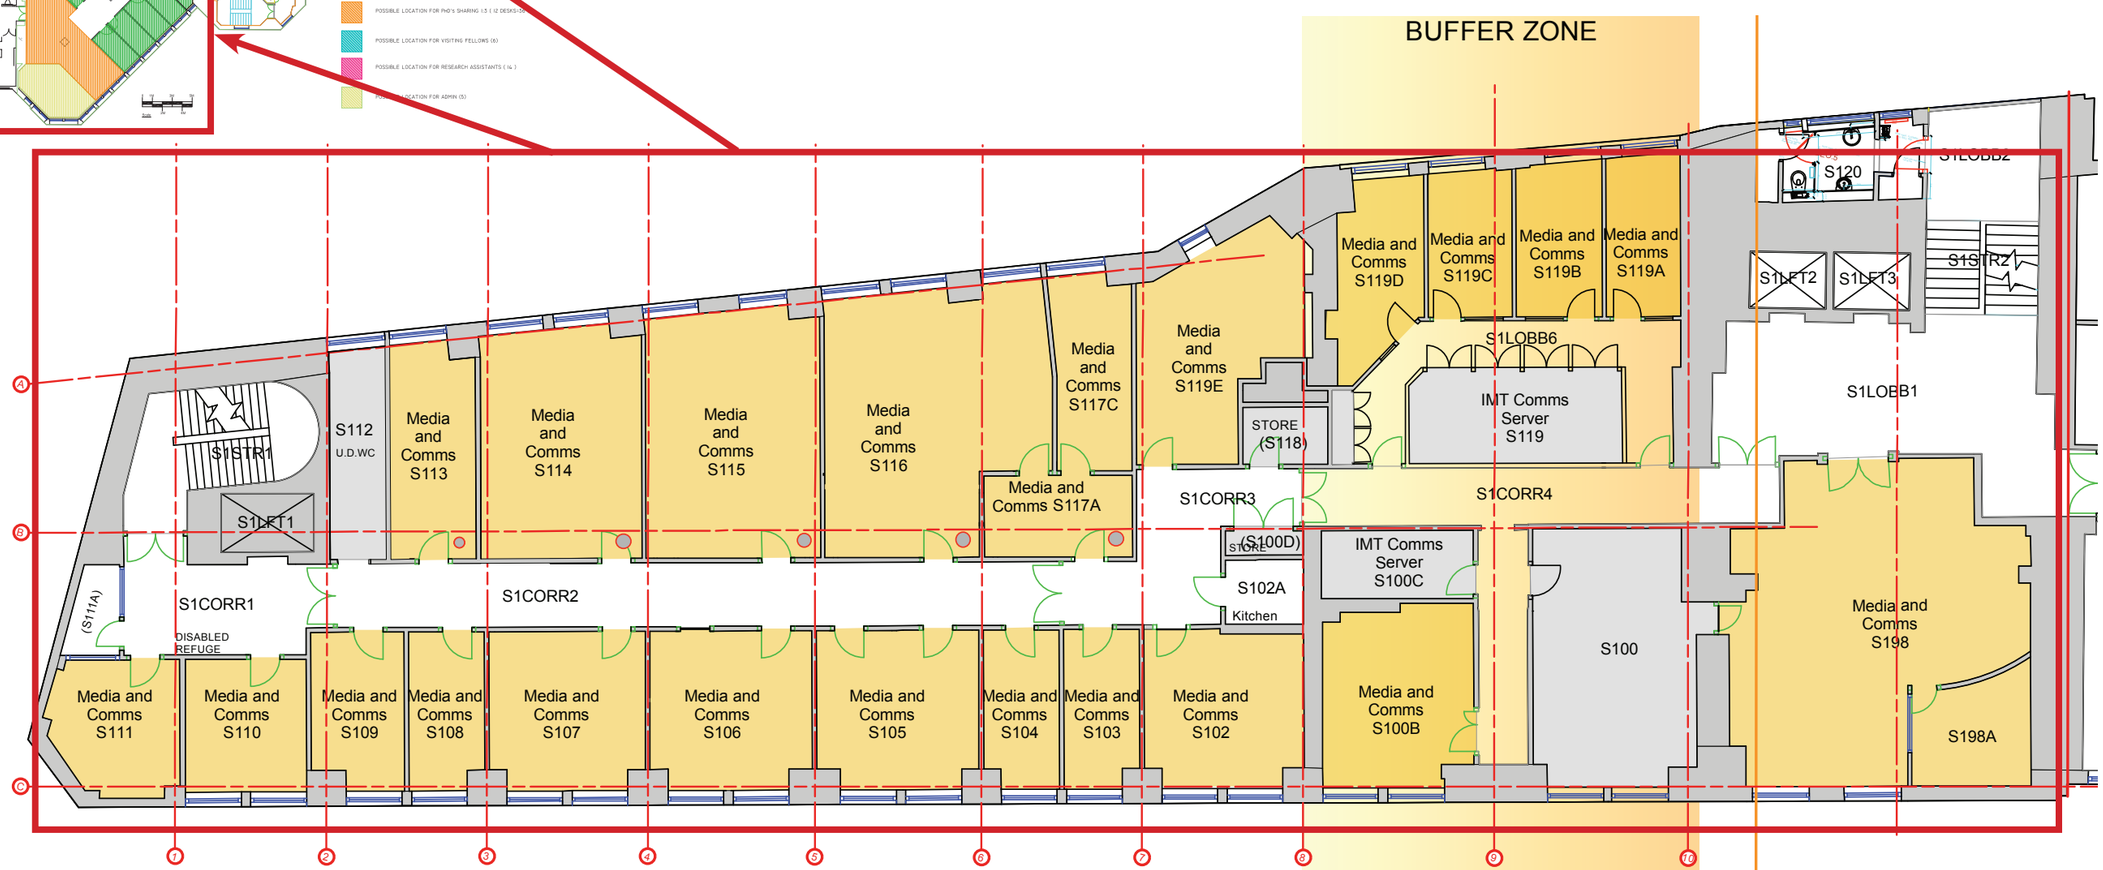

Existing First Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 29 - First Floor - Works

21st Sept - 2nd Oct 2015

Carry out works to 1st floor offices and acoustic blanket to flank wall adjacent to Rm S119A and new door between S102 and S103. S116 is to be provided with a relocated glazed partition and door from S200.

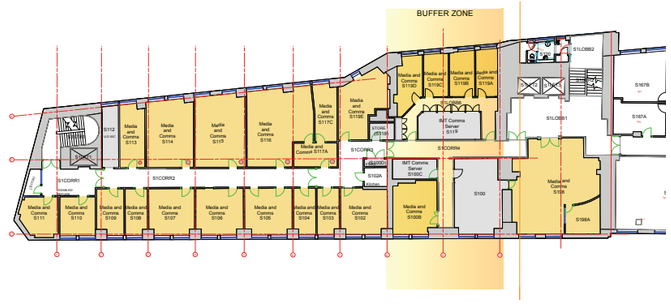

Existing First Floor

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

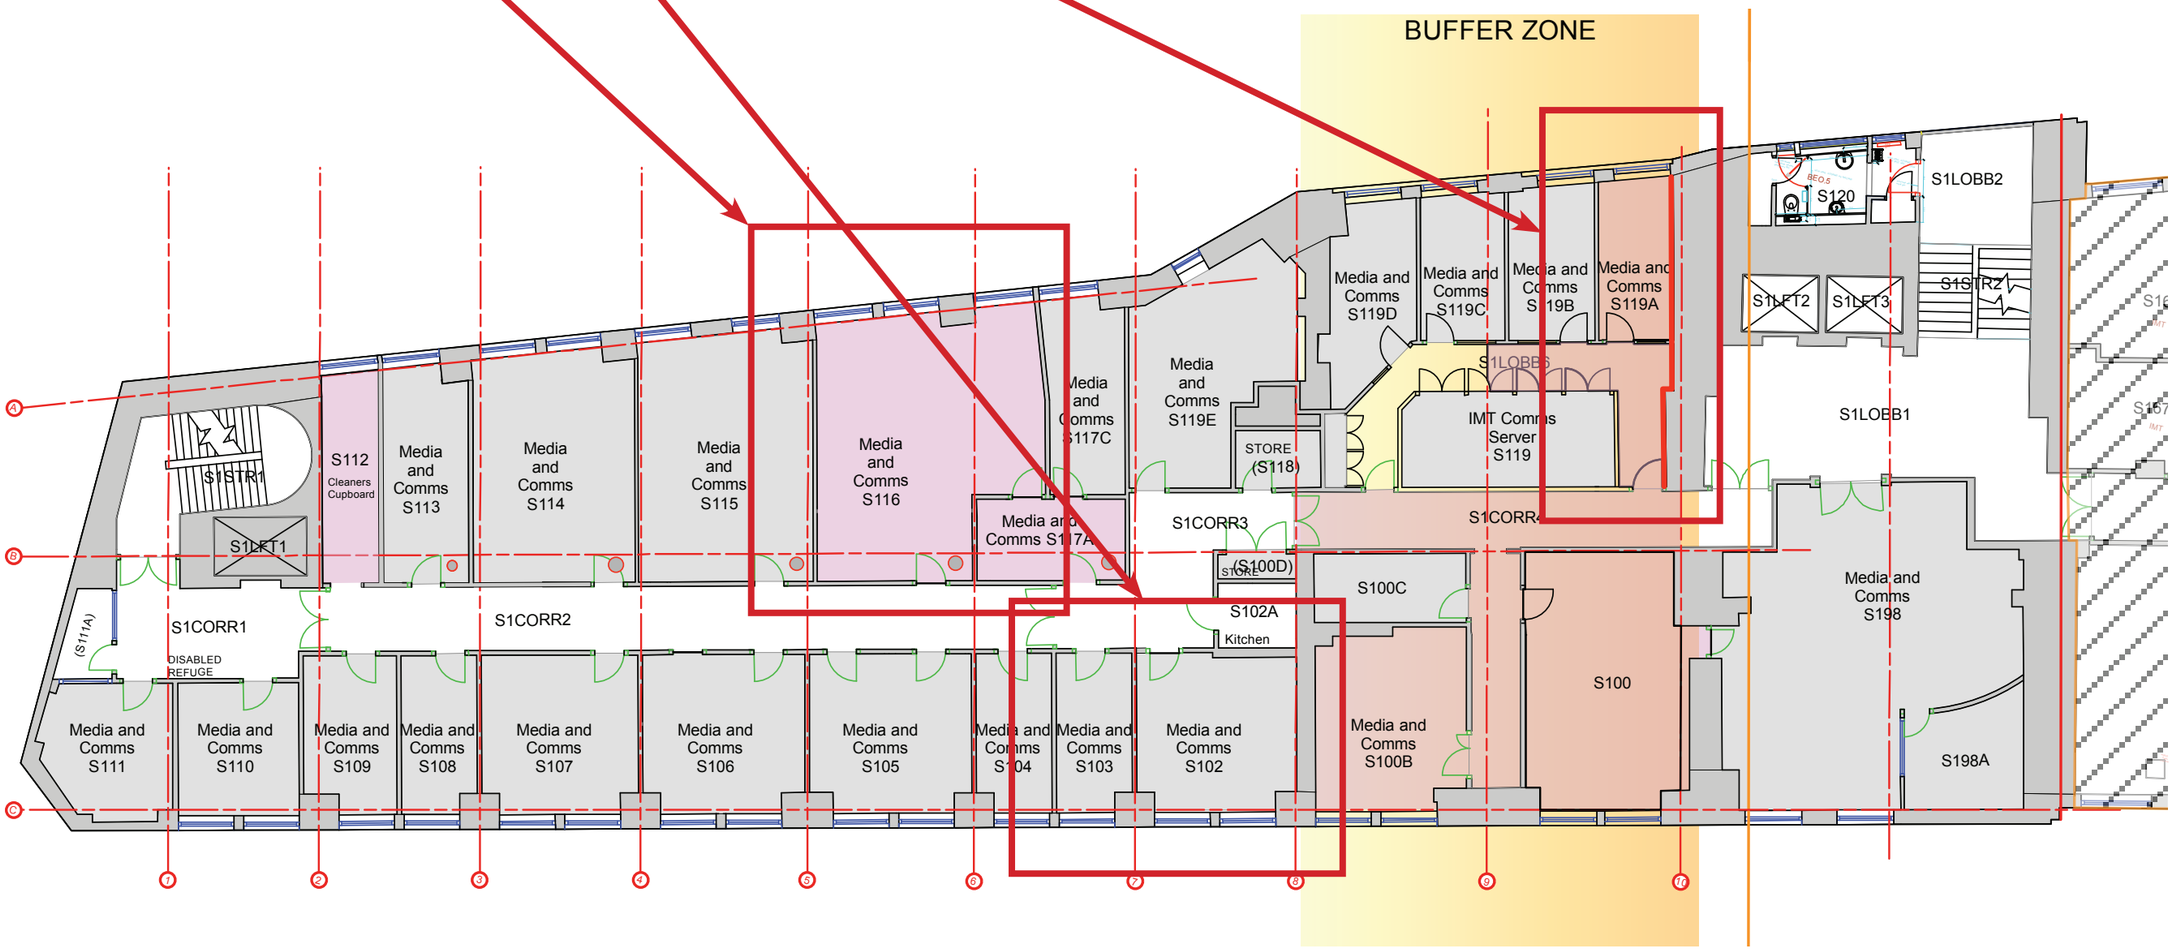

Proposed First Floor



Step 30 - First Floor - Move

2nd Oct - 5th Oct 2015 (TBC)

Move Sociology out of buffer zone and central core of St Clement's into final location.

Rm S319b to S102 (Ulsula Henz - Sociology)
Rm S319a to S103 (Attila Szanto - Sociology)
Rm S501a to S104 (Centennial Professors - Sociology)
Rm S421b to S105 (Robin Archer - Sociology)
Rm S421c to S106 (Suki Ali - Sociology)
Rm S421a to S107 (Pat McGovern - Sociology)
Rm S313 to S108 (Gunter Gassner - Sociology)
Rm S515 to S109 (Michael McQuarrie - Sociology)
Rm S501 to S110 (Don Slater - Sociology)
Rm S501 to S111 (Elettra Bordonaro)
Rm S421d to S113 (Claire Moon - Sociology)

Rm S301 to S114 (Fran Tomkiss - Sociology)
Rm S300 to S115 (Visitors - Sociology)
Rm S200 to S116 (Admin/Student Drop In - Sociology)
Rm S200 to S117 (Administration/Resource - Sociology)
Rm S275 to S119e (GTA's - Sociology)
Rm S318b to S119d (Louise Fisher - Sociology)
Rm S318a to S119c (Louisa Lawrence - Sociology)
Rm S600 to S119b (BJS Manager - Sociology)
Rm S600 to S119a (BJS Admin/E&S Journal Manager - Sociology)

AREA KEY

- Geography Department
- Sociology Department
- Media and Comms Department
- Social Psychology
- IMT Division
- Estates Division
- Centrally Booked Teaching Rooms
- Sanitary and Kitchen Provisions
- Proposed Works
- No Works

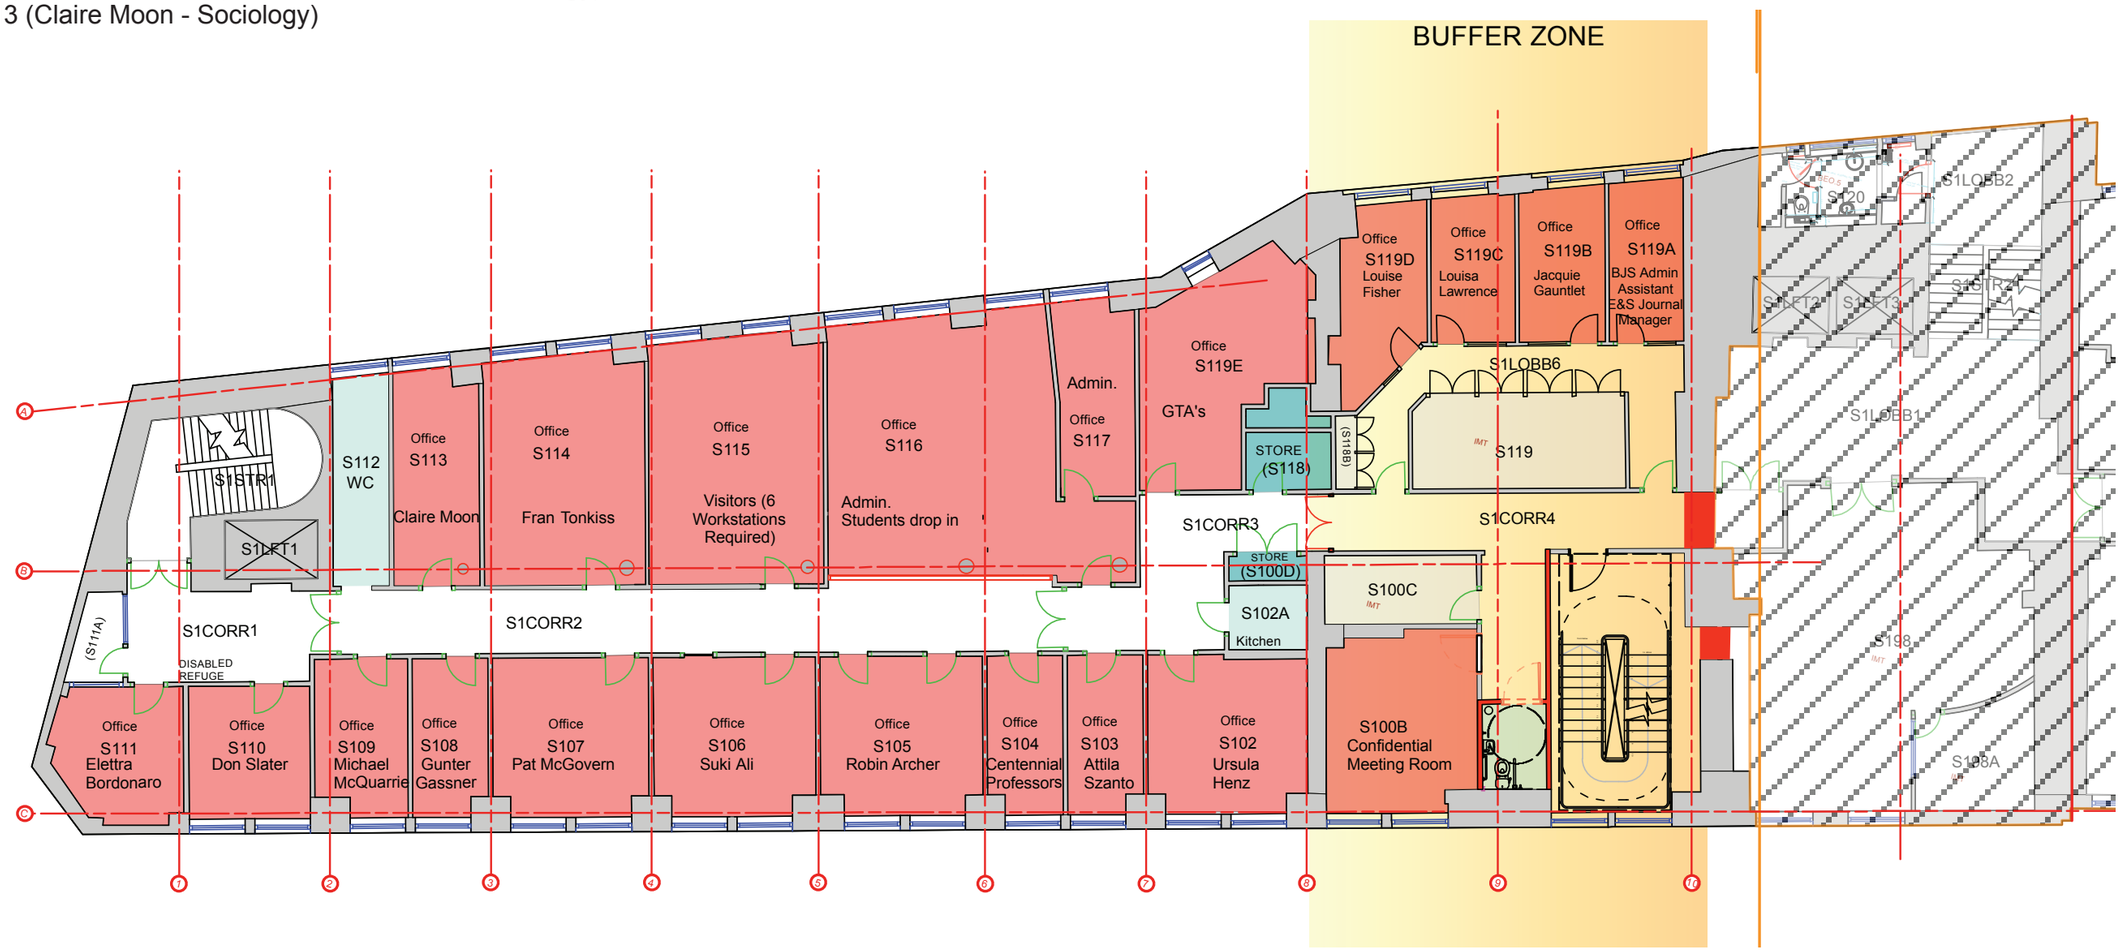

Proposed First Floor

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 31 - Stair Core - Works

23rd Oct 2015

Completion of new Stair core within Buffer Zone

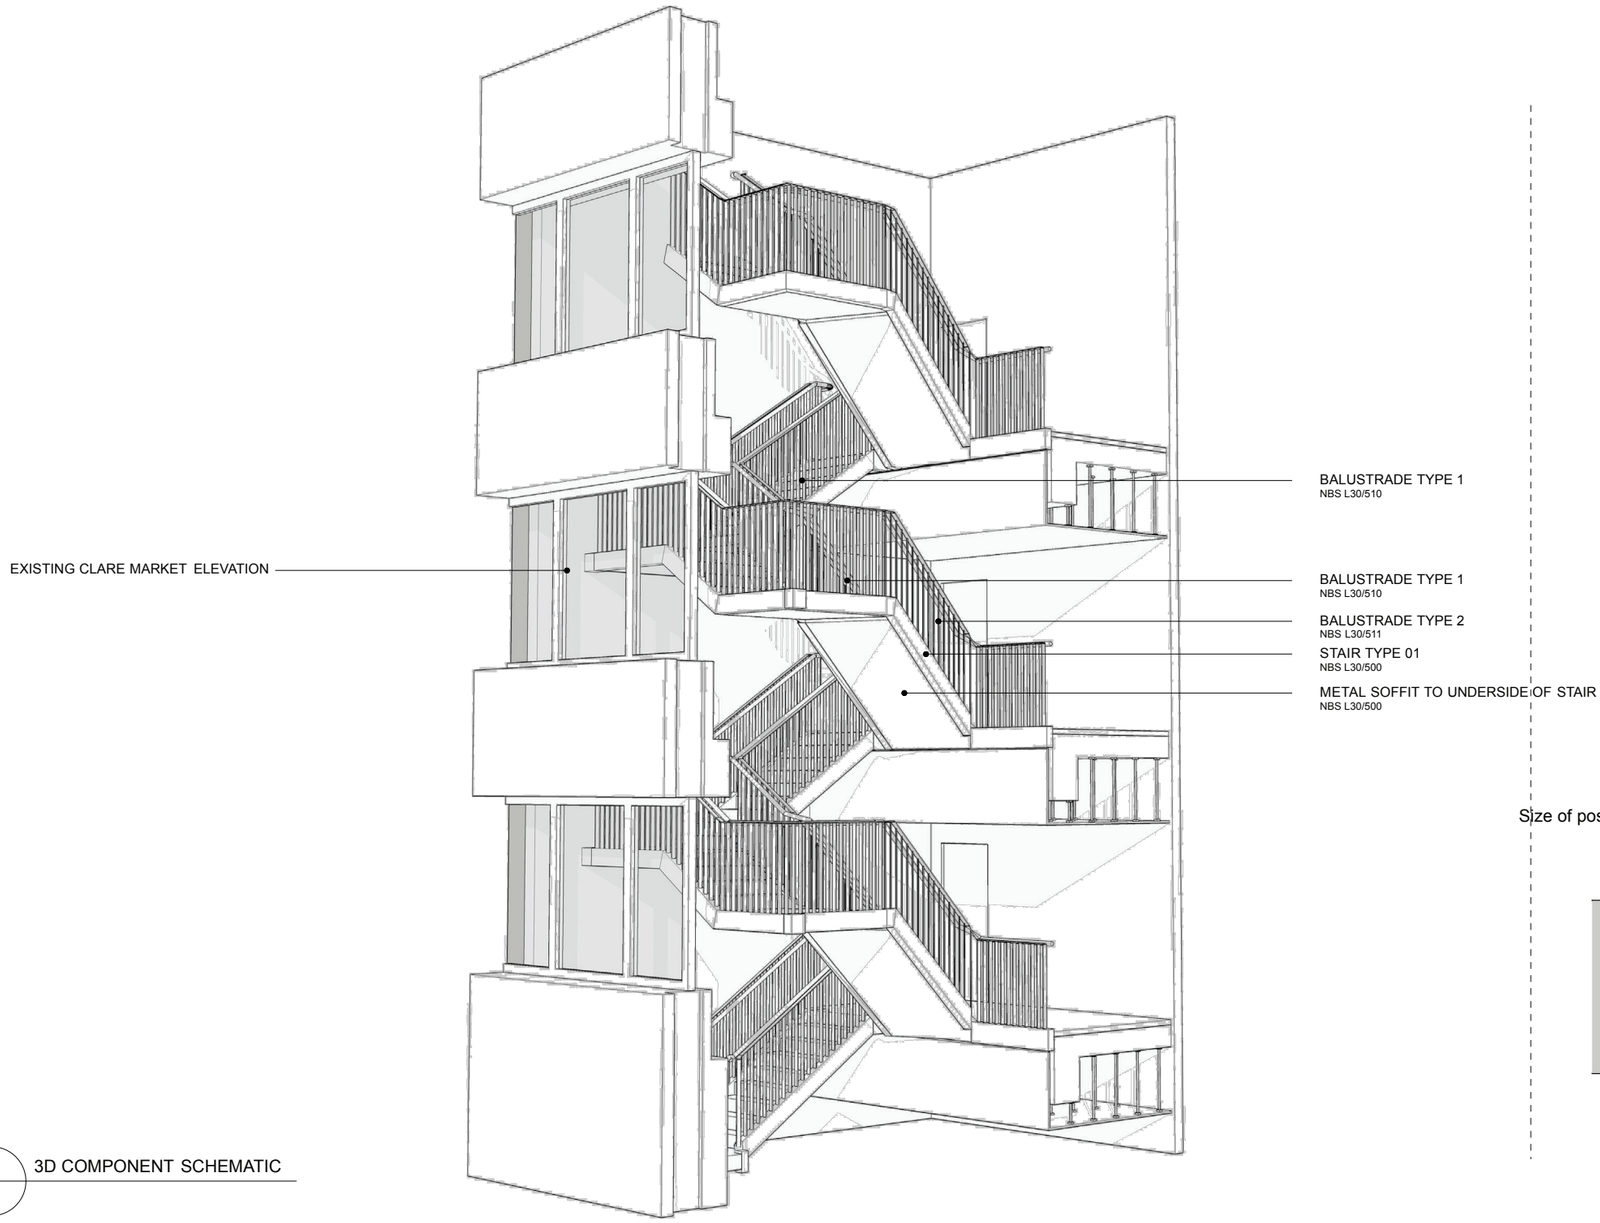

01 3D COMPONENT SCHEMATIC

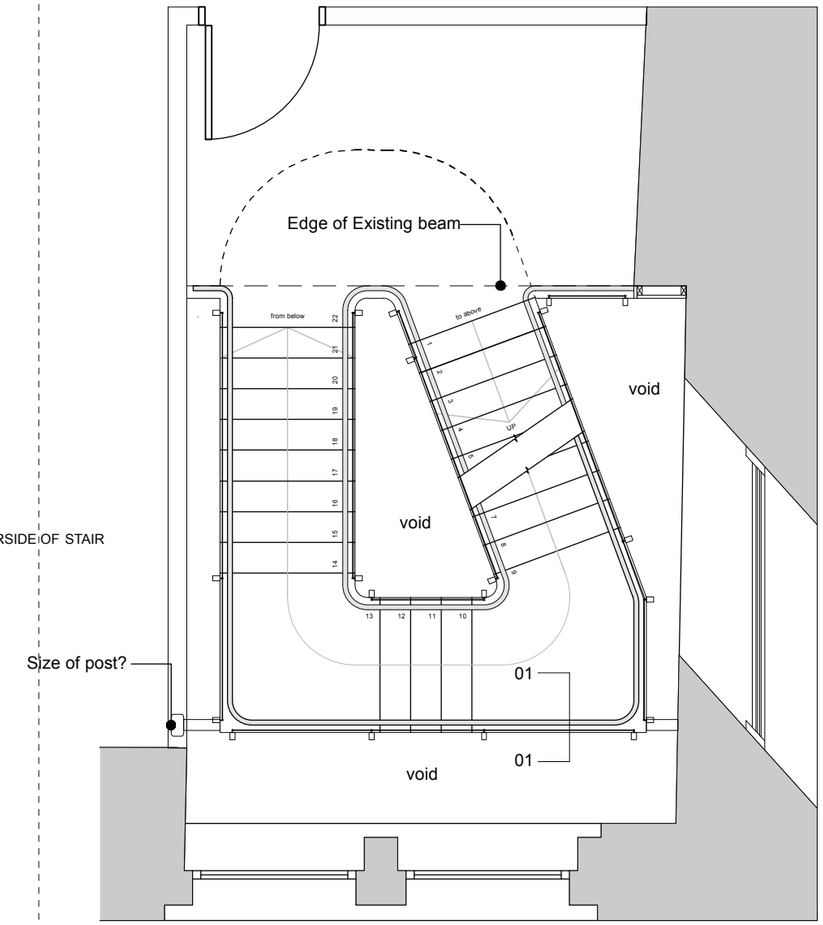

3D Schematic

Typical Plan of Stair

January 2015 | February 2015 | March 2015 | April 2015 | May 2015 | June 2015 | July 2015 | August 2015 | September 2015 | October 2015 | November 2015

Step 32 - Close Up Link to Central Core

26th Oct - 27th Nov 2015

Completion of new Stair core within Buffer Zone

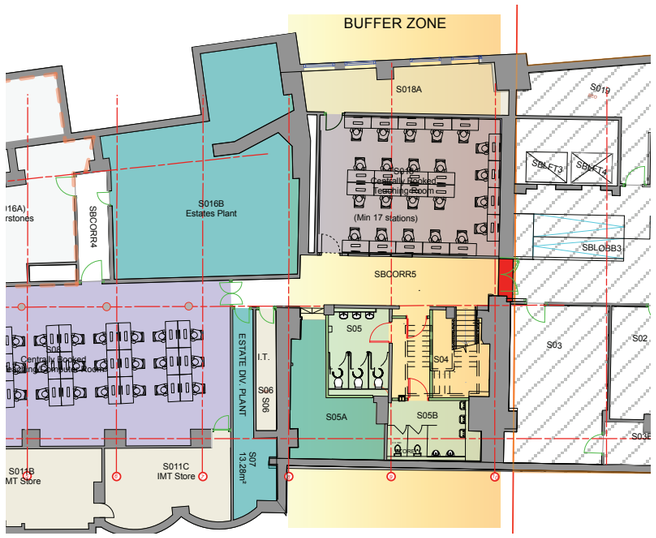

Basement Floor Plan

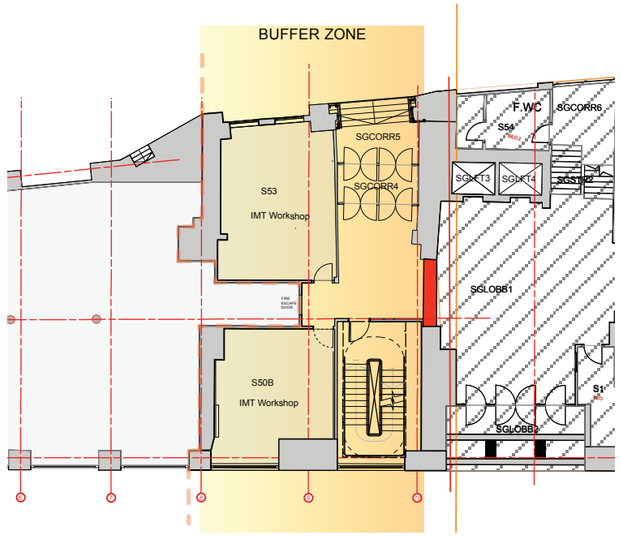

Ground Floor Plan

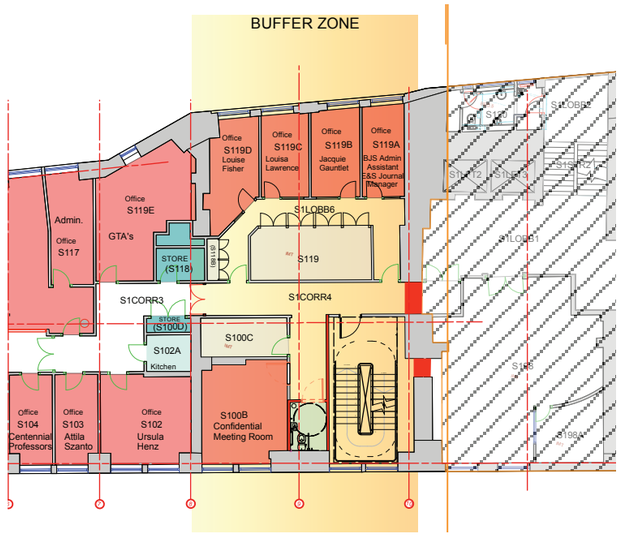

First Floor Plan

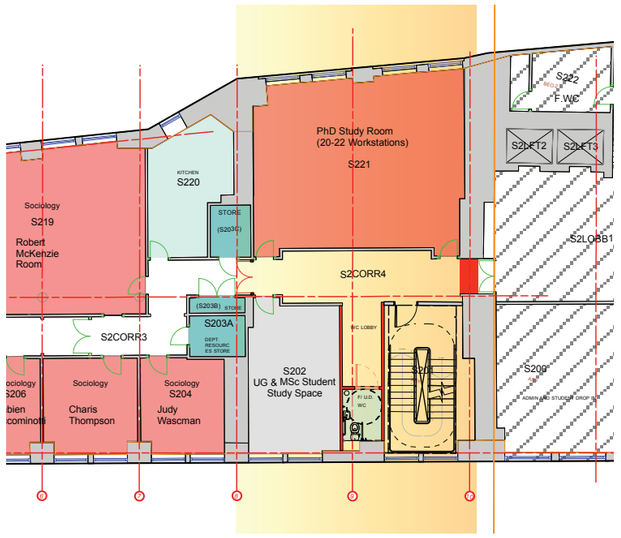

Second Floor Plan

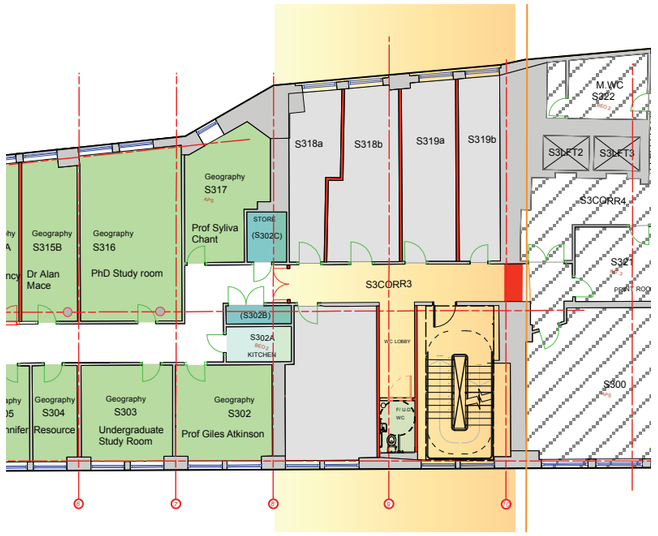

Third Floor Plan

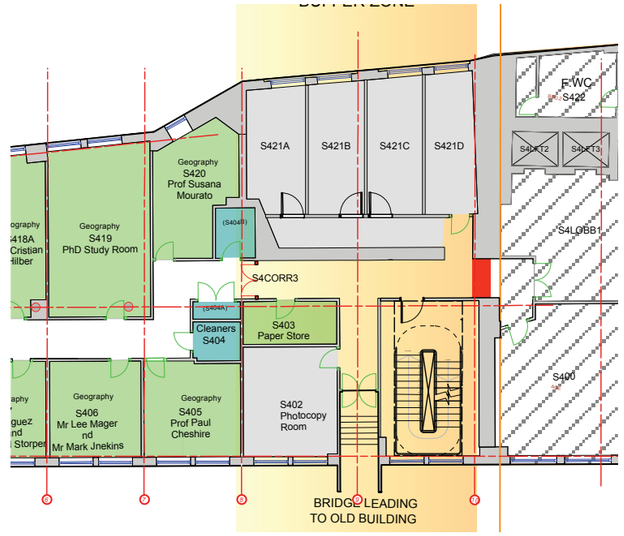

Fourth Floor Plan

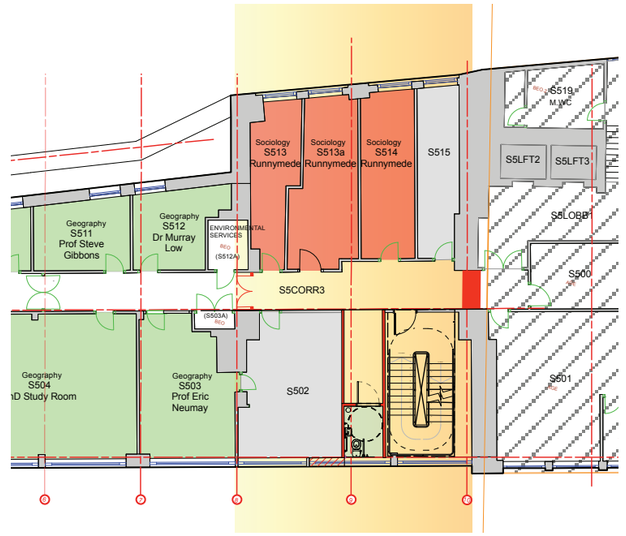

Fifth Floor Plan

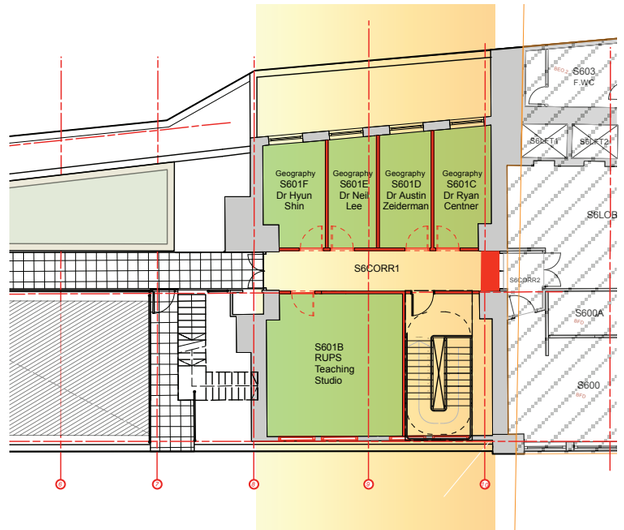

Sixth Floor Plan



Step 33 - Demolitions - Final cut of Central Core

Commence final cut in demolitions works along the line of the Central Core and West Wing Flank Wall.

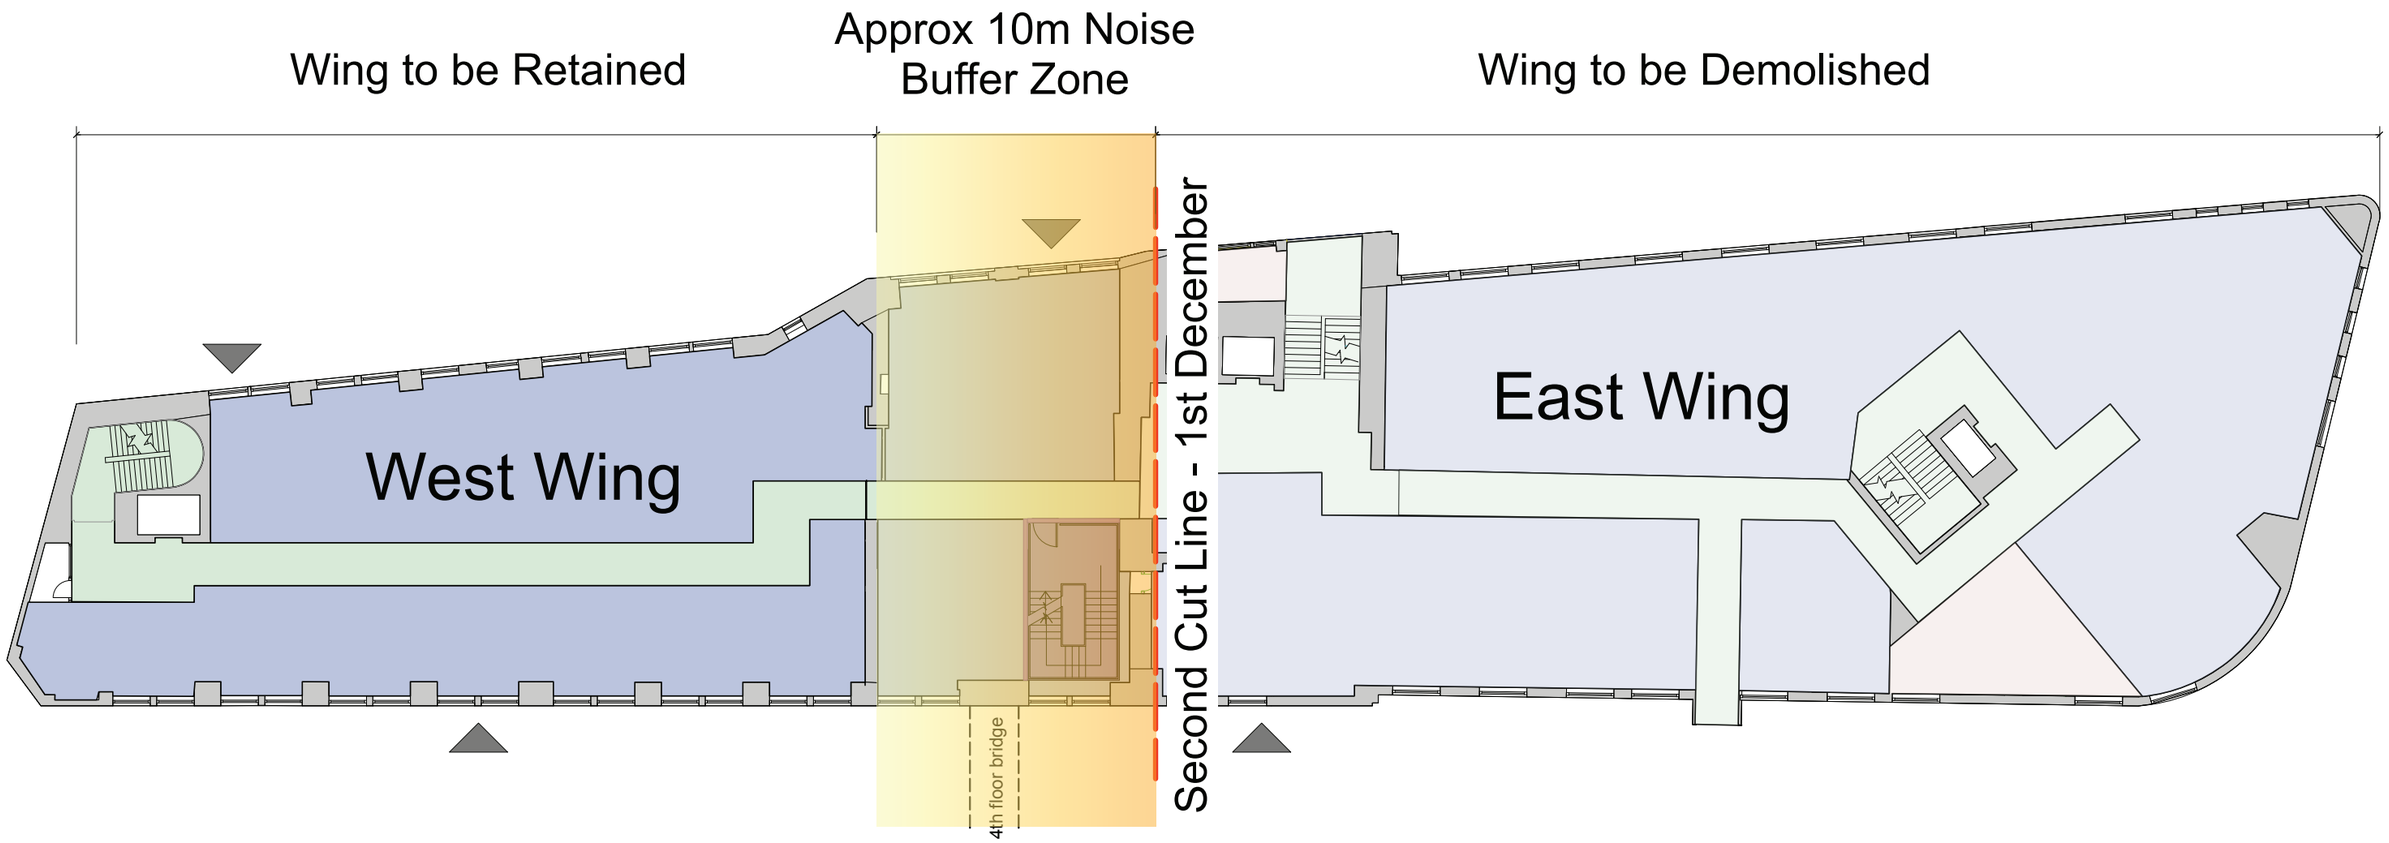

Typical Floor Plan



Final Floor Plans

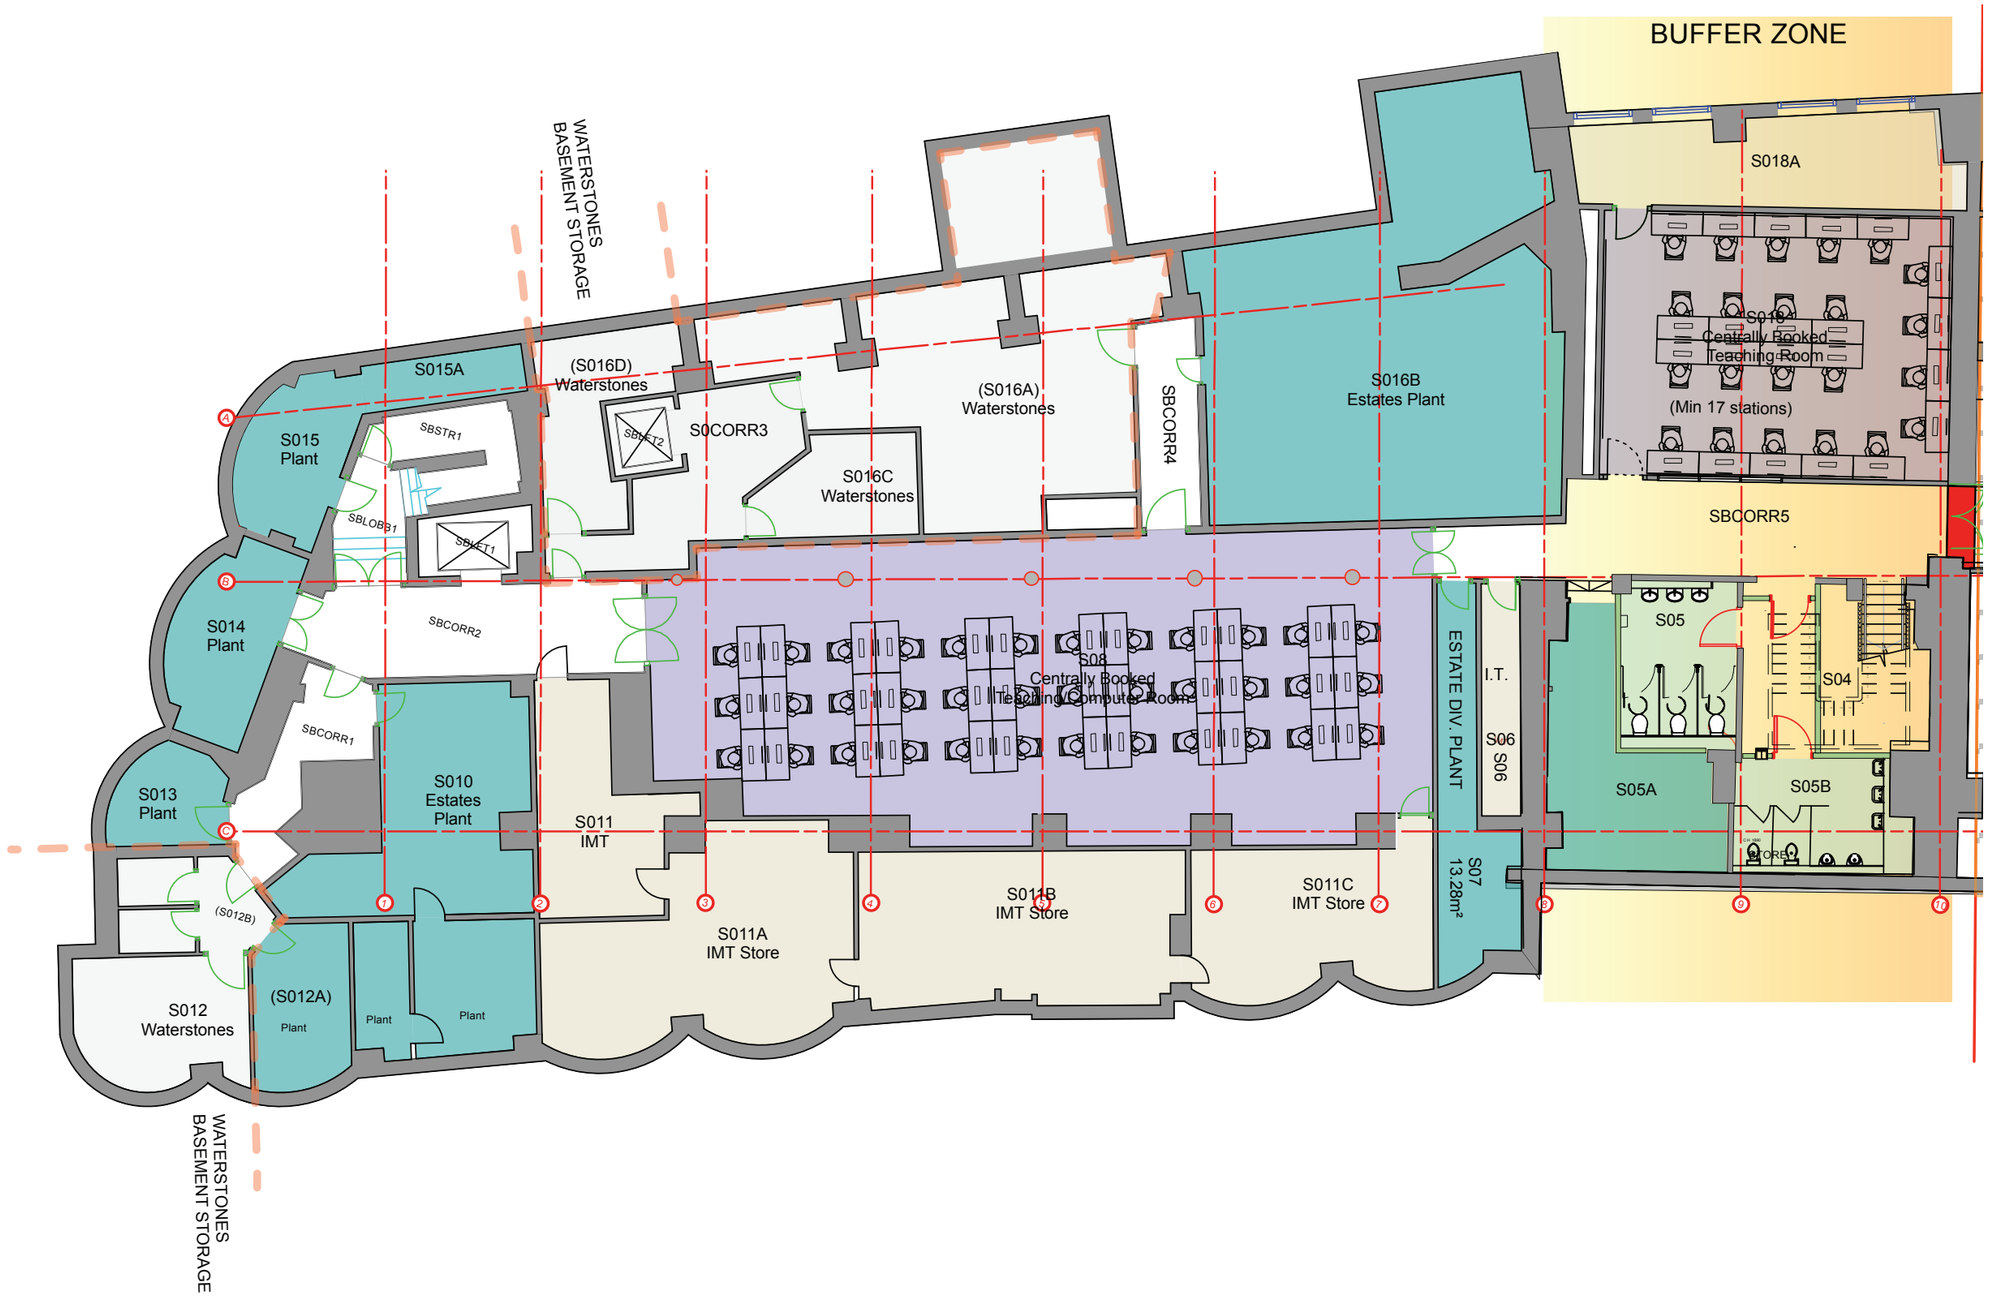

Basement Floor Plan

Final Floor Plans

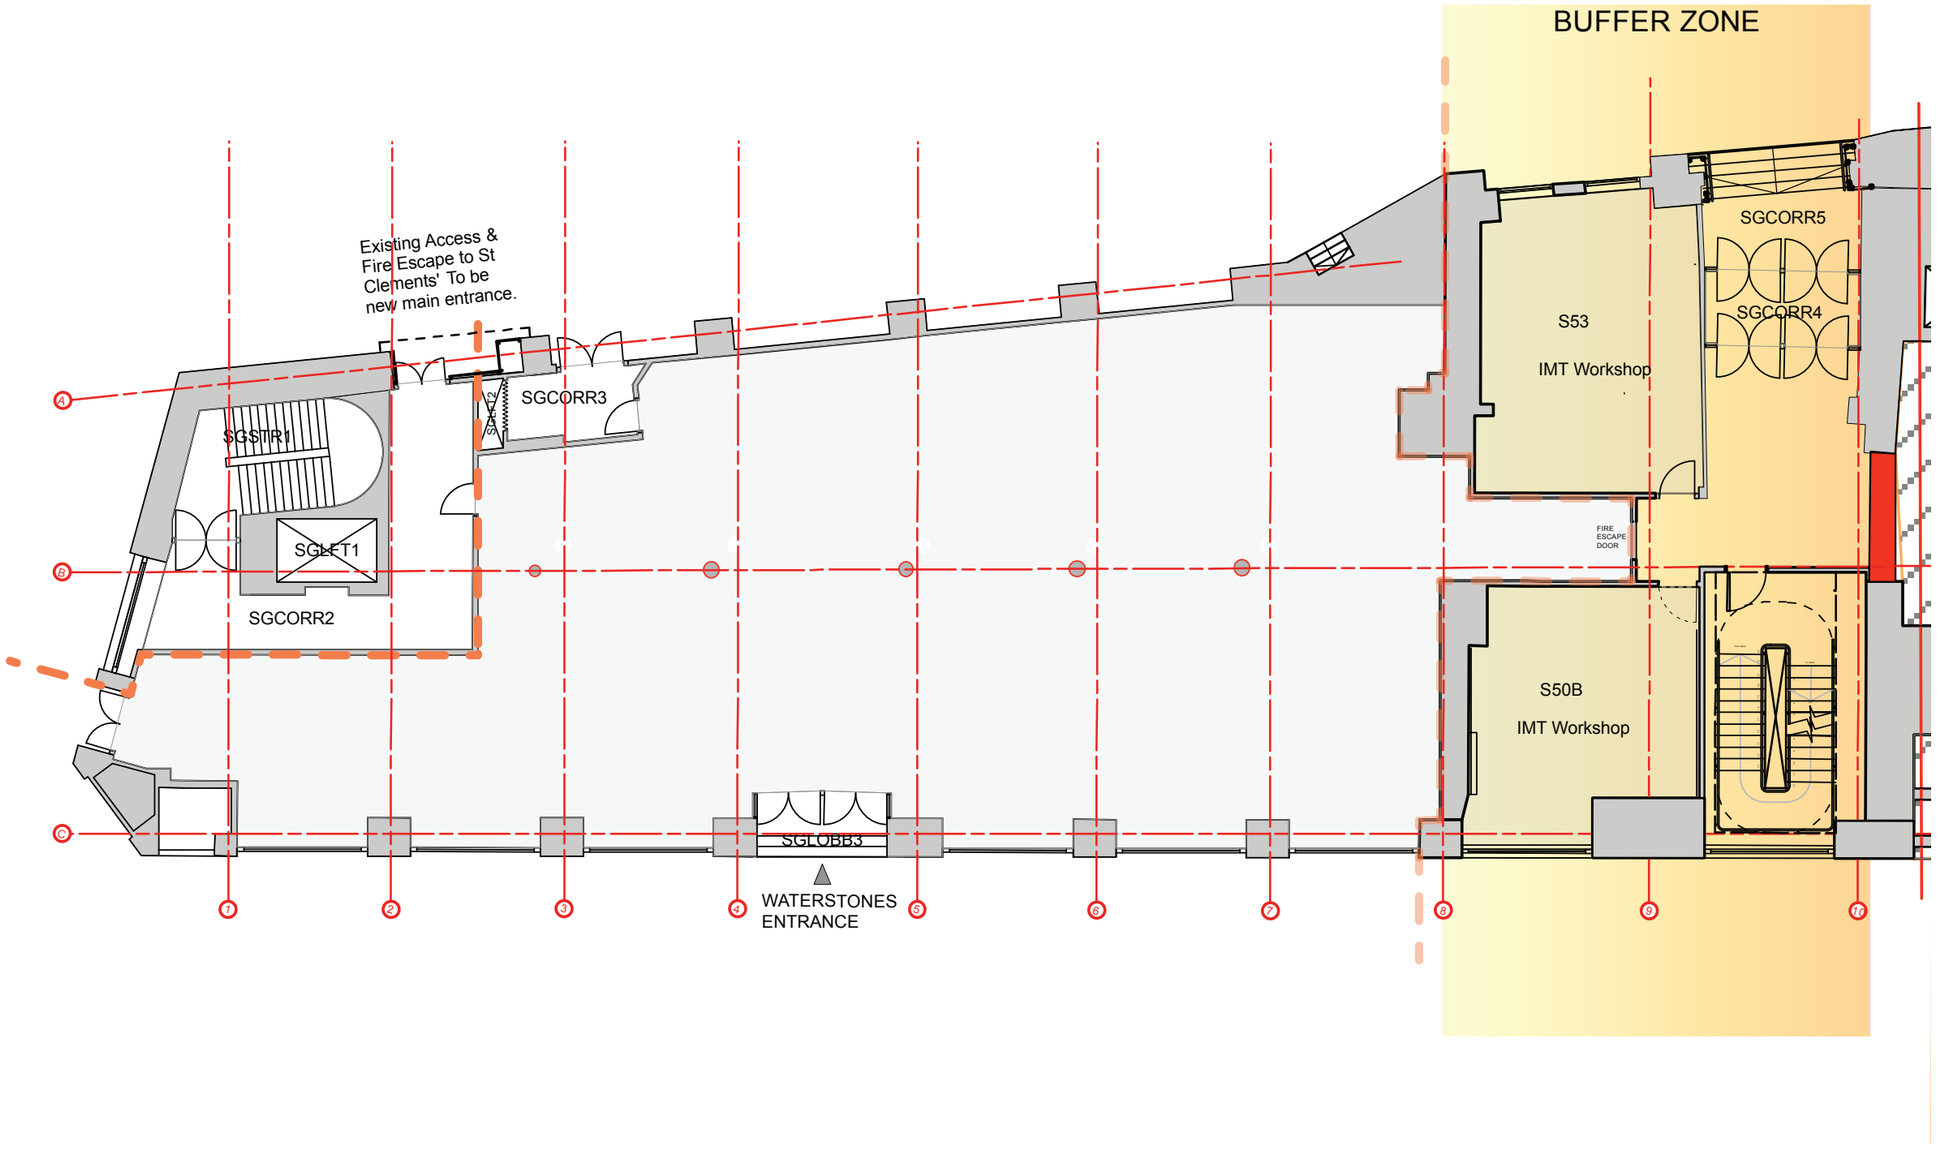

Ground Floor Plan

Final Floor Plans

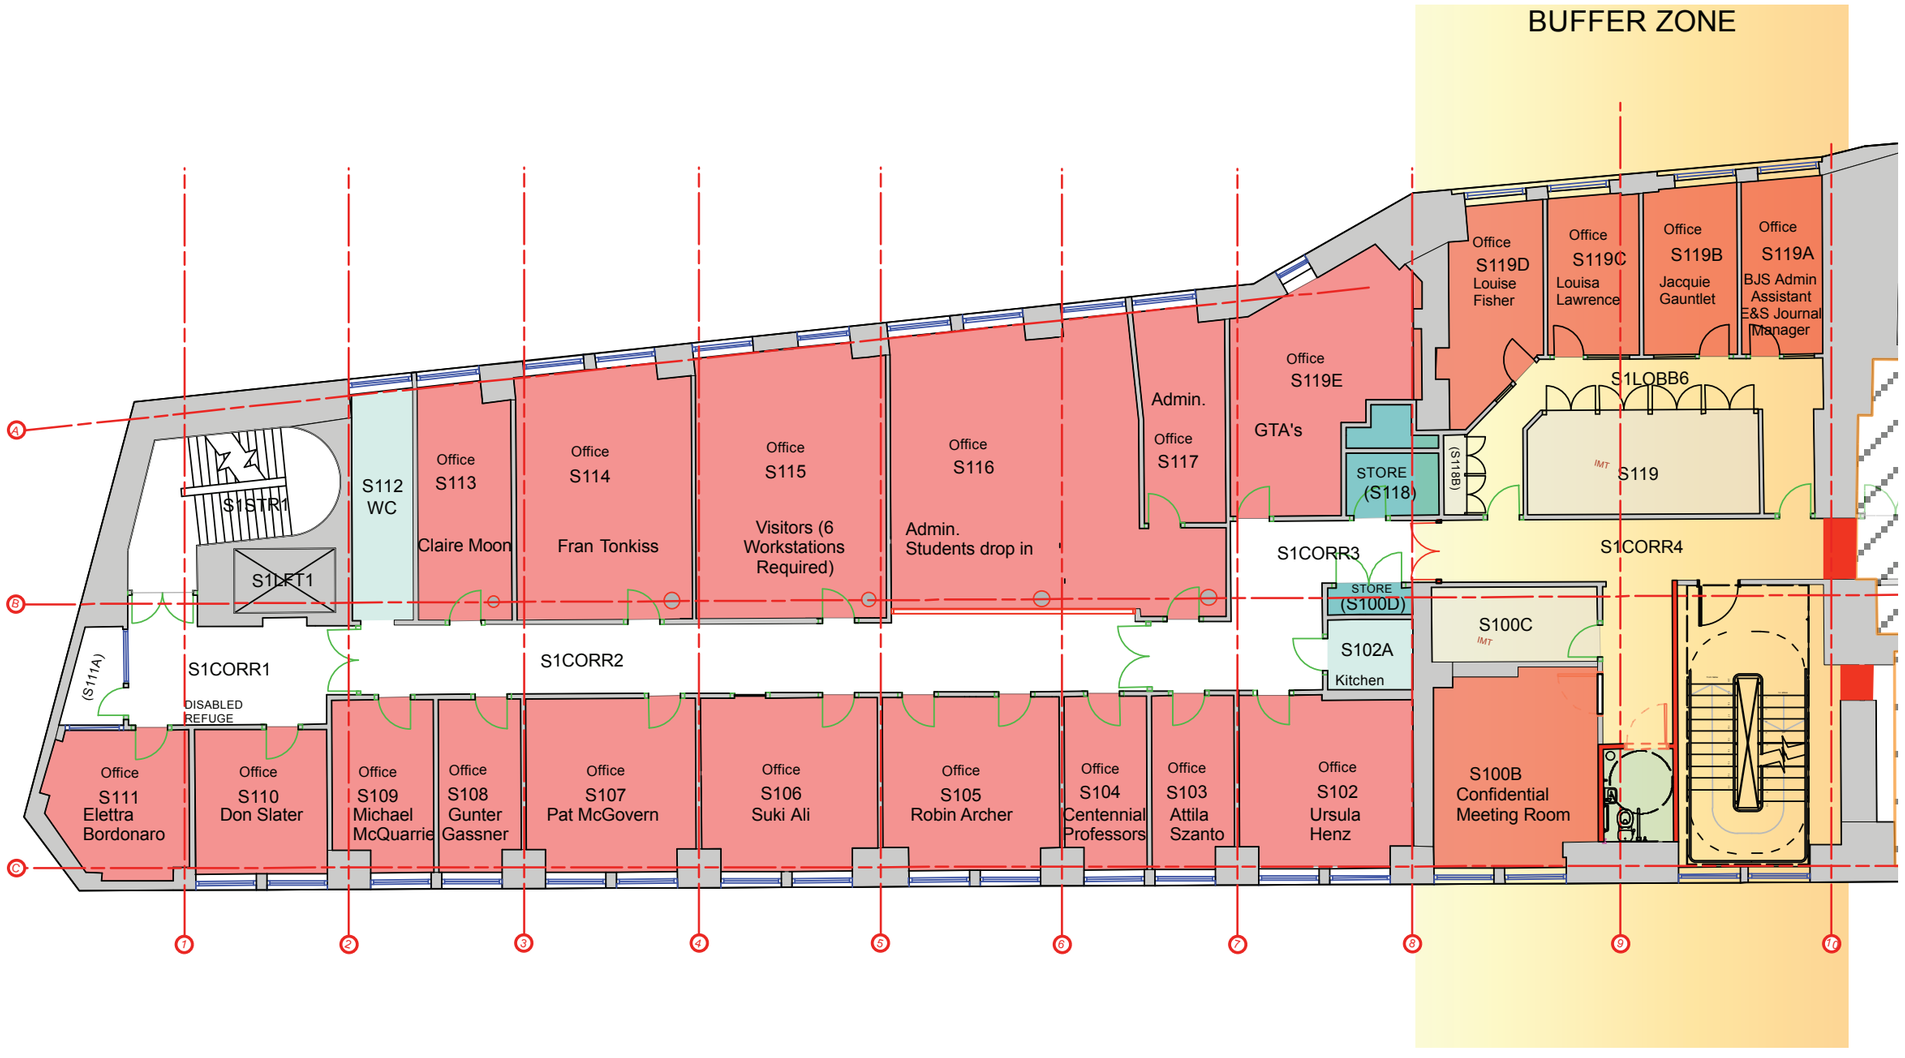

First Floor Plan

Final Floor Plans

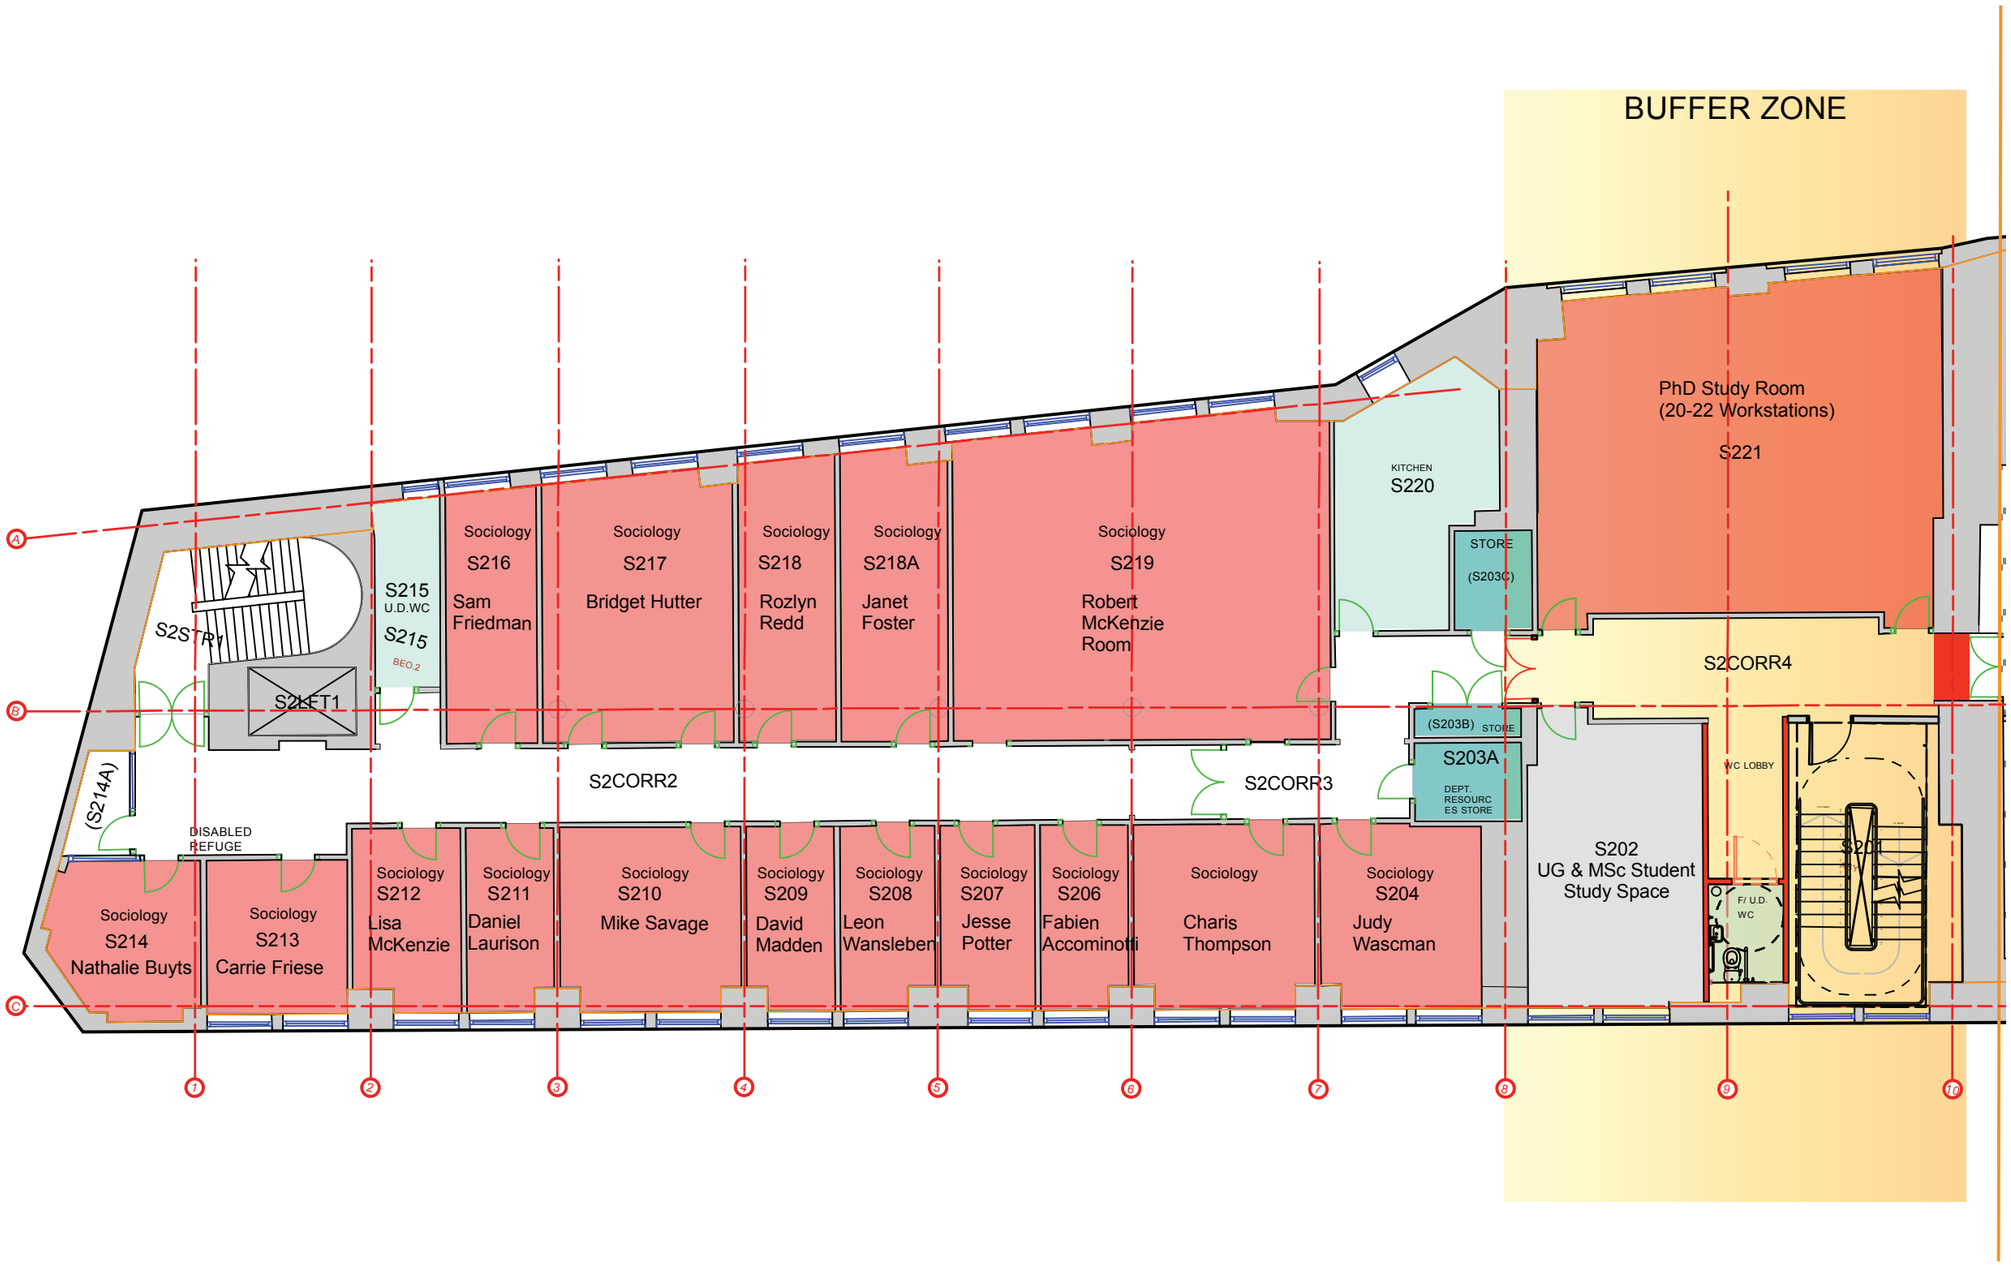

Second Floor Plan

Final Floor Plans

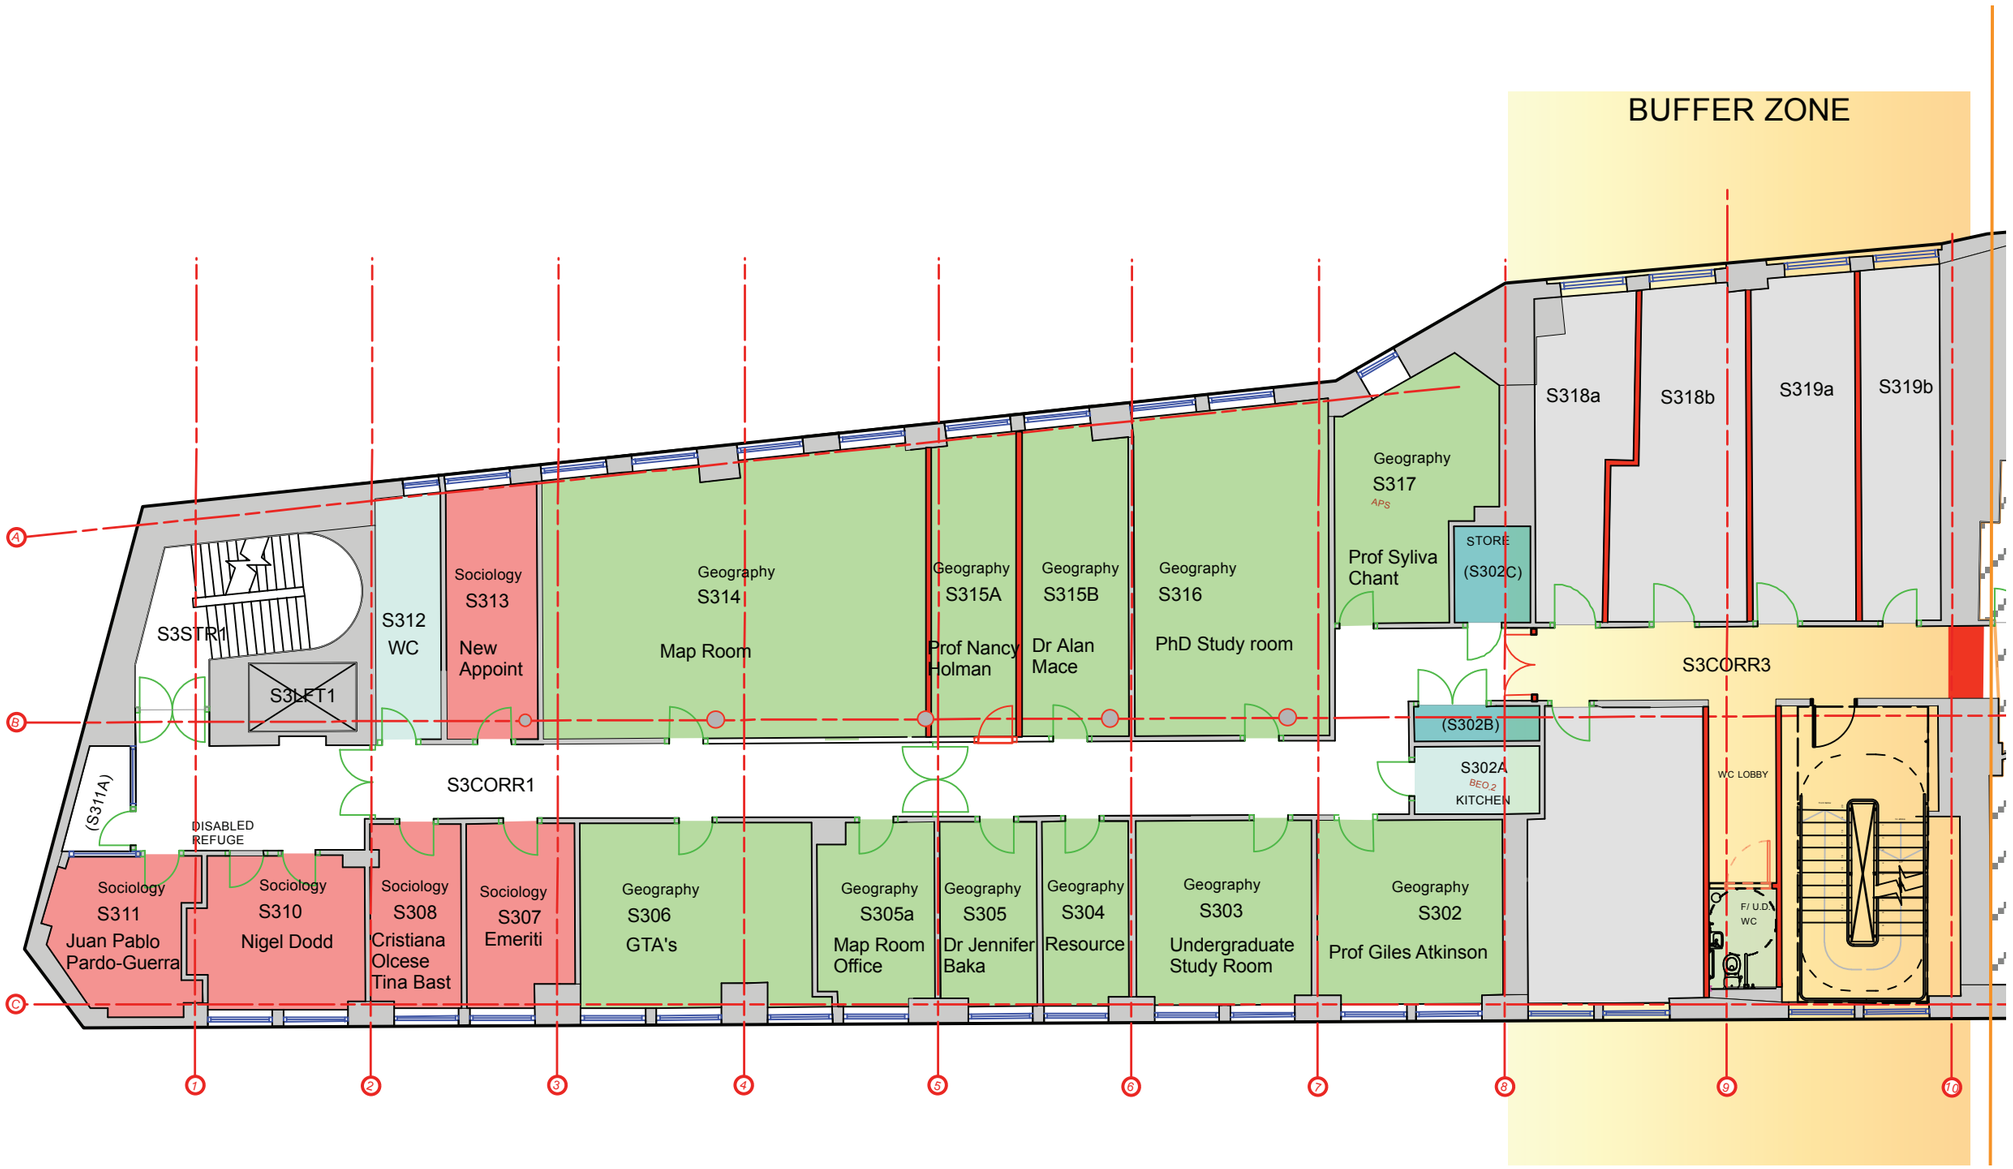

Third Floor Plan

Final Floor Plans

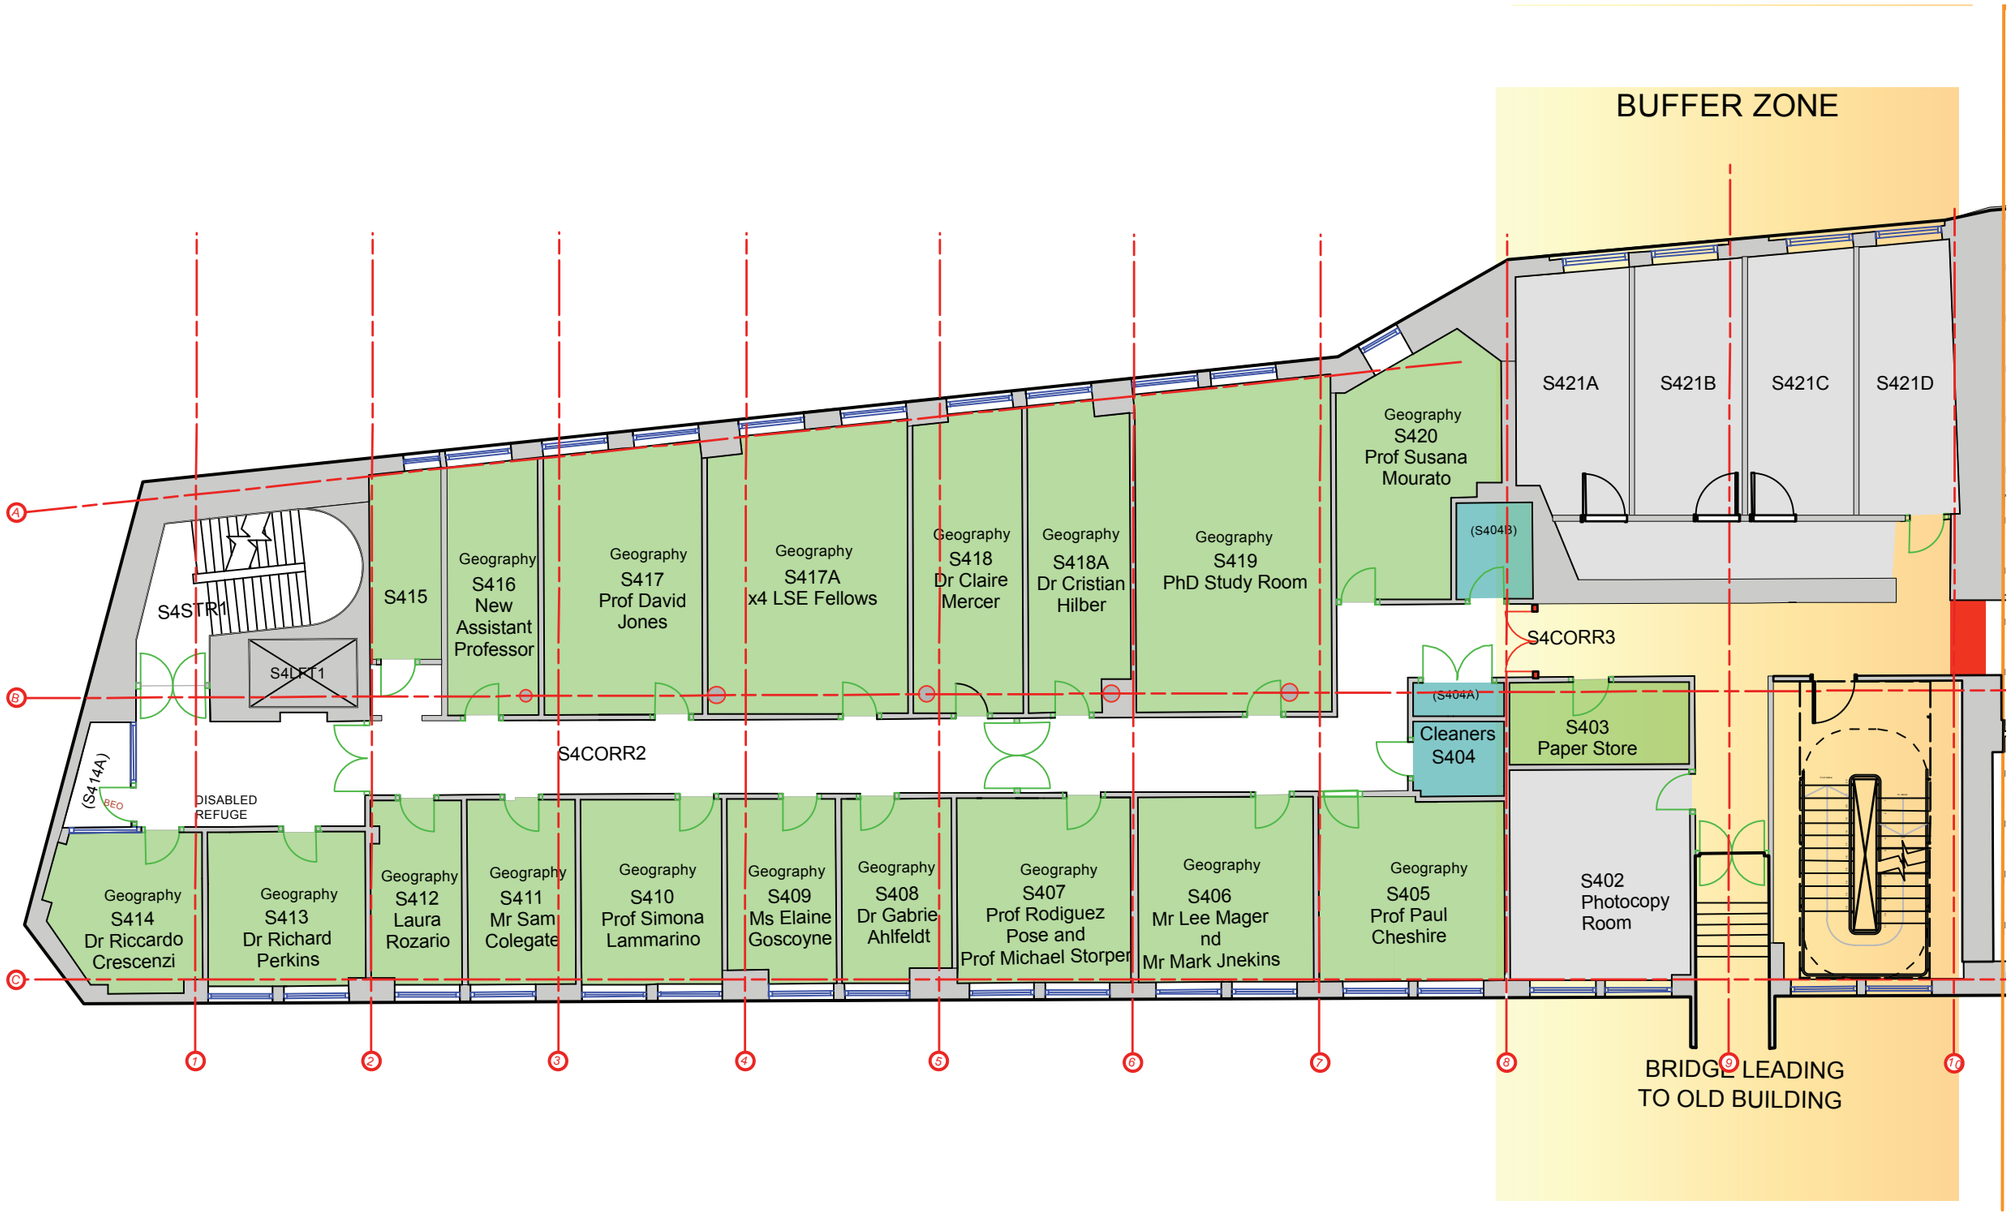

Fourth Floor Plan

Final Floor Plans

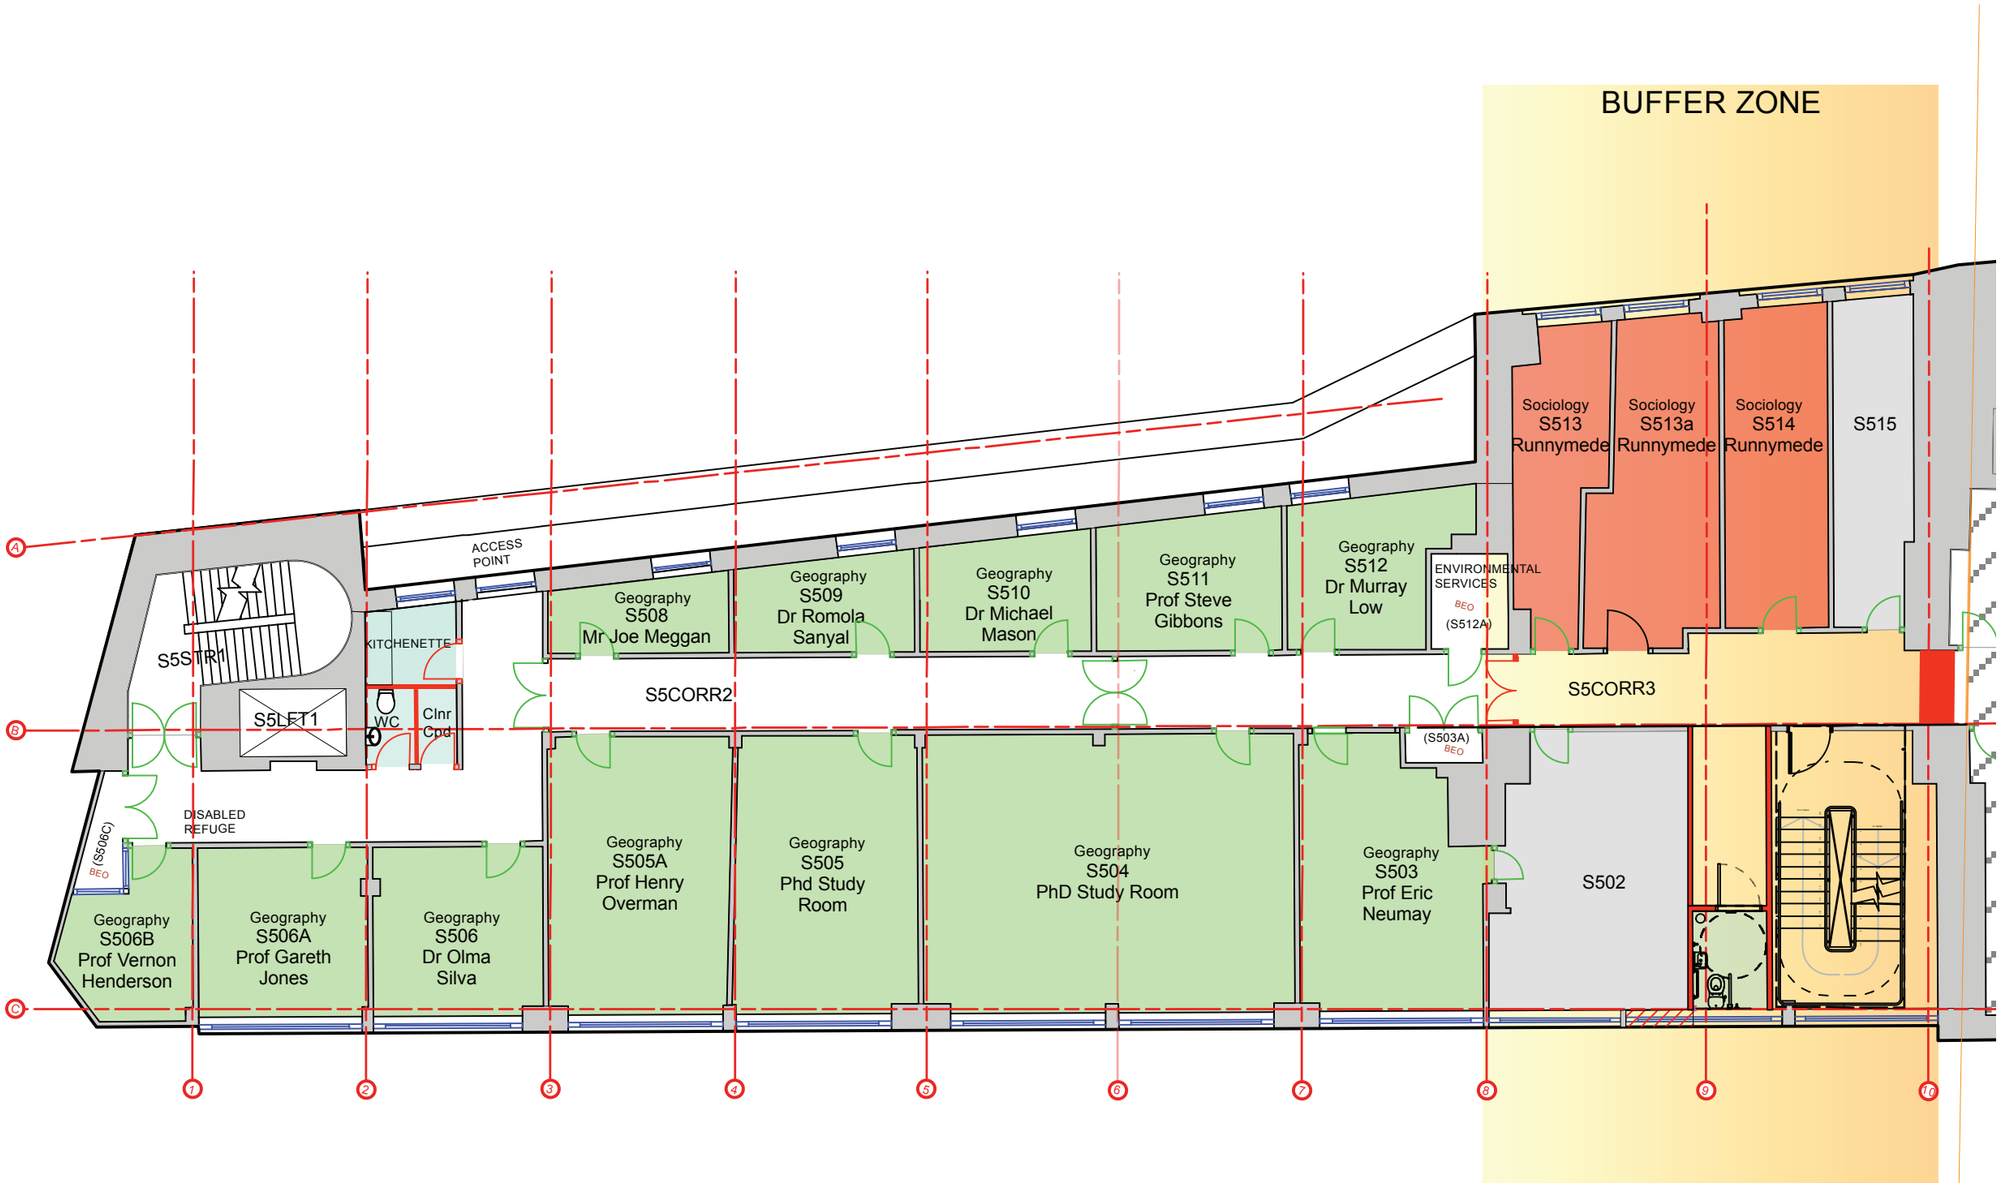

Fifth Floor Plan

Final Floor Plans

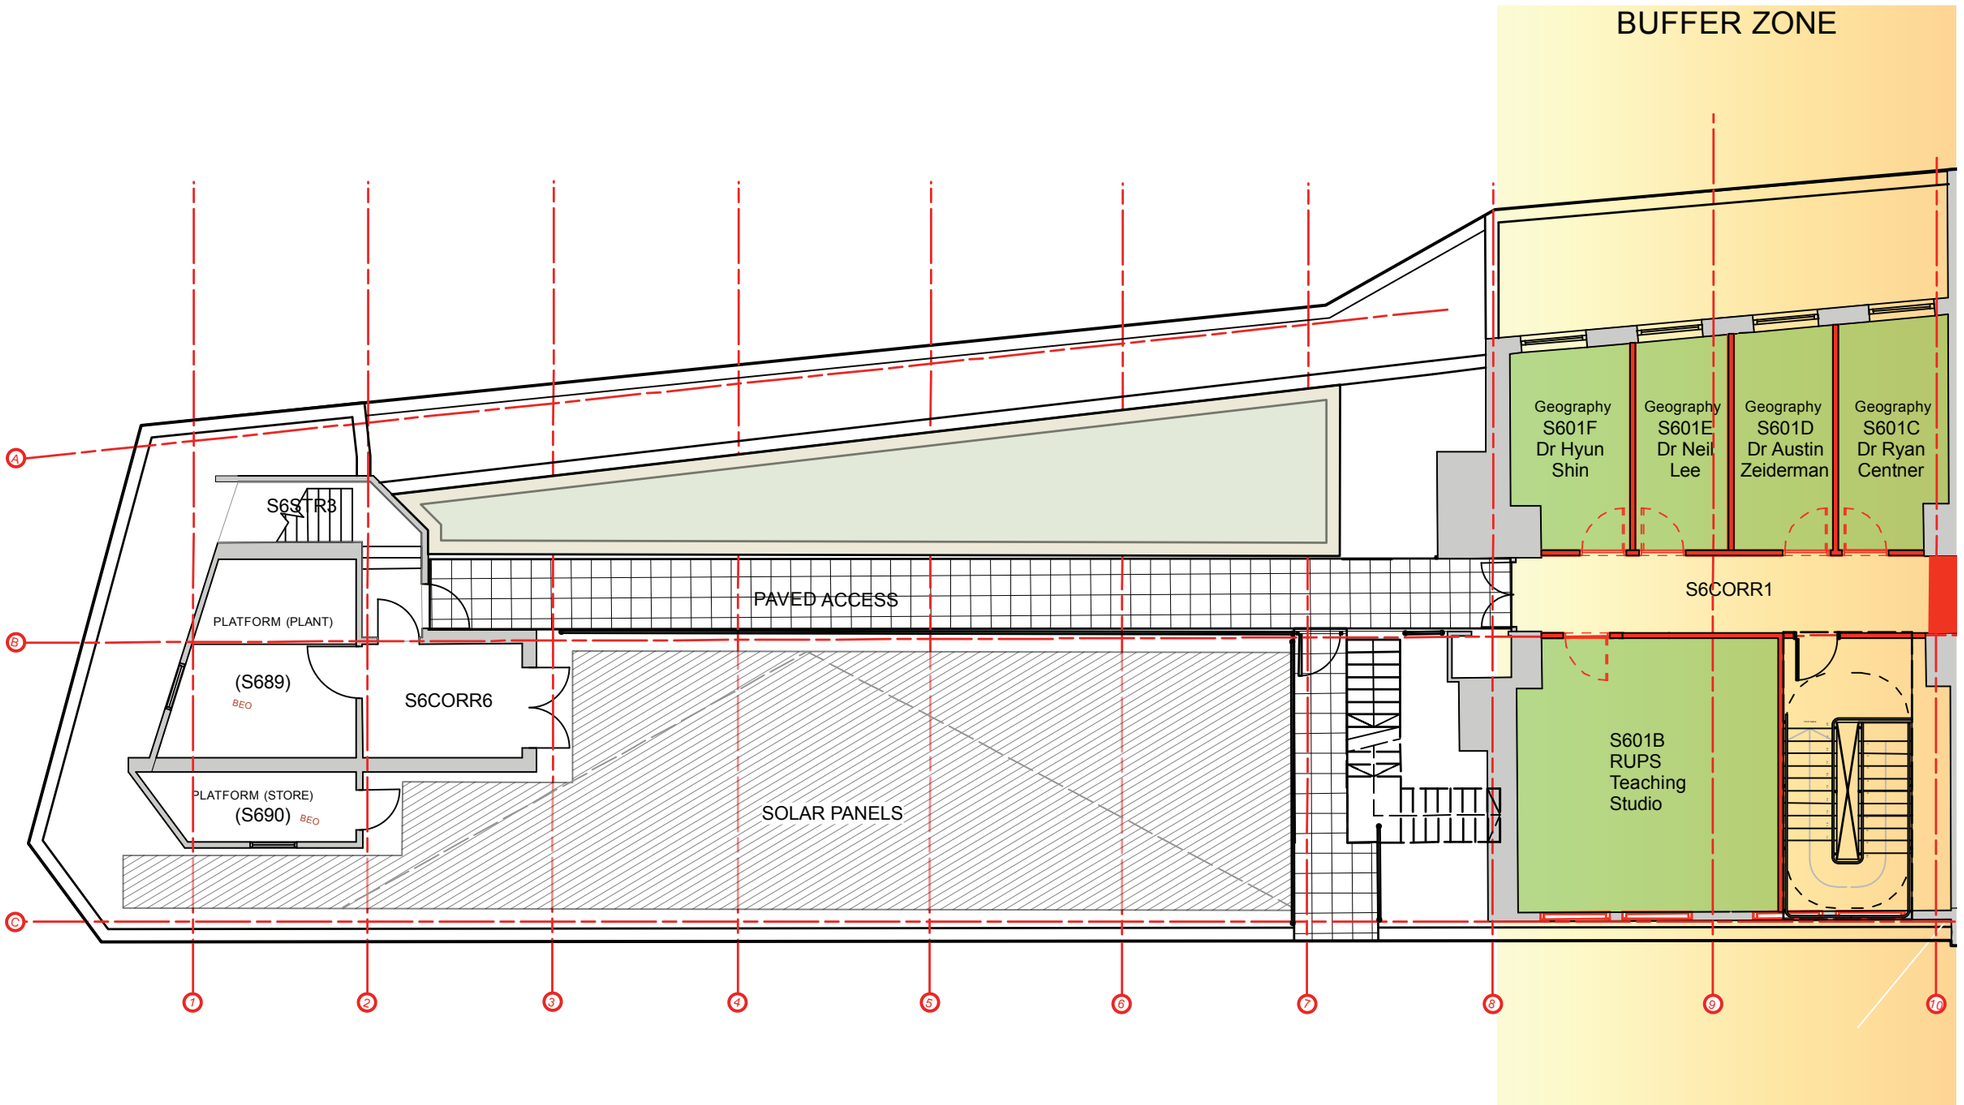

Sixth Floor Plan
